

SPS HS ATHLETICS PHASE 1
Schematic Design (SD)
10.14.2025




SPS HS Athletics Phase 1 – SD Phase

A major milestone was achieved this month with the approval of the HS Athletics Phase 1 Schematic Design (SD) Package and 505 Architects beginning the Design Development (DD) Phase.


- KUG, and DRC SD HS Phase 1 Review meetings were held on October 6th with recommendations to proceed with Design Development Phase.
- Willowbrook Schematic Design Construction Estimate has project tracking on Budget with the incorporation of value engineering considerations from KUG and DRC.
- DD KUG meetings for the various HS spaces have begun and will continue through DD. These meetings are to review next level of details such as millwork, door types, specific finishes, lighting, power and data outlet locations, etc.
- Pre Application meeting is scheduled with City of Stillwater on 10/20.
- Design Development Phase is scheduled to be completed and presented at the January BOE meeting.
- Temporary locker room space is being constructed within the existing Virtual Academy to be utilized during the construction of the Athletics Phase 1 project.





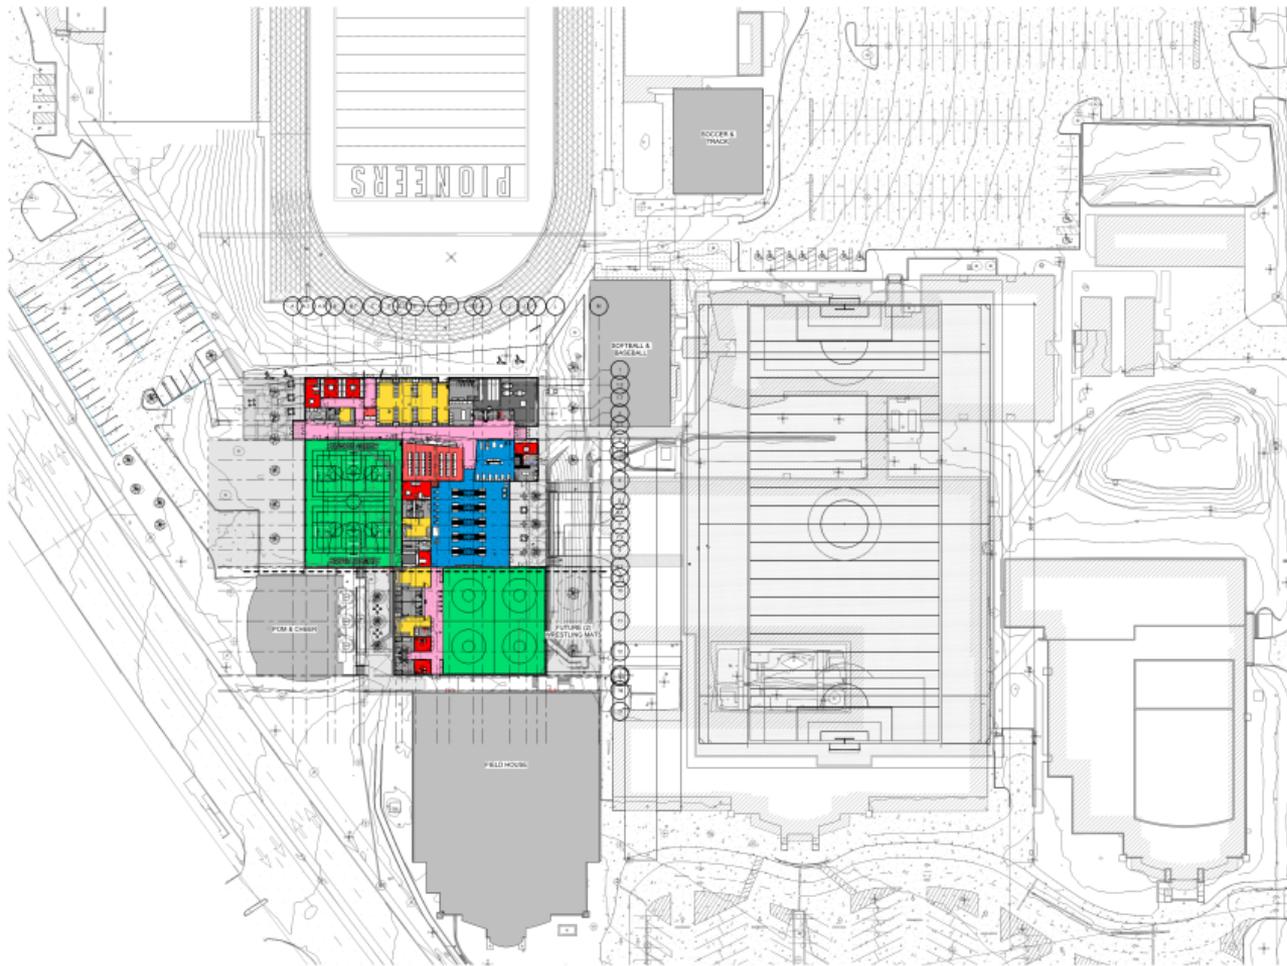

1 CONCEPT FLOOR PLAN - OVERALL
1"=30'-0"

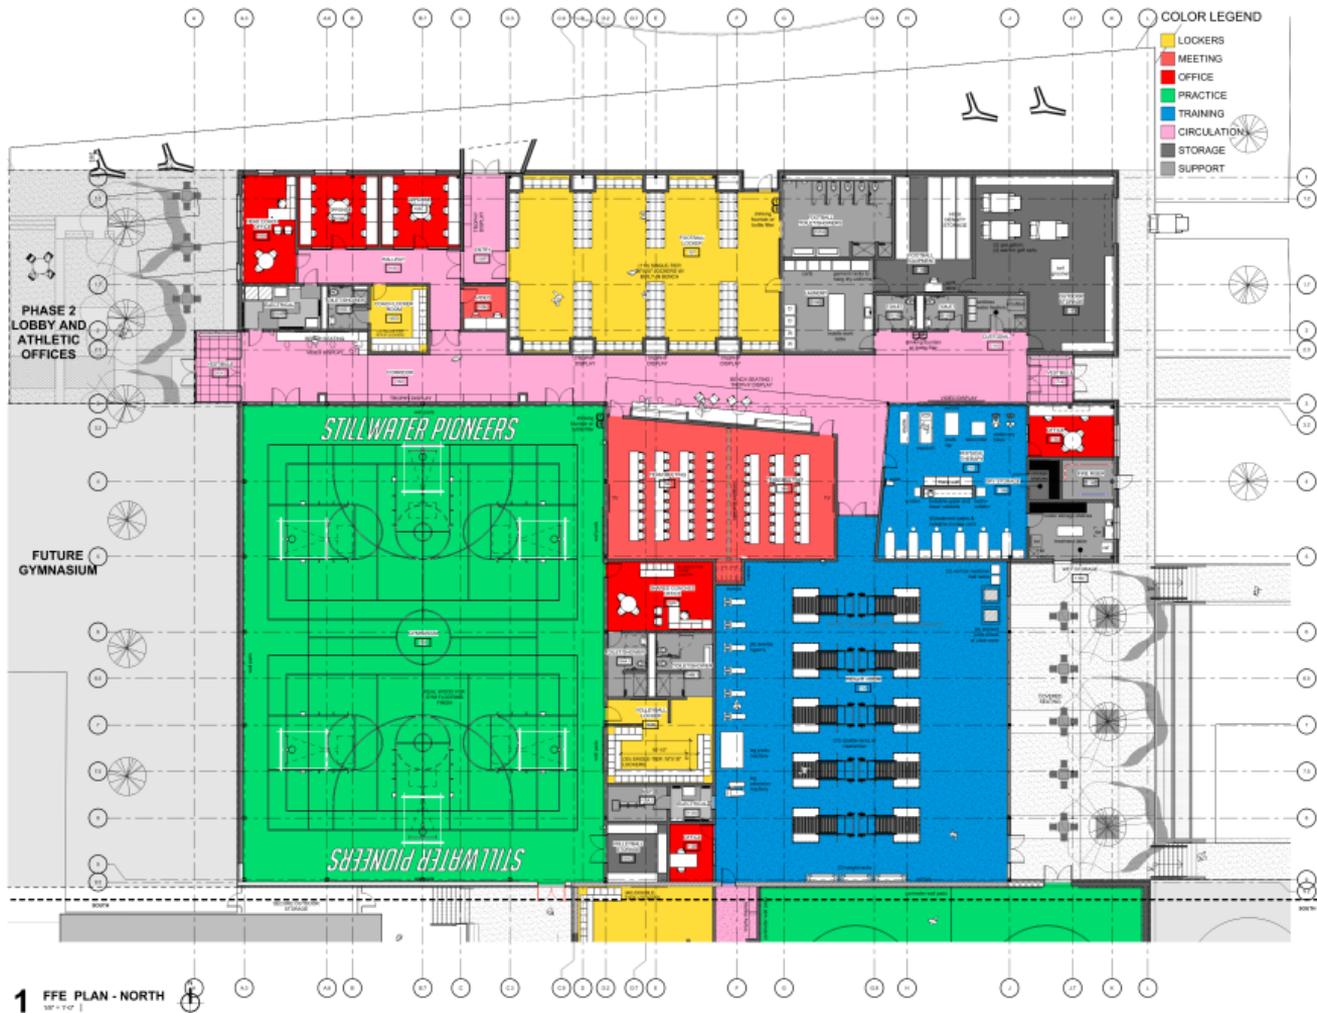





1 FFE PLAN - SOUTH
1/8" = 1'-0"




1 FFE PLAN - SOCCER & TRACK
 1/8" = 1'-0" | 

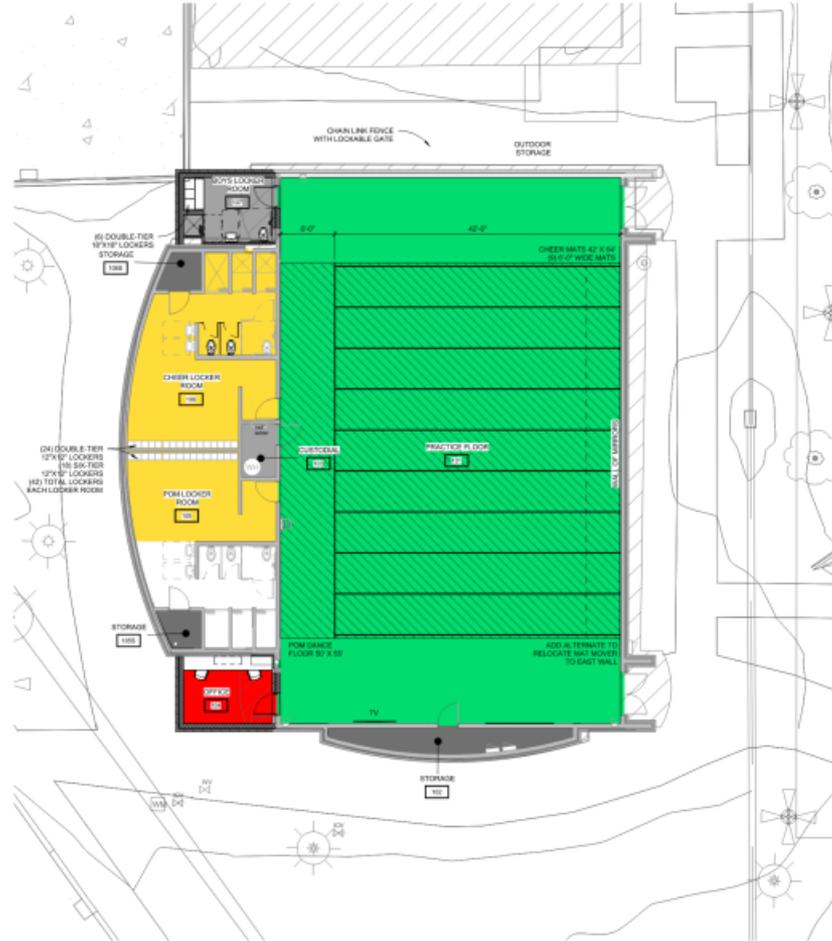

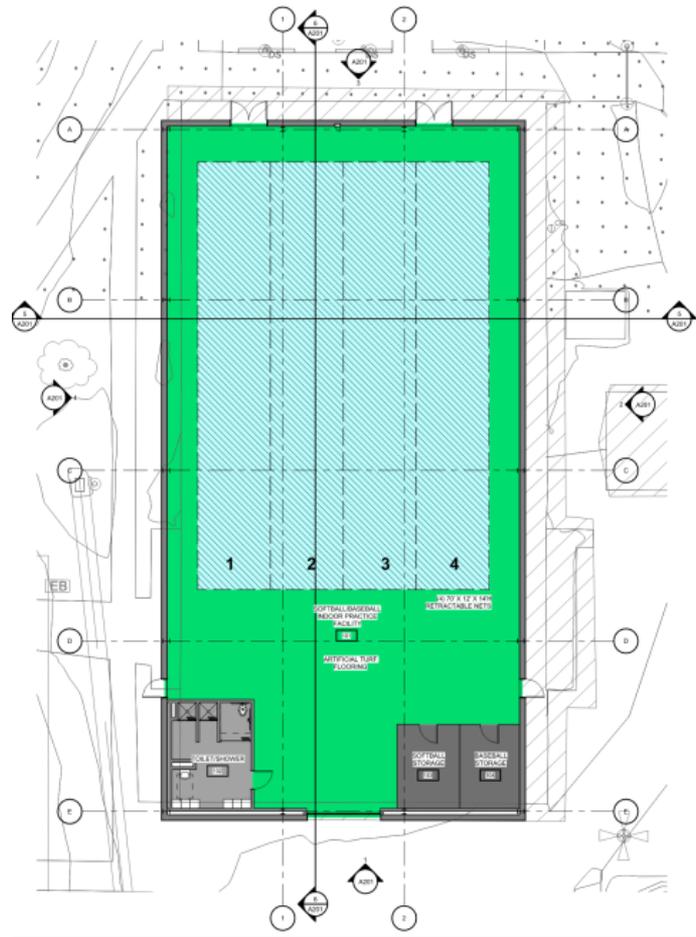

1 FFE PLAN - SOFTBALL & BASEBALL
 1/8" = 1'-0" | 1-A201



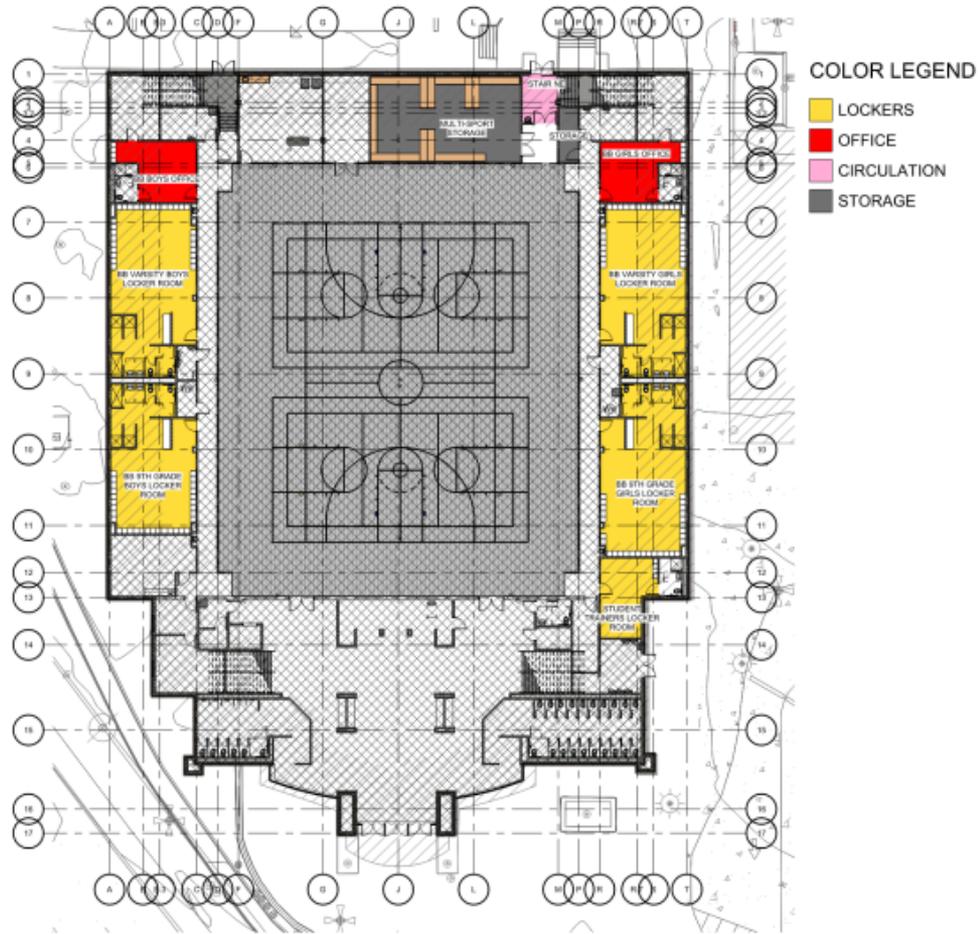

1 FLOOR PLAN FFE - FIRST FLOOR
 1/8" = 1'-0"





505
ARCHITECTS

[Exterior Image | Overall from Stadium](#)







[Interior Images | Pioneer Athletics Hall of Fame / Commons](#)



Interior Images | Third Gymnasium and Football Lockers



Interior Images | Wrestling Room



STILLWATER PUBLIC SCHOOLS

