



BUB Report

Building Update Brief

Facilities and Grounds

&

Summer Construction Projects

August 5th, 2026

Andrew Nordstrom
Director of Facilities, Grounds, and Transportation

Table of Contents

1. Title Page
2. Table of Contents
3. Purpose
4. HS and DO Office Remodel
5. Auditorium Stage Lighting Upgrade
6. Exterior Building Sealing and Caulking
7. HS Gym Floor Refinish
8. CEJ HVAC and Boiler Replacement
9. CEJ Outdoor Classroom
10. HS Cooler and Freezer Replacement
11. End/Questions



Purpose




The purpose of this presentation is to provide the Superintendent and Board of Education updates on Facilities and Grounds and Summer Construction Updates.



High School and District Office Remodel

Current Update:


- Sheetrock is complete.
- Mudding, Taping, and Sanding is finishing up.
- Painting will start next week.
- Security Window will start next week
- Ceiling Grid and Tiles are installing this week.

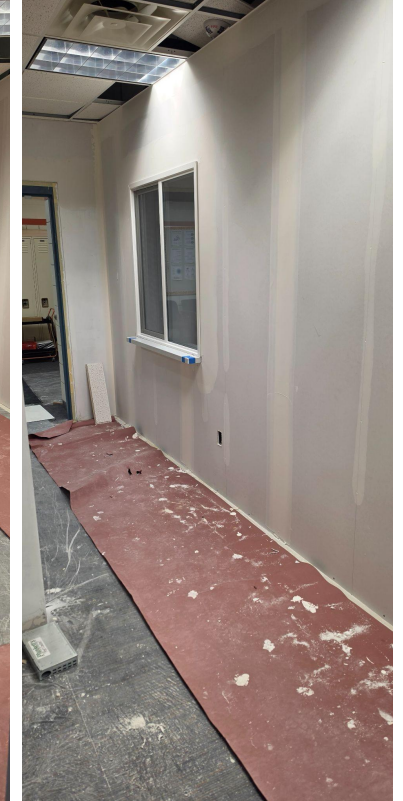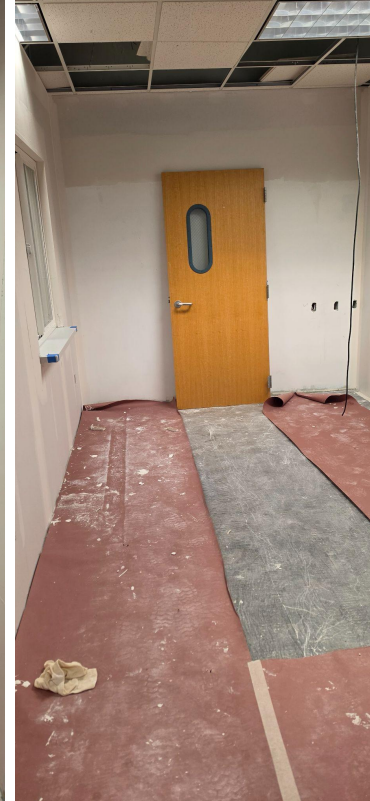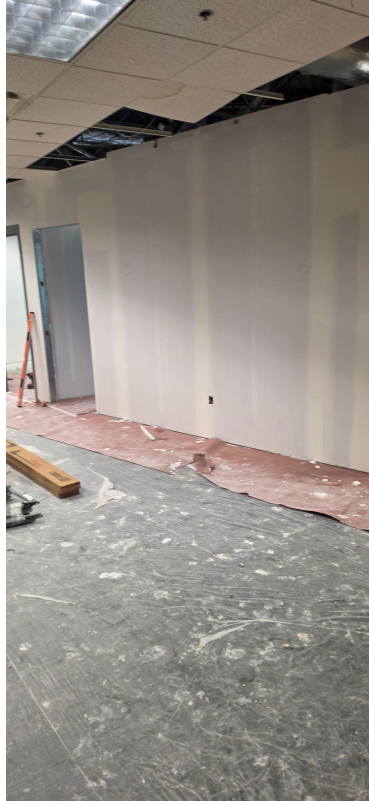

High School Auditorium Stage Lighting Upgrade

Current Update:

Training for Rush City School Staff is set for August 21st @ 8am

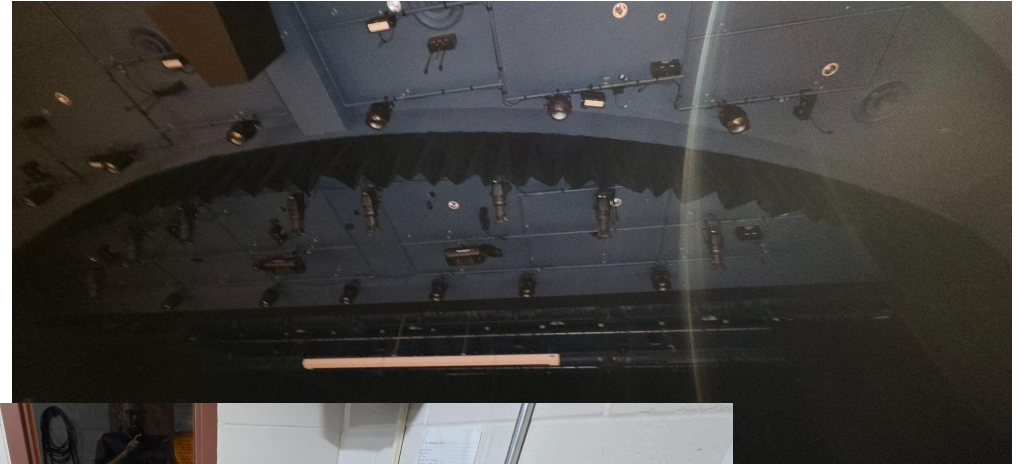

Exterior Building Caulking and Tuckpointing

Current Update:


- Tuckpointing is ongoing right now at the Elementary School.
- They will move to High School once complete.
- This work will go through the month of August.



High School Gym Refinish

Current Update:

- Gym Floor is complete.
- Wax has been installed and curing.
- Baseboard is ordered and will install next week.
- Final clean will start and complete next week.

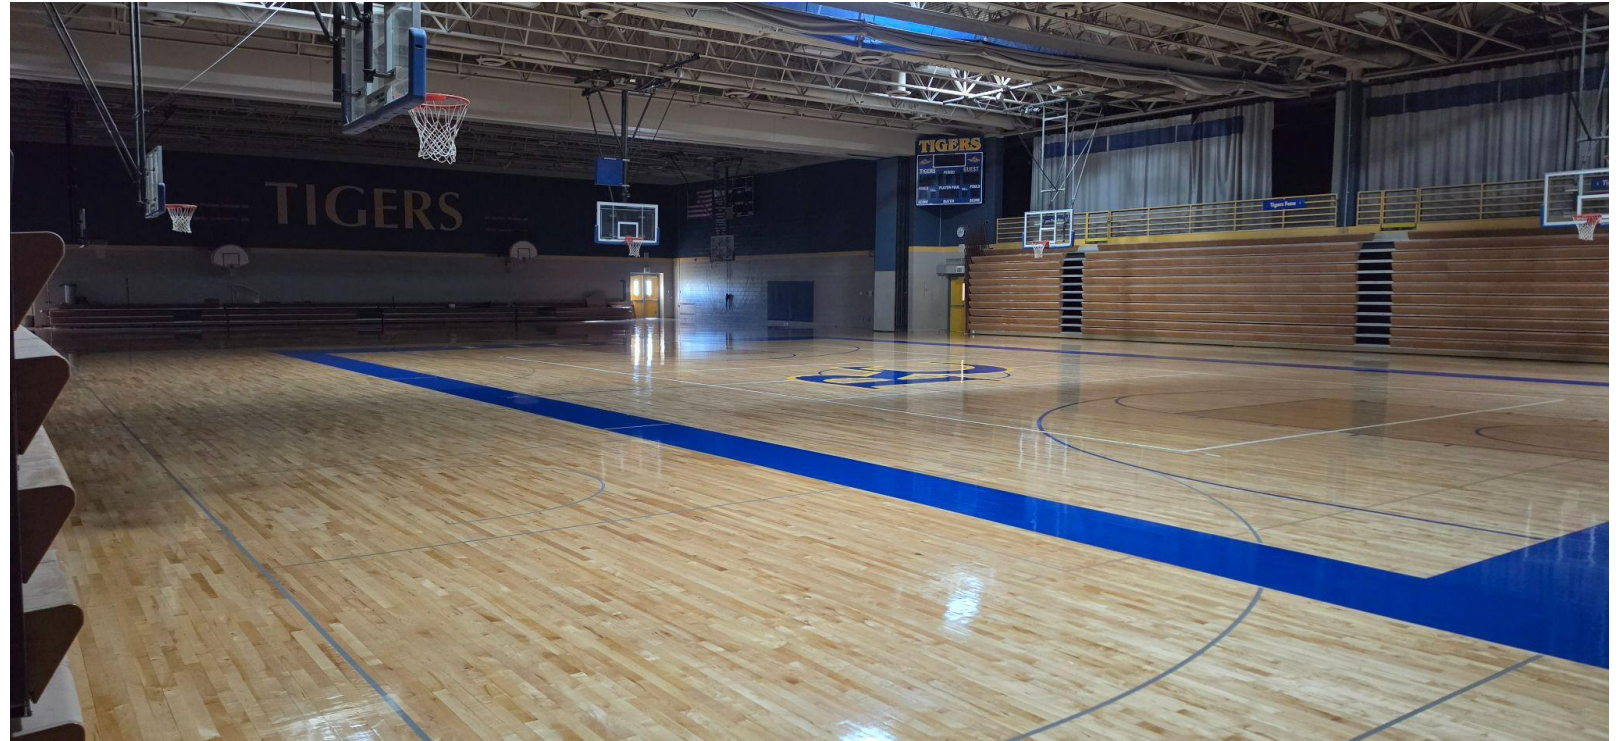

CEJ HVAC and Boiler Replacement

Current Update:

- ❖ Project is underway.
- ❖ Week of 08/03 – Ceilings come down and trades can start working as needed in hallways.
- ❖ Week of 08/10 – Boiler and Electrical Disconnection to take place.
- ❖ Week of 08/10 – Excavation of chiller pad, prep base for concrete pour.
- ❖ Week of 08/17 – Demolition and removal of old boilers.
- ❖ Week of 08/17 – Demo concrete area in boiler room. vii. Week of 08/17 – Pour all new concrete.
- ❖ Week of 08/24 – Ceilings put back, continuation of the boiler plant and VAV installation to continue into school year.



CEJ Outdoor Classroom

Current Update:

- Installation is complete.
- Concrete Pad is complete.
- Cleaning up area and planting grass around.



HS Cooler and Freezer Replacement

Current Update:

- Cooler and Freezer Installation is completed.
- Startup is complete and both are operational!



End of Presentation

Questions???

Thank you!!!

