



BUB Report

Building Update Brief

Facilities and Grounds

&

Summer Construction Projects

August 14th, 2026

Andrew Nordstrom
Director of Facilities, Grounds, and Transportation

Table of Contents

1. Title Page
2. Table of Contents
3. Purpose
4. HS and DO Office Remodel
5. HS and DO Office Remodel - Continued
6. Auditorium Stage Lighting Upgrade
7. Exterior Building Sealing and Caulking
8. HS Locker Room Lighting Upgrade
9. HS Gym Floor Refinish
10. CEJ HVAC and Boiler Replacement
11. CEJ Outdoor Classroom
12. Press Box
13. HS Cooler and Freezer Replacement
14. End/Questions



Purpose



The purpose of this presentation is to provide the Superintendent, Board of Education, Staff, and The Community updates on Facilities, Grounds, and Summer Construction Updates.



High School and District Office Remodel

Current Update:

- Sanding and Painting are 75% complete.
- Fire Alarm and Lighting is underway.
- Security Window is getting installed.
- Above Ceiling inspection is Friday.
- Carpet re-patch work is getting installed this week
- Furniture is delivered end of the week and put together. Next week they will move furniture into place.

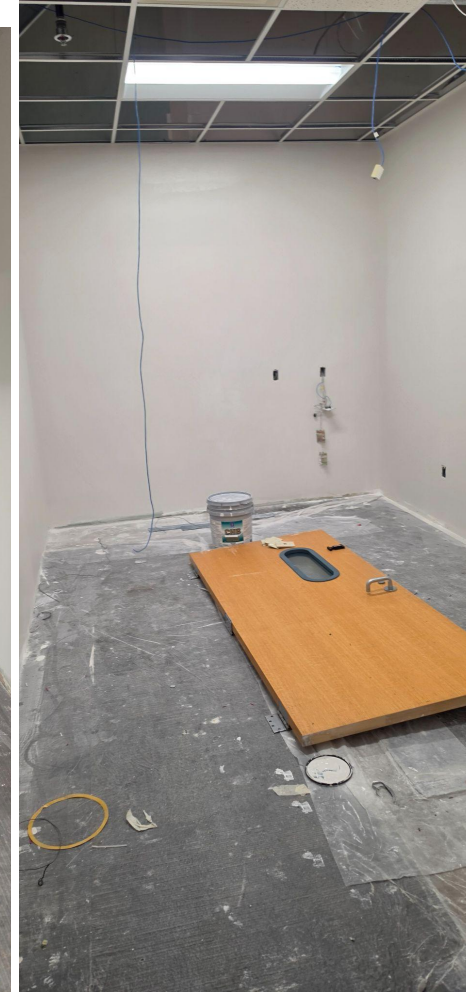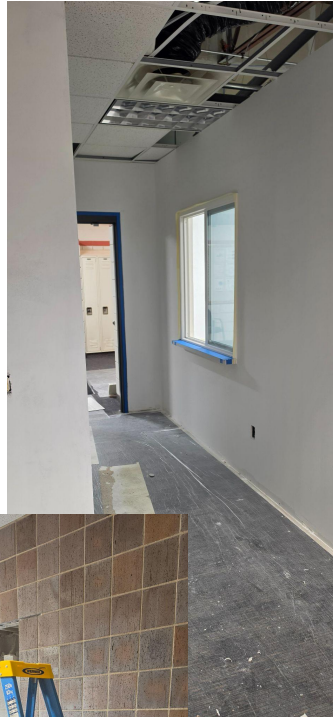


HS and DO Office Remodel - Continued



High School Auditorium Stage Lighting Upgrade

Current Update:

- Training for Rush City School Staff is set for August 21st @ 8am.
- The training will be recorded.

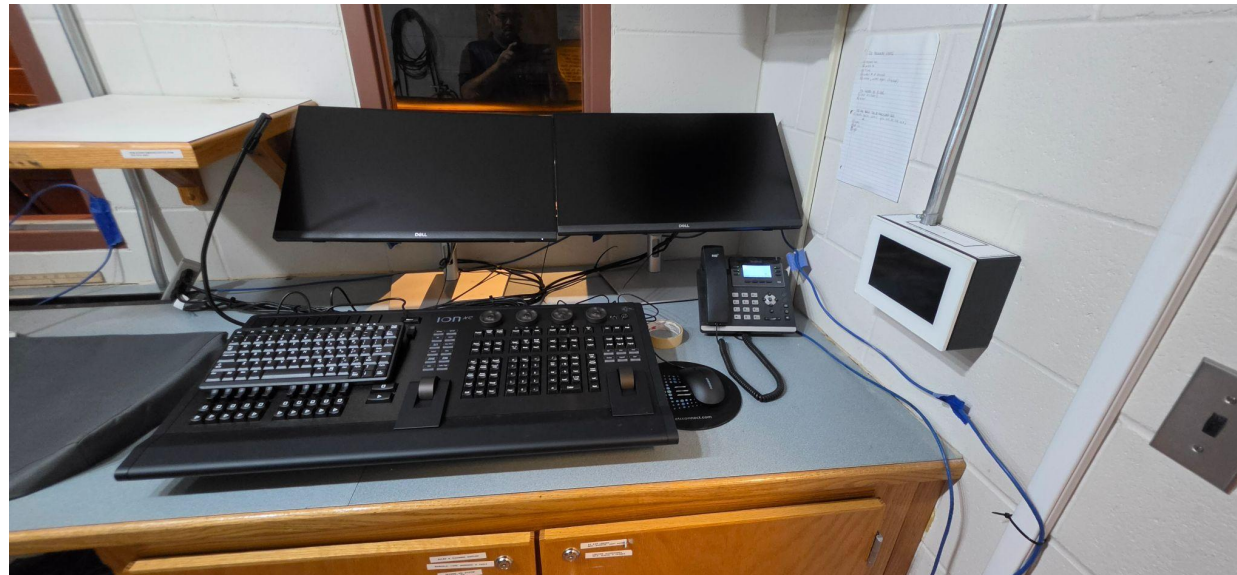

Exterior Building Caulking and Tuckpointing

Current Update:

- Tuckpointing is still in progress at the Elementary School.
- They will move to High School once complete.
- This work will go through the month of August.



HS Boys and Girls Locker Room - LED Light Upgrade

Current Update:

- Lighting Upgrade to LED lights. Due to many bulbs needing to be replaced and light fixture covers where damaged and unable to buy replacements due to age.



High School Gym Refinish

Current Update:

- Gym Floor is complete.
- Wax has been installed and curing.
- Baseboard has been ordered and will install when it comes in.
- Currently Final Clean is underway. Plan to be completed this Friday.



CEJ HVAC and Boiler Replacement

Current Update:

- Week of 08/10 –
 - Boiler and Electrical Disconnection to take place.
 - Excavation of chiller pad, prep base for concrete pour.
 - Core Drilling is
- Week of 08/17 –
 - Demolition and removal of old boilers.
 - Demo concrete area in boiler room.
 - Pouring all new concrete and concrete footings.
- Week of 08/24 –
 - Ceilings put back together.
 - Continuation of the boiler plant and VAV installation to continue into school year.



CEJ Outdoor Classroom

Current Update:

- We have a new Outdoor Classroom ready for use.

**Thank you to the
Education Foundation
for making this
happen!!!**

- Filling in to concrete pad is complete.



Press Box

Current Update:


- Construction is underway.
- Old Press Box has been removed.
- Footings have be installed and waiting to cure.
- Lumber has be delivered.
- Construction will start soon.



HS Cooler and Freezer Replacement

Current Update:

- Cooler and Freezer Installation is completed.
- Startup is complete and both are operational!

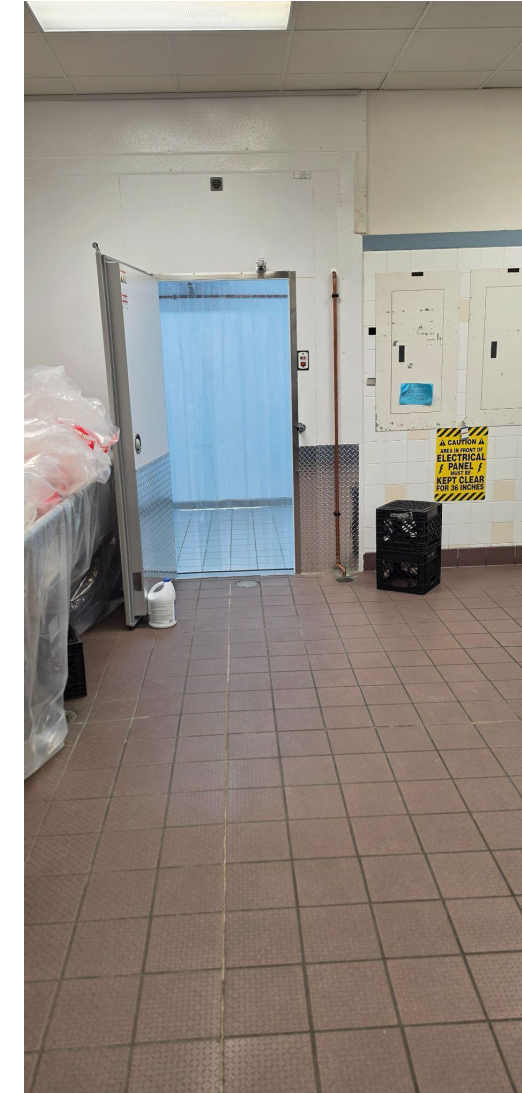

End of Presentation

Questions???

Thank you!!!

