



STILLWATER PUBLIC SCHOOLS
STILLWATER BOARD OF EDUCATION

PREPARED BY: Bo Gamble, Assistant Superintendent of Operations
APPROVED BY: Dr. Janet Vinson, Acting Superintendent
DATE: January 14, 2024

AGENDA ITEM: 5B

Consider Approval of Certificate of Substantial Completion for SPS OES North and South Building Renovation Project.

BOARD ACTION REQUESTED:

Vote to Approve Certificate of Substantial Completion for SPS OES North and South Building Renovation Project.

BACKGROUND INFORMATION:

Attached is the Certificate of Substantial Completion and Punch List for Stillwater Public Schools OES North and South Building Renovation Project. The work identified has been reviewed by the architect and found to be substantially complete in accordance with the contract documents so that the Owner can occupy and utilize the spaces for their intended use. The date of substantial completion of the project, or portion designated, is also the date of commencement of applicable warranties, except those items listed in the attached punch lists. The contractor has 30 days from the date of substantial completion to complete the punch list items, and commencement of those warranties will begin with the date of issuance of final payment.

AIA[®] Document G704[®] – 2017

Certificate of Substantial Completion

PROJECT: *(name and address)*
SPS OES North Building Renovation
5021 North Perkins Road
Stillwater, Oklahoma

SPS OES South Building Renovation
5005 North Perkins Road
Stillwater, Oklahoma 74075

CONTRACT INFORMATION:
Contract For: General Construction
Date: 5/14/2024

CERTIFICATE INFORMATION:
Certificate Number: 01
Date: 12/16/2024

OWNER: *(name and address)*
Independent School District No. 16 of
Payne County of Oklahoma
314 South Lewis Street
Stillwater, Oklahoma 74074

ARCHITECT: *(name and address)*
505 Architects LLC

1631 S. Delaware Avenue
Tulsa, Oklahoma 74104

CONTRACTOR: *(name and address)*
Lippert Bros., Inc.


PO Box 17450
Oklahoma City, Oklahoma 73136

The Work identified below has been reviewed and found, to the Architect's best knowledge, information, and belief, to be substantially complete. Substantial Completion is the stage in the progress of the Work when the Work or designated portion is sufficiently complete in accordance with the Contract Documents so that the Owner can occupy or utilize the Work for its intended use. The date of Substantial Completion of the Project or portion designated below is the date established by this Certificate.

(Identify the Work, or portion thereof, that is substantially complete.)
Entire project except boiler and chiller equipment.

505 Architects LLC

ARCHITECT *(Firm Name)*


SIGNATURE

Brian Thomas, AIA,
LEED AP; Principal

PRINTED NAME AND TITLE

12/13/2024

DATE OF SUBSTANTIAL COMPLETION

WARRANTIES

The date of Substantial Completion of the Project or portion designated above is also the date of commencement of applicable warranties required by the Contract Documents, except as stated below:

(Identify warranties that do not commence on the date of Substantial Completion, if any, and indicate their date of commencement.)
One-year period for correction of the Work

WORK TO BE COMPLETED OR CORRECTED

A list of items to be completed or corrected is attached hereto, or transmitted as agreed upon by the parties, and identified as follows:
(Identify the list of Work to be completed or corrected.)

Refer to attached Punch Lists dated 12.13.2024

The failure to include any items on such list does not alter the responsibility of the Contractor to complete all Work in accordance with the Contract Documents. Unless otherwise agreed to in writing, the date of commencement of warranties for items on the attached list will be the date of issuance of the final Certificate of Payment or the date of final payment, whichever occurs first. The Contractor will complete or correct the Work on the list of items attached hereto within thirty (30) days from the above date of Substantial Completion.

Cost estimate of Work to be completed or corrected: \$25,000.00

The responsibilities of the Owner and Contractor for security, maintenance, heat, utilities, damage to the Work, insurance, and other items identified below shall be as follows:

(Note: Owner's and Contractor's legal and insurance counsel should review insurance requirements and coverage.)
Owner

The Owner and Contractor hereby accept the responsibilities assigned to them in this Certificate of Substantial Completion:

Lippert Bros., Inc.

CONTRACTOR (*Firm Name*)

Independent School District
No. 16 of Payne County of
Oklahoma

OWNER (*Firm Name*)

T.M. Lippert

SIGNATURE

SIGNATURE

T.M. Lippert, President

PRINTED NAME AND TITLE

Dr. Marshall Baker, Board
of Education President

PRINTED NAME AND TITLE

12-16-24

DATE

DATE



Lippert Bros., Inc.
PO Box 17450
Oklahoma City, Oklahoma 73136
United States
(405) 478-3580

Punch Items for 1747 - Stillwater Public Schools - OES North & South Building Renovations 34 Items

#46: NB 1C1 - clean up/touch up base at tech space east entry

Type:	Location:
NB - OAC Punch List 12/13/24	
Date Created:	Due Date:
12/13/2024	12/16/2024
Priority:	Status:
	Work Required
Creator:	Reference:
Shelby Lippert	
Punch Item Manager:	Final Approver:
Mike Jones	Mike Jones
Ball in Court:	Assignee Name:
Mike Jones (Lippert Bros., Inc.)	Jones, Mike (Lippert Bros., Inc.)
	<i>Work Required</i>
Description:	



#47: NB - paint touch up throughout, typ

Type:	Location:
NB - OAC Punch List 12/13/24	
Date Created:	Due Date:
12/13/2024	12/16/2024
Priority:	Status:
	Work Required
Creator:	Reference:
Shelby Lippert	
Punch Item Manager:	Final Approver:
Mike Jones	Mike Jones
Ball in Court:	Assignee Name:
Guillermo Lopez (Silva Spray Foam, Inc.)	Lopez, Guillermo (Silva Spray Foam, Inc.)
	<i>Work Required</i>
Description:	





#48: NB - add wall/floor stop to any door that does not call for one / have one, typ

Type:
NB - OAC Punch List 12/13/24

Location:

Date Created:
12/13/2024

Due Date:
12/16/2024

Priority:

Status:
Work Required

Creator:
Shelby Lippert

Reference:


Punch Item Manager:
Mike Jones

Final Approver:
Mike Jones

Ball in Court:
Mike Jones (Lippert Bros., Inc.)

Assignee Name:
Jones, Mike (Lippert Bros., Inc.)
Work Required

Description:

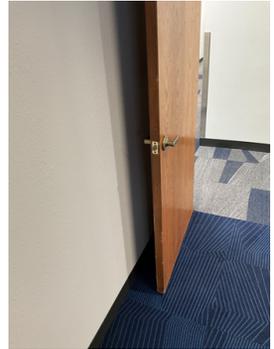

#49: NB - base adjustment add adhesive throughout, typ

Type:
NB - OAC Punch List 12/13/24

Location:

Date Created:
12/13/2024

Due Date:
12/16/2024

Priority:

Status:
Work Required

Creator:
Shelby Lippert

Reference:


Punch Item Manager:
Mike Jones


Final Approver:
Mike Jones

Ball in Court:
Alan Schiete (Akin Brothers Flooring)

Assignee Name:
Schiete, Alan (Akin Brothers Flooring)
Work Required

Description:

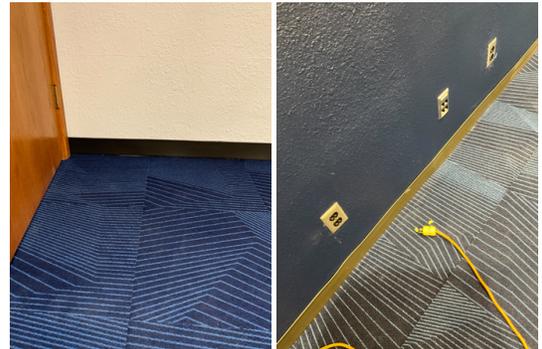

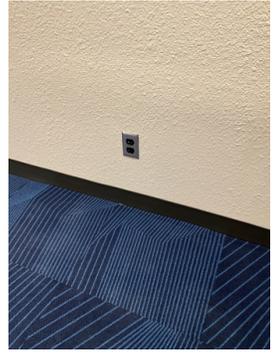

#50: NB 103 - remove paint from window shade chain

Type: **NB - OAC Punch List 12/13/24** Location:

Date Created: **12/13/2024** Due Date: **12/16/2024**

Priority: Status: **Work Required**

Creator: **Shelby Lippert** Reference:

Punch Item Manager: **Mike Jones** Final Approver: **Mike Jones**

Ball in Court: **Guillermo Lopez (Silva Spray Foam, Inc.)** Assignee Name: **Lopez, Guillermo (Silva Spray Foam, Inc.)**
Work Required

Description:



#51: NB 1C1 - west hall adjust light switch cover plate

Type: **NB - OAC Punch List 12/13/24** Location:

Date Created: **12/13/2024** Due Date: **12/16/2024**

Priority: Status: **Work Required**

Creator: **Shelby Lippert** Reference:

Punch Item Manager: **Mike Jones** Final Approver: **Mike Jones**

Ball in Court: **Ayden Hargrove (Stolhand Wells Plumbing, Heating & Air)** Assignee Name: **Hargrove, Ayden (Stolhand Wells Plumbing, Heating & Air)**
Jason Hillhouse (Stolhand Wells Plumbing, Heating & Air) *Work Required*
Hillhouse, Jason (Stolhand



Wells Plumbing, Heating & Air)

Work Required

**Luke Legg (Stolhand Wells
Plumbing, Heating & Air)**

**Legg, Luke (Stolhand Wells
Plumbing, Heating & Air)**

Work Required

Description:

#52: NB 100 - install entry vestibule light fixture

Type:
NB - OAC Punch List 12/13/24

Location:

Date Created:
12/13/2024

Due Date:
12/16/2024

Priority:

Status:
Work Required

Creator:
Shelby Lippert

Reference:

Punch Item Manager:
Mike Jones

Final Approver:
Mike Jones

Ball in Court:

Assignee Name:
**Hillhouse, Jason (Stolhand
Wells Plumbing, Heating & Air)**
Work Required
**Legg, Luke (Stolhand Wells
Plumbing, Heating & Air)**
Work Required
**Hargrove, Ayden (Stolhand
Wells Plumbing, Heating & Air)**
Work Required

**Jason Hillhouse (Stolhand
Wells Plumbing, Heating & Air)**
**Luke Legg (Stolhand Wells
Plumbing, Heating & Air)**
**Ayden Hargrove (Stolhand
Wells Plumbing, Heating & Air)**



Description:

#53: NB 1C1 - remove paint from wood trim in south hallway

Type:
NB - OAC Punch List 12/13/24

Location:

Date Created:
12/13/2024

Due Date:
12/16/2024

Priority:

Status:
Work Required

Creator:
Shelby Lippert

Reference:

Punch Item Manager:
Mike Jones

Final Approver:
Mike Jones

Ball in Court:

**Guillermo Lopez (Silva Spray
Foam, Inc.)**

Assignee Name:
**Lopez, Guillermo (Silva Spray
Foam, Inc.)**
Work Required



Description:

#54: NB 134 - paint along window jamb

Type: Location:

NB - OAC Punch List 12/13/24

Date Created: Due Date:
12/13/2024 12/16/2024

Priority: Status:
Work Required

Creator: Reference:
Shelby Lippert

Punch Item Manager: Final Approver:
Mike Jones Mike Jones

Ball in Court: Assignee Name:
Guillermo Lopez (Silva Spray Foam, Inc.) Lopez, Guillermo (Silva Spray Foam, Inc.)
Work Required

Description:



#55: NB 1C1 - caulk and paint corner guard outside of tech space at SW corner

Type: Location:

NB - OAC Punch List 12/13/24

Date Created: Due Date:
12/13/2024 12/16/2024

Priority: Status:
Work Required

Creator: Reference:
Shelby Lippert

Punch Item Manager: Final Approver:
Mike Jones Mike Jones

Ball in Court: Assignee Name:
Mike Jones (Lippert Bros., Inc.) Jones, Mike (Lippert Bros., Inc.)
Work Required

Description:



#56: NB 123 - regrout/ caulk crack grout joint

Type: Location:

NB - OAC Punch List 12/13/24

Date Created: Due Date:

12/13/2024

12/16/2024

Priority:

Status:

Work Required

Creator:

Shelby Lippert

Reference:

Punch Item Manager:

Mike Jones

Final Approver:

Mike Jones


Ball in Court:

Alan Schiete (Akin Brothers Flooring)

Assignee Name:

Schiete, Alan (Akin Brothers Flooring)
Work Required

Description:

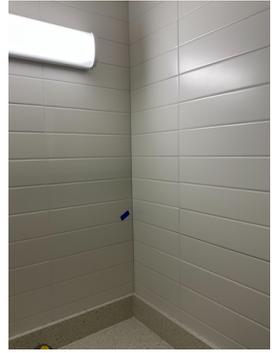

#57: NB 123 - seal backsplash to wall

Type:

NB - OAC Punch List 12/13/24

Location:

Date Created:

12/13/2024

Due Date:

12/16/2024

Priority:

Status:

Work Required

Creator:

Shelby Lippert

Reference:

Punch Item Manager:

Mike Jones

Final Approver:

Mike Jones

Ball in Court:

Kenneth Warner (NexSpaces)

Assignee Name:

Warner, Kenneth (NexSpaces)
Work Required

Description:



#58: NB 120 - seal backsplash to wall

Type:

NB - OAC Punch List 12/13/24

Location:

Date Created:

12/13/2024

Due Date:

12/16/2024

Priority:

Status:

Work Required

Creator:

Shelby Lippert

Reference:

Punch Item Manager:

Mike Jones

Final Approver:

Mike Jones

Ball in Court:

Assignee Name:



Kenneth Warner (NexSpaces)

Warner, Kenneth (NexSpaces)
Work Required

Description:

#59: NB 120 - install wall light fixture

Type:

Location:

NB - OAC Punch List 12/13/24

Date Created:

Due Date:

12/13/2024

12/16/2024

Priority:

Status:

Work Required

Creator:

Reference:

Shelby Lippert

Punch Item Manager:

Final Approver:

Mike Jones

Mike Jones

Ball in Court:

Assignee Name:

**Luke Legg (Stolhand Wells
Plumbing, Heating & Air)**

**Legg, Luke (Stolhand Wells
Plumbing, Heating & Air)**

Work Required

**Ayden Hargrove (Stolhand
Wells Plumbing, Heating & Air)**

**Hargrove, Ayden (Stolhand
Wells Plumbing, Heating & Air)**

Work Required

**Jason Hillhouse (Stolhand
Wells Plumbing, Heating & Air)**

**Hillhouse, Jason (Stolhand
Wells Plumbing, Heating & Air)**

Work Required

Description:



#60: NB 121 - install face plate at light switch

Type:

Location:

NB - OAC Punch List 12/13/24

Date Created:

Due Date:

12/13/2024

12/16/2024

Priority:

Status:

Work Required

Creator:

Reference:

Shelby Lippert

Punch Item Manager:

Final Approver:

Mike Jones

Mike Jones

Ball in Court:

Assignee Name:

**Luke Legg (Stolhand Wells
Plumbing, Heating & Air)**

**Legg, Luke (Stolhand Wells
Plumbing, Heating & Air)**

Work Required

**Jason Hillhouse (Stolhand
Wells Plumbing, Heating & Air)**

**Hillhouse, Jason (Stolhand
Wells Plumbing, Heating & Air)**

Work Required

**Ayden Hargrove (Stolhand
Wells Plumbing, Heating & Air)**



**Hargrove, Ayden (Stolhand
Wells Plumbing, Heating & Air)**
Work Required

Description:

#61: NB 120 - adjust handicap stall door

Type: **NB - OAC Punch List 12/13/24** Location:

Date Created: **12/13/2024** Due Date: **12/16/2024**

Priority: Status: **Work Required**

Creator: **Shelby Lippert** Reference:

Punch Item Manager: **Mike Jones** Final Approver: **Mike Jones**

Ball in Court: **Mike Jones (Lippert Bros., Inc.)** Assignee Name: **Jones, Mike (Lippert Bros., Inc.)**
Work Required

Description:



#62: NB 123 - install mirror

Type: **NB - OAC Punch List 12/13/24** Location:

Date Created: **12/13/2024** Due Date: **12/16/2024**

Priority: Status: **Work Required**

Creator: **Shelby Lippert** Reference:

Punch Item Manager: **Mike Jones** Final Approver: **Mike Jones**

Ball in Court: **Mike Jones (Lippert Bros., Inc.)** Assignee Name: **Jones, Mike (Lippert Bros., Inc.)**
Work Required

Description:



#63: NB 110 - install cord reels

Type: Location:

NB - OAC Punch List 12/13/24

Date Created: **12/13/2024** Due Date: **12/16/2024**
Priority: Status: **Work Required**

Creator: **Shelby Lippert** Reference:

Punch Item Manager: **Mike Jones** Final Approver: **Mike Jones**

Ball in Court: Assignee Name: **Legg, Luke (Stolhand Wells Plumbing, Heating & Air)**
Work Required
Hargrove, Ayden (Stolhand Wells Plumbing, Heating & Air)
Work Required
Jason Hillhouse (Stolhand Wells Plumbing, Heating & Air)
Work Required
Mike Jones (Lippert Bros., Inc.)
Work Required
Jones, Mike (Lippert Bros., Inc.)
Work Required

Description:



#64: NB 120 - install mirror


Type: **NB - OAC Punch List 12/13/24** Location:
Date Created: **12/13/2024** Due Date: **12/16/2024**
Priority: Status: **Work Required**

Creator: **Shelby Lippert** Reference:

Punch Item Manager: **Mike Jones** Final Approver: **Mike Jones**

Ball in Court: Assignee Name: **Jones, Mike (Lippert Bros., Inc.)**
Work Required

Description:

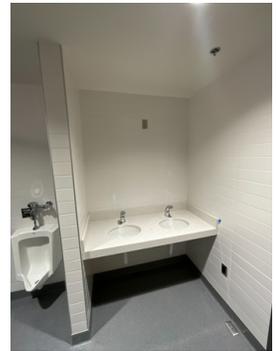

#65: NB - Ensure occupancy sensor controls in all offices and storage spaces are set to occupancy sensing

Type: **NB - MEP Punch List 12/13/24** Location:

Date Created:
12/13/2024

Due Date:
12/16/2024

Priority:

Status:
Work Required

Creator:
Shelby Lippert

Reference:

Punch Item Manager:
Mike Jones

Final Approver:
Mike Jones

Ball in Court:

Assignee Name:
**Hillhouse, Jason (Stolhand
Wells Plumbing, Heating & Air)**

**Jason Hillhouse (Stolhand
Wells Plumbing, Heating & Air)**
**Luke Legg (Stolhand Wells
Plumbing, Heating & Air)**
**Ayden Hargrove (Stolhand
Wells Plumbing, Heating & Air)**

Work Required
**Legg, Luke (Stolhand Wells
Plumbing, Heating & Air)**
Work Required

**Hargrove, Ayden (Stolhand
Wells Plumbing, Heating & Air)**
Work Required

Description:

#66: NB General - remove dirt, dust, debris and fingerprints from all fixtures

Type:
NB - MEP Punch List 12/13/24

Location:

Date Created:
12/13/2024

Due Date:
12/16/2024

Priority:

Status:
Work Required

Creator:
Shelby Lippert

Reference:

Punch Item Manager:
Mike Jones

Final Approver:
Mike Jones

Ball in Court:

**Mike Jones (Lippert Bros.,
Inc.)**

Assignee Name:
**Jones, Mike (Lippert Bros.,
Inc.)**
Work Required

Description:

#67: NB - Adjust all downlight fixture trims tight to ceiling with no gaps or spaces

Type:
NB - MEP Punch List 12/13/24

Location:

Date Created:
12/13/2024

Due Date:
12/16/2024

Priority:

Status:

Work Required

Creator:
Shelby Lippert

Reference:

Punch Item Manager:
Mike Jones

Final Approver:
Mike Jones

Ball in Court:

Assignee Name:
Hillhouse, Jason (Stolhand Wells Plumbing, Heating & Air)
Work Required
Hargrove, Ayden (Stolhand Wells Plumbing, Heating & Air)
Work Required
Legg, Luke (Stolhand Wells Plumbing, Heating & Air)
Work Required

Jason Hillhouse (Stolhand Wells Plumbing, Heating & Air)
Ayden Hargrove (Stolhand Wells Plumbing, Heating & Air)
Luke Legg (Stolhand Wells Plumbing, Heating & Air)

Description:

#68: NB - remove dust and paint from duplex receptacles, devices and cover plates

Type:
NB - MEP Punch List 12/13/24

Location:

Date Created:
12/13/2024

Due Date:
12/16/2024

Priority:

Status:
Work Required

Creator:
Shelby Lippert

Reference:

Punch Item Manager:
Mike Jones

Final Approver:
Mike Jones

Ball in Court:

Guillermo Lopez (Silva Spray Foam, Inc.)
Mike Jones (Lippert Bros., Inc.)

Assignee Name:
Lopez, Guillermo (Silva Spray Foam, Inc.)
Work Required
Jones, Mike (Lippert Bros., Inc.)
Work Required

Description:

#69: NB - verify operations of emergency fixtures

Type:
NB - MEP Punch List 12/13/24

Location:

Date Created:
12/13/2024

Due Date:
12/16/2024

Priority:

Status:
Work Required

Creator:
Shelby Lippert

Reference:

Punch Item Manager:
Mike Jones

Final Approver:
Mike Jones

Ball in Court:

Assignee Name:
**Hillhouse, Jason (Stolhand
Wells Plumbing, Heating & Air)**

**Jason Hillhouse (Stolhand
Wells Plumbing, Heating & Air)**
**Ayden Hargrove (Stolhand
Wells Plumbing, Heating & Air)**
**Luke Legg (Stolhand Wells
Plumbing, Heating & Air)**

Work Required
**Hargrove, Ayden (Stolhand
Wells Plumbing, Heating & Air)**
Work Required
**Legg, Luke (Stolhand Wells
Plumbing, Heating & Air)**
Work Required

Description:

#70: NB 1C1 - ceiling mounted WAP's not installed in Hallway

Type:
NB - MEP Punch List 12/13/24

Location:

Date Created:
12/13/2024

Due Date:
12/16/2024

Priority:

Status:
Work Required

Creator:
Shelby Lippert

Reference:

Punch Item Manager:
Mike Jones

Final Approver:
Mike Jones

Ball in Court:

Garrett Gil (Scout Systems)

Assignee Name:
Gil, Garrett (Scout Systems)
Work Required

Description:

#71: NB - adjust toilet flush valves as best as possible to assist with water pressure issues

Type:
NB - MEP Punch List 12/13/24

Location:

Date Created:
12/13/2024

Due Date:
12/16/2024

Priority:

Status:
Work Required

Creator:
Shelby Lippert

Reference:

Punch Item Manager:
Mike Jones

Final Approver:
Mike Jones

Ball in Court: Aaron Short (Stolhand Wells Plumbing, Heating & Air)
Assignee Name: Short, Aaron (Stolhand Wells Plumbing, Heating & Air)
Work Required

Description:

#72: NB - ensure water piping identification has been provided

Type: NB - MEP Punch List 12/13/24
Location:
Date Created: 12/13/2024
Due Date: 12/16/2024
Priority:
Status: Work Required

Creator: Shelby Lippert
Reference:

Punch Item Manager: Mike Jones
Final Approver: Mike Jones

Ball in Court: Aaron Short (Stolhand Wells Plumbing, Heating & Air)
Assignee Name: Short, Aaron (Stolhand Wells Plumbing, Heating & Air)
Work Required

Description:

#73: NB - Adjust "run time" for all automatic sensor faucets. LBI to assist with Owner's desired run time

Type: NB - MEP Punch List 12/13/24
Location:
Date Created: 12/13/2024
Due Date: 12/16/2024
Priority:
Status: Work Required

Creator: Shelby Lippert
Reference:

Punch Item Manager: Mike Jones
Final Approver: Mike Jones

Ball in Court: Aaron Short (Stolhand Wells Plumbing, Heating & Air)
Assignee Name: Short, Aaron (Stolhand Wells Plumbing, Heating & Air)
Work Required
Mike Jones (Lippert Bros., Inc.)
Jones, Mike (Lippert Bros., Inc.)
Work Required

Description:

#74: NB - provide return air grilles in rooms 109, 111, & 129 as indicated on drawings

Type: **NB - MEP Punch List 12/13/24** Location:
Date Created: **12/13/2024** Due Date: **12/16/2024**
Priority: Status: **Work Required**
Creator: **Shelby Lippert** Reference:
Punch Item Manager: **Mike Jones** Final Approver: **Mike Jones**
Ball in Court: **Jason Troutman (Stolhand Wells Plumbing, Heating & Air)** Assignee Name: **Troutman, Jason (Stolhand Wells Plumbing, Heating & Air)**
Work Required
Description:

#75: NB - Add two 24x24 return air grilles in room 110

Type: **NB - MEP Punch List 12/13/24** Location:
Date Created: **12/13/2024** Due Date: **12/16/2024**
Priority: Status: **Work Required**
Creator: **Shelby Lippert** Reference:
Punch Item Manager: **Mike Jones** Final Approver: **Mike Jones**
Ball in Court: **Jason Troutman (Stolhand Wells Plumbing, Heating & Air)** Assignee Name: **Troutman, Jason (Stolhand Wells Plumbing, Heating & Air)**
Work Required
Description:

#76: NB - replace all ceiling grilles in Science Kit Storage 800

Type: **NB - MEP Punch List 12/13/24** Location:
Date Created: **12/13/2024** Due Date: **12/16/2024**
Priority: Status: **Work Required**

Creator:
Shelby Lippert

Reference:

Punch Item Manager:
Mike Jones

Final Approver:
Mike Jones

Ball in Court:
**Jason Troutman (Stolhand
Wells Plumbing, Heating & Air)**

Assignee Name:
**Troutman, Jason (Stolhand
Wells Plumbing, Heating & Air)**
Work Required

Description:

#77: (OWNER) NB - AI to complete installation of all HVAC temperature controls

Type:
NB - MEP Punch List 12/13/24

Location:

Date Created:
12/13/2024

Due Date:
12/16/2024

Priority:

Status:
Work Required

Creator:
Shelby Lippert

Reference:

Punch Item Manager:
Mike Jones

Final Approver:
Mike Jones

Ball in Court:
**Tory Friesen (Automations
Integrated, LLC)**

Assignee Name:
**Friesen, Tory (Automations
Integrated, LLC)**
Work Required

Description:

#78: NB - complete TAB and submit report

Type:
NB - MEP Punch List 12/13/24

Location:

Date Created:
12/13/2024

Due Date:
12/16/2024

Priority:

Status:
Work Required

Creator:
Shelby Lippert

Reference:

Punch Item Manager:
Mike Jones

Final Approver:
Mike Jones

Ball in Court:
**Jason Troutman (Stolhand
Wells Plumbing, Heating & Air)**

Assignee Name:
**Troutman, Jason (Stolhand
Wells Plumbing, Heating & Air)**
Work Required

Description:

#79: NB - provide as-built drawings

Type: Location:

NB - MEP Punch List 12/13/24

Date Created: Due Date:
12/13/2024 12/16/2024

Priority: Status:
Work Required

Creator: Reference:
Shelby Lippert

Punch Item Manager: Final Approver:
Mike Jones Mike Jones

Ball in Court: Assignee Name:
Jason Hillhouse (Stolhand Wells Plumbing, Heating & Air)
Work Required
Aaron Short (Stolhand Wells Plumbing, Heating & Air)
Work Required
Jason Troutman (Stolhand Wells Plumbing, Heating & Air)
Work Required

Description:
