MIDWAY OPERATIONS




2026 BOND PROJECT UPDATE

November 17, 2026

MIDWAY HS ADDITIONS & RENOVATIONS

- Grade Beams Complete
- Underground Plumbing 70%
- Electrical Conduits Schudeled for 11/23
- 1st Slab Pour Scheduled for 12/1
- Structural CMU Scheduled to Start 12/14
- Project Remains on Schedule

Midway HS	GMP1	GMP2
Total GMP	$1,327,908	$12,131,859
Billed To Date	$747,745	$977,175
Balance To Finish	$580,162	$11,154,683
Remaining Contingency	$164,720	$1,349,242

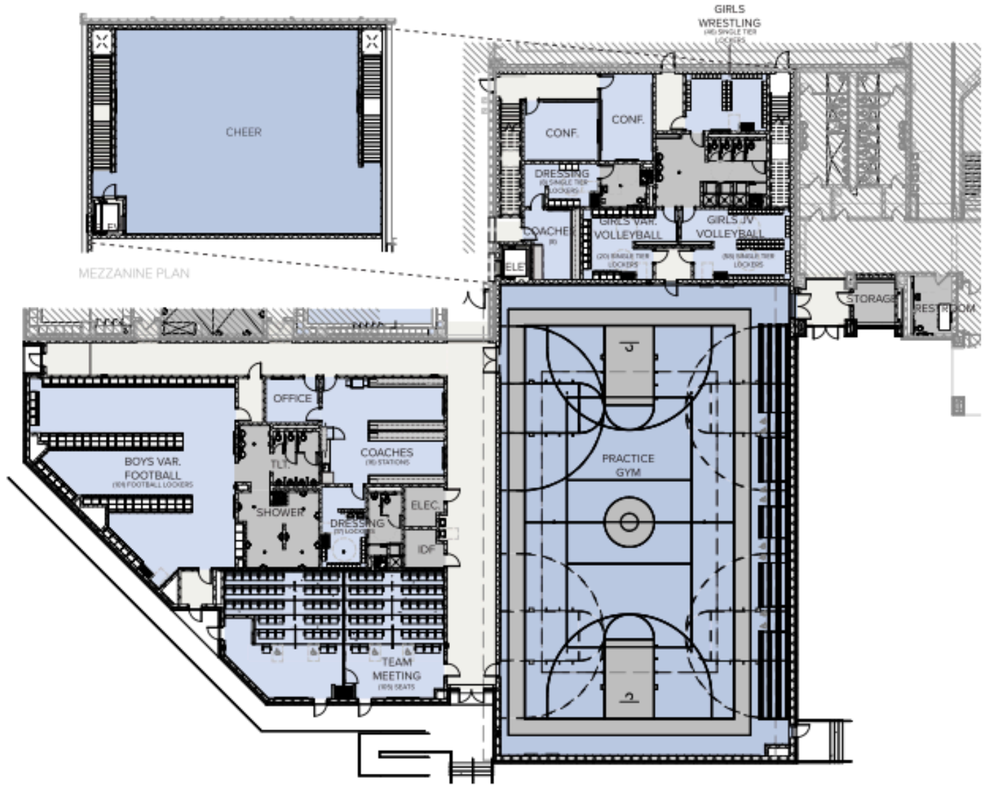

MIDWAY HS ADDITIONS & RENOVATIONS





Overhead Drone Pics of Construction Site

MIDWAY HS ADDITIONS & RENOVATIONS



Underground Plumbing



Underground Plumbing



Underground Plumbing

MIDWAY HS ADDITIONS & RENOVATIONS



Termite Treatment Complete



Structural CMU Support



Brick Veneer Selection

DEFERRED MAINTENANCE

Up-Coming Projects

- Castleman Creek
  - HVAC - Offices/Classrooms
    - This will complete CCE HVAC Update
    - Work will happen over Thanksgiving/Christmas Breaks
- Administration Building
  - Generator Install and Electrical Upgrades for Technology
  - Work is tentatively scheduled for Christmas Break
  - Equipment leadtimes driving project schedule
- RVMS
  - Drinking fountain replacements over Thanksgiving Break

QUESTIONS

Ken Wolf, Director of Operations
