



Mission Consolidated Independent School District

- 1201 Bryce Drive, Mission, Texas 78572
- Telephone: (956) 323 5505 Fax: (956) 323 5634
- Website: www.mcisd.net

Notice and Agenda

The Board of Trustees of the Mission Consolidated Independent School District will hold a **Special Meeting on Wednesday, February 2, 2022, at 6:30 PM** in the **Mission CISD Annex, 925 E. Business HWY. 83, Mission, Tx 78572**. At this meeting, the Board may deliberate or act on any of the subjects listed on the following agenda. The President may change the order of items listed below for the convenience of the Board.

A G E N D A

- I. Call to Order and Establish Quorum**
- II. Pledge of Allegiance and Moment of Silence**
 - 1. U. S. Flag and Texas Flag -**
- III. Comments from the Public**
- IV. Public Comment(s) on Specific Agenda Item(s)**
- V. Superintendent's Updates and Recognitions**
- VI. Presentation(s) to the Board of Trustees**
 - 1. Status Report/Presentation on the Tom Landry Stadium Repairs – Ricardo Hinojosa Structural Engineering & G&G Contracting** **3**
- VII. Discussion and Possible Action**
 - 1. Consideration and Approval of Change Order(s) for the Tom Landry Stadium Repairs Project – Ricardo Hinojosa Structural Engineering & G&G Contracting** **31**
 - 2. Consideration and Approval of Project and Proposed Budget for Supplemental Repairs (Visitors Side) for the Tom Landry Stadium Project** **53**
 - 3. Consideration and Approval of Procurement Method, Selection Criteria, Review and Ranking Committee, Wage Rate, and Authorization to Seek Proposals/Bids for Supplemental Repairs (Visitors Side) for the Tom Landry Stadium Project** **75**
- VIII. Executive Session**
 - 1. Private Consultation with Board Attorney (Texas Gov't Code §551.071)**
- IX. Action, if Necessary, on Matters Discussed in Executive Session**
- X. Important Dates to Remember**
 - 1. February 9, 2022 Regular Board of Trustees Meeting at 6:30 p.m.**
 - 2. February 14, 2022 School Holiday**
- XI. Adjournment**

In accordance with the Texas Open Meetings Act, the Board may enter into a closed meeting to deliberate any item that is listed above that fits within an exception listed in Subchapter D. Any final action, decision, or vote on a subject deliberated in closed meeting will be taken in an open meeting held in compliance with the Texas Open Meetings Act.

This Notice was posted by 6:00 p.m., on January 28, 2022


Dr. Carol G. Perez, Superintendent of Schools
Mission Consolidated Independent School District

MCISD Tom Landry Stadium
Civil & Structural Repairs
Competitive Seal Proposal #520-21-0

February 2, 2022
MCISD School Board of Trustees Meeting
PROGRESS REPORT

General Contractor: R&G Enterprises, LLC dba G&G Contractors
Contract Amount: \$1,024,850.00
Overall Completion: 10%

MILESTONES

Receipt of Bids: April 22, 2021
Contract Time: 210 Days
Notice to Proceed: July 28, 2021
Original Substantial Completion: February 23, 2022
Delays (Weather/AEP/CPs/COs): 44 Days
New Substantial Completion: April 8, 2022
Original Final Completion: March 25, 2022
(30 Calendar Days after Substantial Completion)
New Final Completion: May 8, 2022

Allowances

Contingency-bird screen under press box: \$25,000.00	0%	Used
Contingency-Project Sign: \$2,000.00 Owner's	0%	Used
Contingency-for use according To owner's written instructions: \$20,000.00	41.2%	Used: \$8,241.88 Balance: \$11,758.12


Home Side Bleacher Area

Aluminum Bleacher and Ramp Repairs	20%	Complete
Cardinal Chairs Repairs/Replacement	0%	Complete
Flatwork in front of Building Repairs	0%	Complete
Demolition of Existing Piers (25 of 102)	24%	Complete
Repair of Existing Piers (25 of 102 have Reinforcement)	12%	Complete
Replacement of Galvanized Steel Columns	0%	Complete
Replacement of Galvanized Steels Cross Bracing	0%	Complete
Guard Rail & Barriers Installation	0%	Complete

Visitors Side Bleacher Area

Aluminum Bleacher and Ramp Repairs	10%	Complete
Demolition of Existing Piers (0 of 54)	0%	Complete
Repair of Existing Piers (0 of 54)	0%	Complete
Replacement of Galvanized Steel Columns	0%	Complete
Replacement of Galvanized Steels Cross Bracing	0%	Complete

MCISD TOM LANDRY STADIUM
CIVIL AND STRUCTURAL REPAIRS CSP #520-21-0
MCISD Board of Trustees Workshop Meeting
January 13, 2022

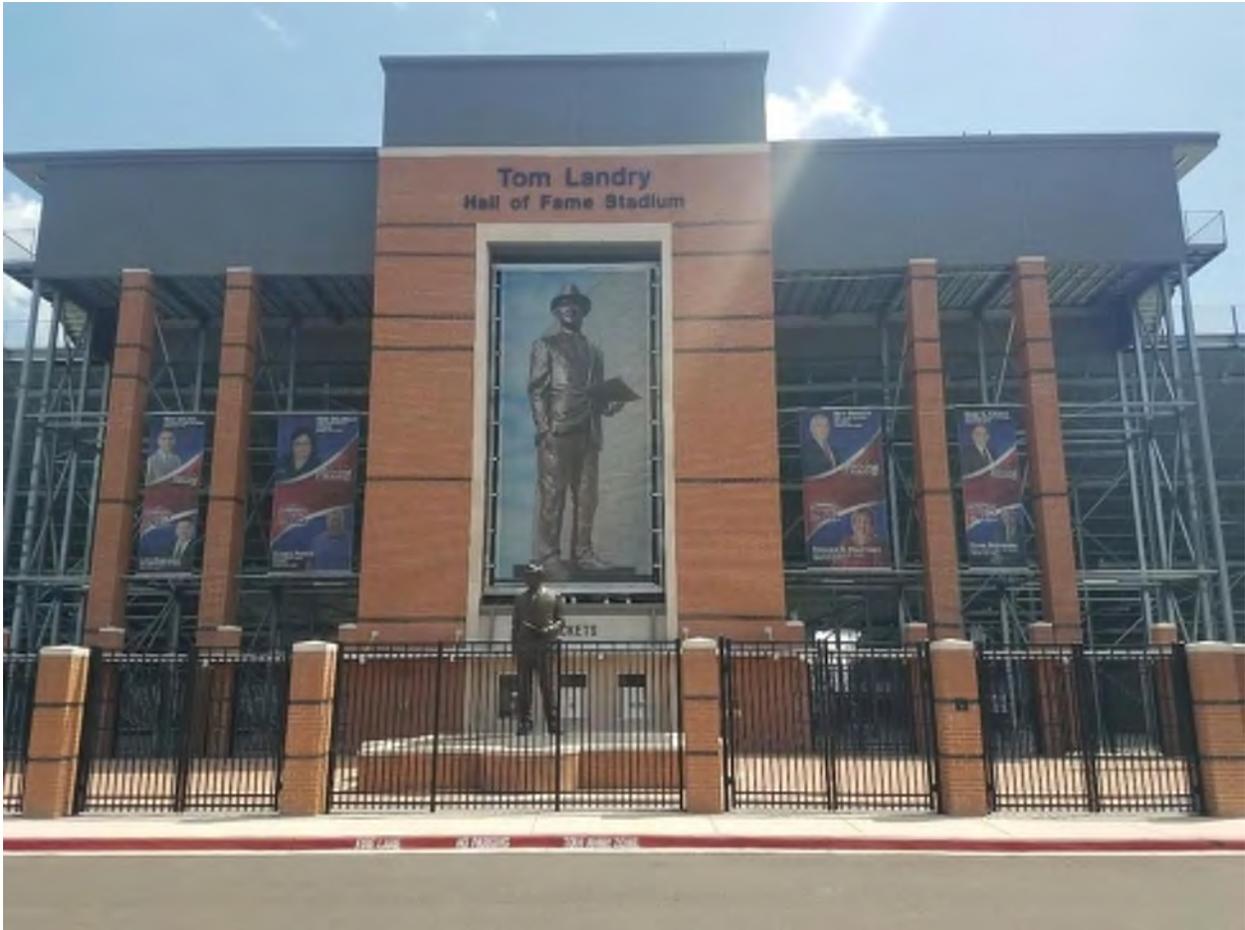

Status as of January 24th

Updates:

Home Side Piers

- 25 piers of the 102 piers have had the concrete removed a minimum of 42 inches per the repair detail. (See Attachments)
- 25 piers of the 102 piers have had the reinforcing in place. It was noticed that several existing pier reinforcement centers from the existing piers are not aligned with the center of the anchor rod group along gridline "B" and at the center of the columns along gridline "C". Cost and time change order is pending.

Home Side Pier Located at Gridlines “C” &”16” (See Attachments)

- The center of the exposed pier vertical reinforcement does not align with the center of the column. Debris was found during the excavation of this pier.
- Cost and time change order is pending.

Home Side Pier Located at Gridline “C2” and “E14-E5”, Offsets above Existing Construction Joint. (See Attachments)

- It was noticed that the existing conditions of the pier construction above the construction joint were offsetted. Cost and time change order is pending.

Visitors side piers

Visitor Side Pier Located at Gridline “B3”, “B5”, “B7”, “B9”, “B11”, “B13”, “B15”, Offsets above Existing Construction Joint. (See Attachments)

- It was noticed that the existing conditions of the pier construction above the construction joint were offsetted. Cost and time change order is pending.



HINOJOSA ENGINEERING, INC.

Civil Engineering • Structural Engineering

108 West 18th Street Mission, Texas 78572

Tel: (956) 581-0143 | Fax: (956) 581-2074

Registration Number F-908 | Expiration Date 09/30/2022


Date: 01/03/2022

Project Name: MCISD Tom Landry Stadium Civil & Structural Repairs Competitive Seal Proposal #520-21-0

Project Location: W 15th St., Mission, TX 78572

Comments: 01-03-2022 Tom Landry Stadium Home Side Gridline A


Piers A17-A12

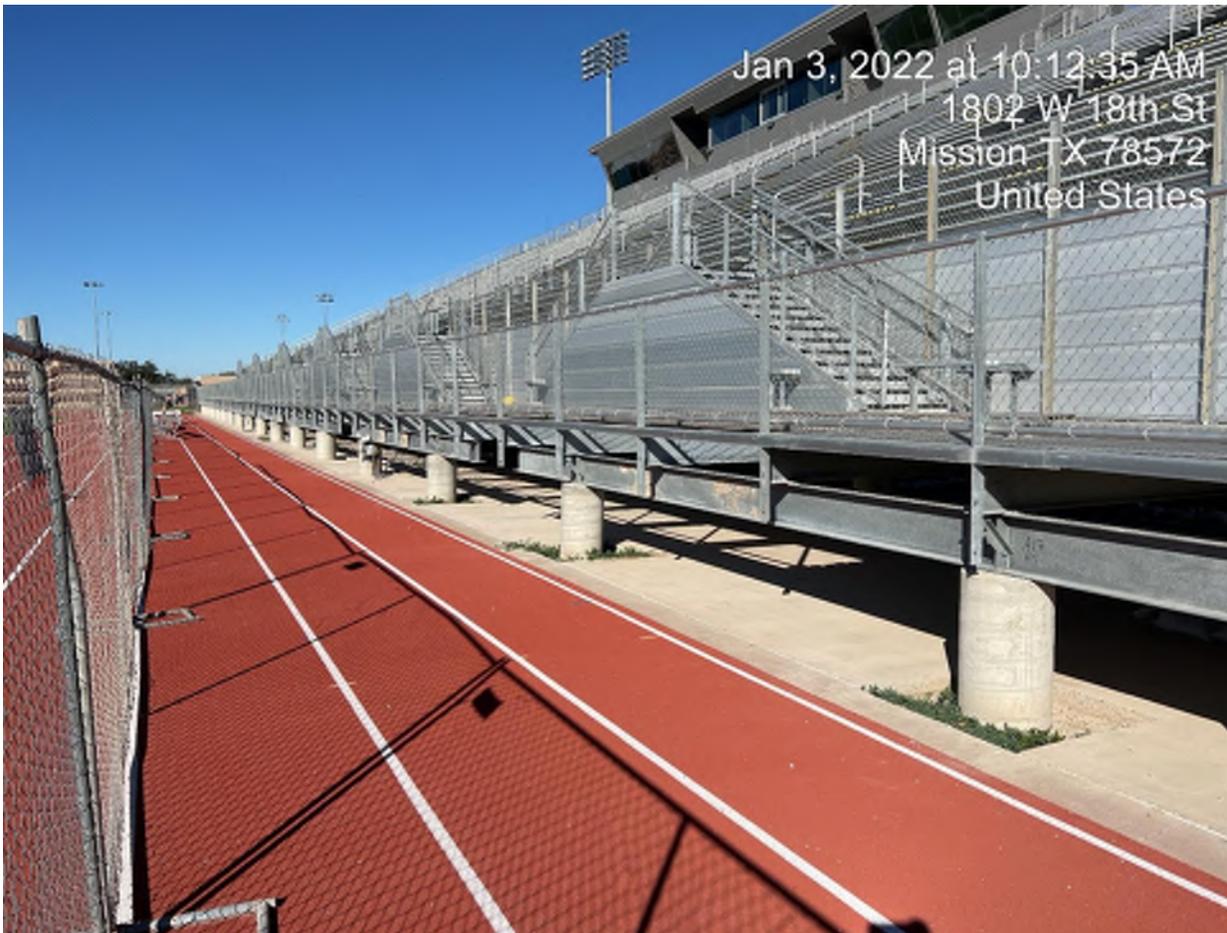

Comments:

- Homeside Gridline A is shown above


Piers A11-A7

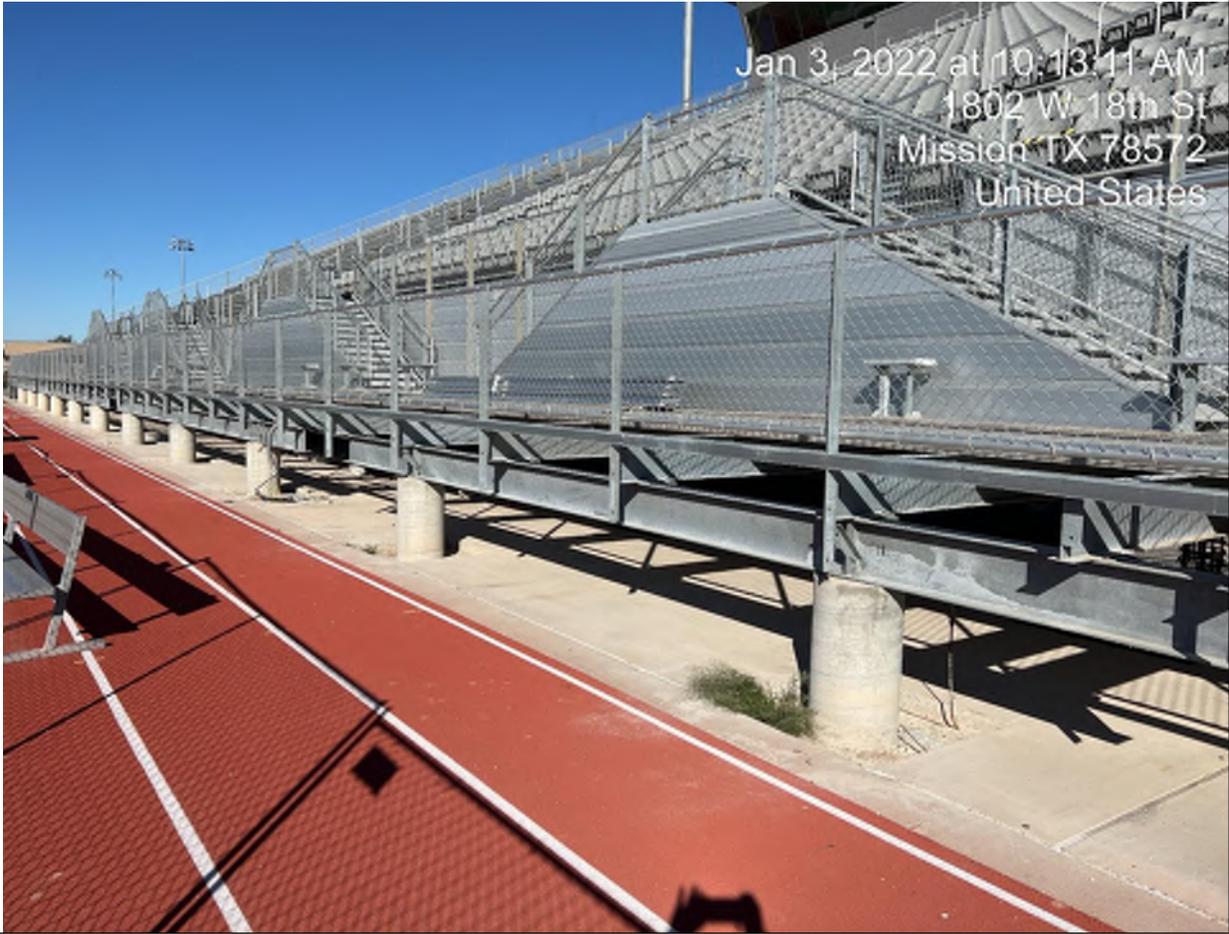

Comments:

- Homeside Gridline A is shown above

Piers A6-A1

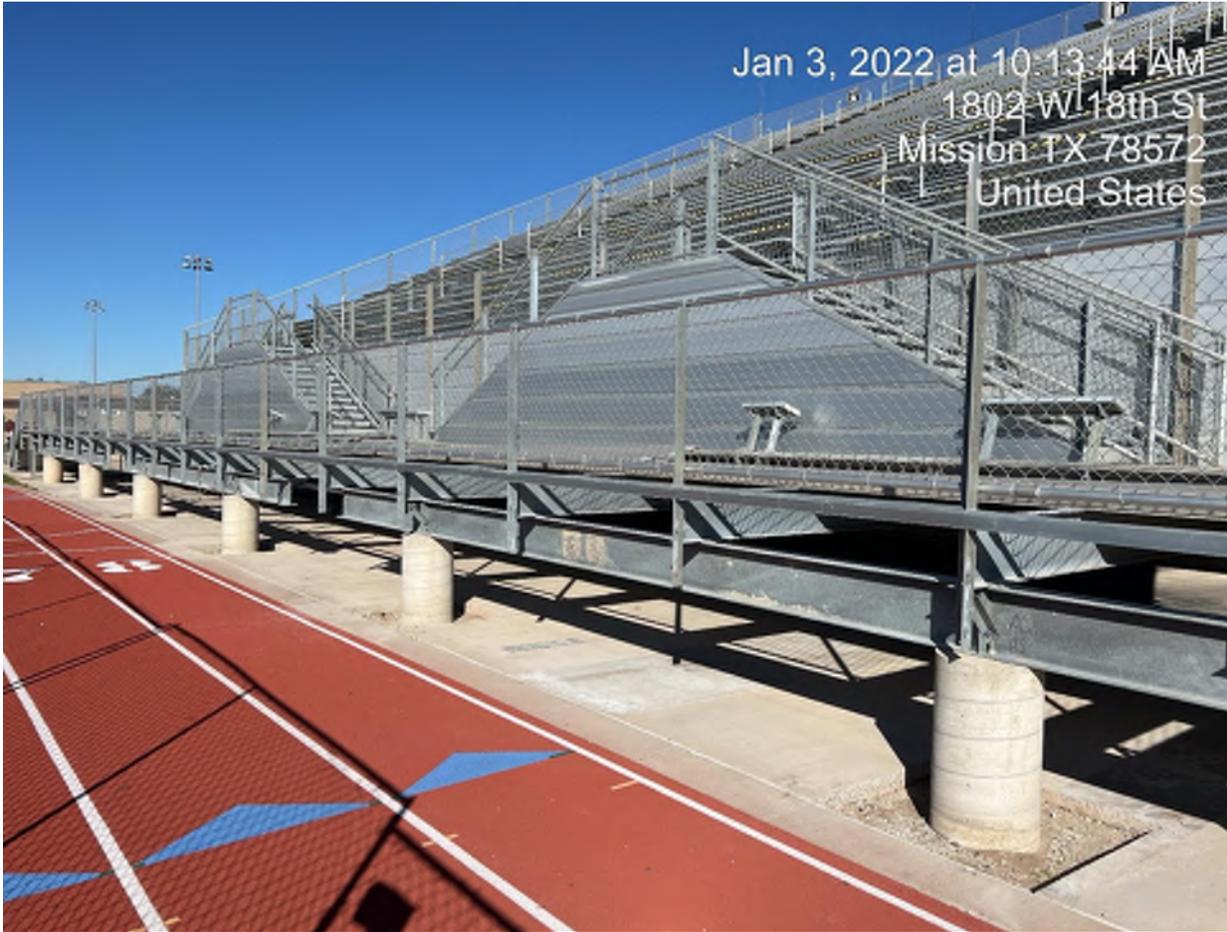

Comments:

- Homeside Gridline A is shown above

Notice: Observation and/or statements made on this document do not affect or replace project plans, specifications, or contractual requirements.

Respectfully Submitted,
Alberto Trevino Sr.

Photos By: Antonio Navarro IV (Construction administrator)
Report Typed By: Antonio Navarro IV (Construction administrator)
Report Done By: Alberto Trevino Sr. (Structural Project Manager)



HINOJOSA ENGINEERING, INC.

Civil Engineering • Structural Engineering

108 West 18th Street Mission, Texas 78572

Tel: (956) 581-0143 | Fax: (956) 581-2074

Registration Number F-908 | Expiration Date 09/30/2022

Date: 01/03/2022

Project Name: MCISD Tom Landry Stadium Civil & Structural Repairs Competitive Seal Proposal #520-21-0

Project Location: W 15th St., Mission, TX 78572

Comments: 01-03-2022 Tom Landry Stadium Home Side Piers

East Section



Comments:

- Homeside Gridline B-D East section is shown above

Middle Section



Comments:

- Homeside Gridline B-D East section is shown above

West Section



Comments:

- Homeside Gridline B-D East section is shown above

Notice: Observation and/or statements made on this document do not affect or replace project plans, specifications, or contractual requirements.

Respectfully Submitted,
Alberto Trevino Sr.

Photos By: Antonio Navarro IV (Construction administrator)
Report Typed By: Antonio Navarro IV (Construction administrator)
Report Done By: Alberto Trevino Sr. (Structural Project Manager)



HINOJOSA ENGINEERING, INC.

Civil Engineering • Structural Engineering

108 West 18th Street Mission, Texas 78572

Tel: (956) 581-0143 | Fax: (956) 581-2074

Registration Number F-908 | Expiration Date 09/30/2022

Date: 01/03/2022

Project Name: MCISD Tom Landry Stadium Civil & Structural Repairs Competitive Seal Proposal #520-21-0

Project Location: W 15th St., Mission, TX 78572

Comments: 01-03-2022 Tom Landry Stadium Home Side Gridline F

Piers F17-F12



Comments:

- Homeside Gridline F is shown above

Piers F11-F7



Comments:

- Homeside Gridline F is shown above

Piers F6-F1



Comments:

- Homeside Gridline F is shown above

Notice: Observation and/or statements made on this document do not affect or replace project plans, specifications, or contractual requirements.

Respectfully Submitted,
Alberto Trevino Sr.

Photos By: Antonio Navarro IV (Construction administrator)
Report Typed By: Antonio Navarro IV (Construction administrator)
Report Done By: Alberto Trevino Sr. (Structural Project Manager)



HINOJOSA ENGINEERING, INC.

Civil Engineering • Structural Engineering

108 West 18th Street Mission, Texas 78572

Tel: (956) 581-0143 | Fax: (956) 581-2074

Registration Number F-908 | Expiration Date 09/30/2022

Date: 01/03/2022

Project Name: MCISD Tom Landry Stadium Civil & Structural Repairs Competitive Seal Proposal #520-21-0

Project Location: W 15th St., Mission, TX 78572

Comments: 01-03-2022 Tom Landry Stadium Home Side Excavation of Gridline E

Photo: 1

E17

- The demolished flatwork around the pier has been removed.



Photo: 2

E16

- The demolished flatwork around the pier has been removed.



Photo: 3

E15

- The demolished flatwork around the pier has been removed.



Photo: 4

E14

- Pier has been Excavated.
- Offset can be seen.



Photo: 5

E13

- Pier has been Excavated.
- Offset can be seen.



Photo: 6

- Pier has been Excavated.
- Offset can be seen.

E12



Photo: 7

- Pier has been Excavated.
- Offset can be seen.

E11



Photo: 8

- Pier has been Excavated.
- Offset can be seen.

E10



Photo: 9

- Pier has been Excavated.
- Offset can be seen.

E9



Photo: 10

- Pier has been Excavated.
- Offset can be seen.

E8



Photo: 11

- Pier has been Excavated.
- Offset can be seen.

E7



<p>Photo: 12</p> <ul style="list-style-type: none"> • Pier has been Excavated. • Offset can be seen. 	<p>E6</p>	
<p>Photo: 13</p> <ul style="list-style-type: none"> • Pier has been Excavated. • Offset can be seen. 	<p>E5</p>	
<p>Photo: 14</p> <ul style="list-style-type: none"> • The demolished flatwork around the pier has been removed. • Pier dirt removal Has commenced. 	<p>E4</p>	

<p>Photo: 15 E3</p> <ul style="list-style-type: none"> The demolished flatwork around the pier has been removed. 	
<p>Photo: 16 E2</p> <ul style="list-style-type: none"> The demolished flatwork around the pier has been removed. 	
<p>Photo: 17 E1</p> <ul style="list-style-type: none"> The demolished flatwork around the pier has been removed. 	

Notice: Observation and/or statements made on this document do not affect or replace project plans, specifications, or contractual requirements.

Respectfully Submitted,
Alberto Trevino Sr.

Photos By: Jose L. Gomez (Construction Administrator)
Report Typed By: Jose L. Gomez (Construction Administrator)
Report Done By: Alberto Trevino Sr. (Structural Project Manager)



HINOJOSA ENGINEERING, INC.

Civil Engineering • Structural Engineering

108 West 18th Street Mission, Texas 78572

Tel: (956) 581-0143 | Fax: (956) 581-2074

Registration Number F-908 | Expiration Date 09/30/2022

Date: 01/03/2022

Project Name: MCISD Tom Landry Stadium Civil & Structural Repairs Competitive Seal Proposal #520-21-0

Project Location: W 15th St., Mission, TX 78572

Comments: 01-03-2022 Tom Landry Stadium Visitors Side Piers

East Section



Comments:

- Homeside Gridline A and B East section is shown above

Middle Section



Comments:

- Homeside Gridline A and B middle section is shown above

West Section



Comments:

- Homeside Gridline A and B West section is shown above

Notice: Observation and/or statements made on this document do not affect or replace project plans, specifications, or contractual requirements.

Respectfully Submitted,
Alberto Trevino Sr.

Photos By: Antonio Navarro IV (Construction administrator)
Report Typed By: Antonio Navarro IV (Construction administrator)
Report Done By: Alberto Trevino Sr. (Structural Project Manager)



HINOJOSA ENGINEERING, INC.

Civil Engineering • Structural Engineering

108 West 18th Street Mission, Texas 78572

Tel: (956) 581-0143 | Fax: (956) 581-2074

Registration Number F-908 | Expiration Date 09/30/2022

Date: 01/03/2022

Project Name: MCISD Tom Landry Stadium Civil & Structural Repairs Competitive Seal Proposal #520-21-0

Project Location: W 15th St., Mission, TX 78572

Comments: 01-03-2022 Tom Landry Stadium Visitors side Side gridline C

Piers C18-C13



Comments:

- Visitors side Gridline C is shown above

Pier C7-12



Jan 3, 2022 at 10:43:10 AM
1802 W 18th St
Mission TX 78572
United States

Comments:

- Visitors side Gridline C is shown above

Pier C6-C1



Comments:

- Visitors side Gridline C is shown above

Notice: Observation and/or statements made on this document do not affect or replace project plans, specifications, or contractual requirements.

Respectfully Submitted,
Alberto Trevino Sr.

Photos By: Antonio Navarro IV (Construction administrator)
Report Typed By: Antonio Navarro IV (Construction administrator)
Report Done By: Alberto Trevino Sr. (Structural Project Manager)



HINOJOSA ENGINEERING, INC.

Civil Engineering • Structural Engineering

108 West 18th Street Mission, Texas 78572

Tel: (956) 581-0143 | Fax: (956) 581-2074

Registration Number F-908 | Expiration Date 09/30/2022

Date: 01/10/2022

Project Name: MCISD Tom Landry Stadium Civil & Structural Repairs Competitive Seal Proposal #520-21-0

Project Location: W 15th St., Mission, TX 78572

Comments: 01-10-2022 Tom Landry Stadium Visitors Side Progress Report

Pier B3 Visitors side



Comments:

- Excavation of Pier B3 has commenced

Pier B5 Visitors side



Comments:

- Excavation of Pier B5 has commenced

Pier B7 Visitors side



Comments:

- Excavation of Pier B7 has commenced

Pier B9 Visitors side



Comments:

- Excavation of Pier B9 has commenced

Pier B11 Visitors side



Comments:

- Excavation of Pier B11 has commenced

Pier B13 Visitors side



Comments:

- Excavation of Pier B13 has commenced

Pier B15 Visitors side



Comments:

- Excavation of Pier B15 has commenced

Notice: Observation and/or statements made on this document do not affect or replace project plans, specifications, or contractual requirements.

Respectfully Submitted,

Alberto Trevino Sr.

Photos By: Antonio Navarro IV (Construction administrator)

Report Typed By: Antonio Navarro IV (Construction administrator)

Report Done By: Alberto Trevino Sr. (Structural Project Manager)

SUBJECT: Consideration and Approval of Change Order(s) for the Tom Landry Stadium Repairs Project

PRESENTER: Ricardo Rivera
Assistant Superintendent for Operations

BACKGROUND INFORMATION

STADIUM:

Tom Landry Stadium was built in approximately 1976 and additional seating was installed in approximately 1989. It currently has only four (4) handicap seating spaces on both the home and visitors' side. The home side has a seating capacity for 5000 persons and the visitor's side has a seating capacity for 4000 persons.

At the Regular Board of Trustees meeting held on Wednesday, August 11, 2010 the Board approved a structural assessment to be conducted by Rick Hinojosa Structural Engineering. A report was completed on August 27, 2010. No further action was taken.

At a football game on September 26, 2013 and at the Regular Board of Trustees meeting of Wednesday, October 09, 2013, a concerned citizen brought to attention the fact that Tom Landry Stadium was not in compliance with the American Disabilities Act (ADA) current code concerning the required handicap seating spaces. As per ADA the breakdown for seating is 6 spaces for 1 – 500 seats then 1 seat for every 150 additional seats. As per calculations required additional seating on the home side will be 36 ADA seats and, on the visitors, side will be an additional 30.

On October 08, 2013 I contacted Mr. Tim Petty, Program Specialist V with the Texas Education Agency (TEA) to discuss this issue and he confirmed that we were not in compliance with current codes and standards concerning stadium seating.

At the Regular Board of Trustees meeting held on Wednesday, December 11, 2013 and after consultation with our legal counsel, the Board approved for renovations to the Tom Landry Stadium Press Box and for the additional required ADA stadium seating.

The current press box is approximately 30 years old and has never been renovated. When new bleacher seating was installed the press was moved by crane to its current location. With the installation of a new scoreboard additional staff will need to be placed in the press box to operate the system. Currently approximately nine persons are in the box, however, it is now estimated that up to twenty-two persons may be in the box at any given time. This added weight along with the additional weight of chairs and equipment may cause a stress on the structure. As per our legal counsel, there is no legal law that states that the structure needs to be evaluated, however, for safety precautions Administration is considering a structural assessment study to be conducted on the press box to ensure that the structure is capable of sustaining the additional weight.

At the Regular Board of Trustees meeting held on Wednesday, March 20, 2013 Administration presented and the Board approved Consideration and Approval to Contract with Rick Hinojosa Engineering for a Re-Assessment of the Tom Landry Stadium Press Box.

At the Regular Board of Trustees meeting held on Wednesday, April 10, 2013 the Board was advised that due to concerns and possible code regulations requiring an elevator to be installed for the press box, inquiries were made to Mr. David Hansen, Legal Counsel. As per building code an elevator is required should the square footage of a press box be larger than 500 sq. ft. Our current press box is approximately 40' X 8' which is 320 sq. ft.. However, should only renovations be required without the addition of sq. footage the initial structural assessment will need to be considered. Furthermore, it is the responsibility of the structural engineer to make the decisions of what is currently within building codes and regulations even if it is only renovations. The possible recommendation of constructing adjacent press boxes may still require an elevator to be installed. The sq. footage requirement applies to the "aggregate" total sq. footage of all press boxes. Again, it will be the responsibility of the structural engineer to make that determination. Renovations to include floor support, the construction of an interior wall, counter tops, sliding windows.

At the February 05, 2014 Facilities Committee meeting, a presentation by Rick Hinojosa Structural Engineering stated that current plans to improve the press box must include the installation of an elevator or a ramp access to the press box as per the State of Texas current code. At this meeting the committee decided to cancel the press box renovation project.

At the Special Board of Trustees Meeting held on Wednesday, April 20, 2016, the Board approved the following:

Administration is again exploring the possibility of a stadium renovation to include a new press box, new reserve section seating with back rests, new concession stands, new concrete base under the bleachers along with new bleachers to meet current ADA rules and regulations. New bleachers to also include those at Leo Najo Baseball Park.

Administration is requesting approval to advertise for Request for Qualifications (RFQ's) for architectural/civil engineer services as the recommended process for the selection.

The ranking of Request for Qualifications responses must be on the basis of demonstrated competence, qualifications, capability to perform, the past performance of the firm and members of the firm, and other appropriate factors submitted by the firm in response to the request for qualifications, except that cost-related or price related evaluation factors are not permitted as provided by Section 2254.004, Government Code.

If approved, Administration will begin advertising for architects and then begin the process of reviewing the firms as per the RFQ's and schedule presentations for the Board to review and possibly select a firm.

Advertisements for Request for Qualifications (RFQ's) for architects were advertised in the local newspaper on Wednesday, June 1st and June 8th, 2016 along with being posted on the MCISD website. RFQ's were due at Central Office on Thursday, June 23, 2016 at 2:00 p.m...

Three (3) architectural firms submitted an RFQ and they were reviewed for completeness and adherence to the instructions of the request by Mr. Roosevelt Rios, Purchasing

Coordinator and Ms. Tammy Tijerina, Project Manager on Thursday, July 28, 2016. The firms are listed below:

PBK Architects GIGNAC &
Assoc.
Alvarado Architects

This agenda item and presentation(s) were originally scheduled for Wednesday, August 03, 2016, however, they were postponed for a later date and time.

At the Facilities/Environment Committee held on Wednesday, August 24, 2016, the three ranked firms were invited to make a presentation to a Special Facilities/Environment Committee meeting and those Board members in attendance. The Committee allowed the firms a 15-minute presentation session along with a 15-minute question and answer session. The Committee along with Mr. Ricardo Rivera evaluated and ranked the firms on the basis of demonstrated competence and qualifications pursuant to the Professional Services Procurement Act as per the presentations. The rankings were then presented at the Special Board of Trustees meeting for consideration and approval for the selection of services.

At the Special Board Meeting held on Wednesday, August 24, 2016, the Board approved the rankings and selection of Alvarado Architects for services for the Tom Landry Stadium Renovations Project.

At the Regular Board Meeting held on Wednesday, September 14, 2016, the Board approved the contract for Alvarado Architects for the Tom Landry Stadium Renovations Project.

At the Regular Board Meeting held on Wednesday, November 09, 2016, the Board approved the project and budget, the procurement method and Alvarado Architects request of Schematic Design and Design Development for the Tom Landry Stadium Renovations Project. Alvarado Architects, District Staff and Coaches have been working on the design due to the extremely tight timeline, this project has to be completed by late July 2017. Current design will have new concession stands, new parking, new parking over-lay where needed, concrete area below home side, new stadium fascia, new complete seating bleachers at both home and visitor side, home side reserved seating to have back rests, seating and ramps to be ADA compliant, new ticket booths, press box with elevator as recommended design, new stadium lighting as required along with other required items needed for the project.

At the Regular Board meeting held on Wednesday, December 14, 2016, the Board approved Alvarado & Associates final design and Approval for 24-inch-Wide Seats in the Reserved Section for the Tom Landry Stadium Renovations Project.

Advertisements in the local newspapers and at the Association of General Contractors Office (AGC) were posted on December 18, 2016 and December 25, 2016 for the new design. A pre-proposal meeting was held on Tuesday, January 10, 2017 at 2:00 P.M. at Central Office.

Proposals were publicly opened on Tuesday, January 17, 2017 at 4:00 P.M. at Central Office. Pre-ranking of the proposals were conducted by Mr. Roosevelt Rios, Mr. Albert Rodriguez and Mr. Adrian Hernandez, Project Manager on Tuesday, January 17 and Wednesday, January 18, 2017.

At the Facilities Committee meeting the Committee reviewed the pre-ranking of firms and then proceeded to officially rank the firm's proposals. These rankings will then be presented to the Board of Trustees for consideration and approval for entering into negotiations in the order of ranking recommended at a special called meeting on Monday, January 23, 2017 at 7:30 a.m.

Pre-ranking of proposals by Administration is merely a district process to pre-check if all requested documents and information in the Request for Proposals (RFP) was submitted prior to the Evaluation and Selection Committee formal evaluation. The pre-ranking of proposals is strictly unofficial. The Request for Proposal (RFP) package includes document CSP – 00350 Evaluation and Selection Criteria for Competitive Sealed Proposals which defines this portion of the procurement process. The District Evaluation and Selection Committee is comprised of three (3) Board of Trustees Facilities Committee Members and one (1) appointed Administration Staff. The Evaluation and Selection Committee will evaluate, rank and publish all proposals. The Evaluation and Selection criteria has been approved by the Mission C. I. S. D.'s Board. Once the M. C. I. S. D. Board of Trustees approves the ranking, the District Evaluation and Selection Committee will then proceed to negotiate a contract with the highest-ranking Proposer.

The Finance department in conjunction with the districts finance consultants have been designing a funding package for this project. In order to ensure this project under this funding source be securely financed Administration is recommending to adjust the contingency budget by an increase of \$2 million. Thus, the total construction budget to include all soft-costs will not exceed \$10 million.

Three proposals were submitted for this project and were ranked by the Facilities Committee as per MCISD guidelines and procedures. The Board must now consider the rankings and approve to enter into negotiations with the top ranked firms in the order selected. Rankings listed below:

<u>Company</u>	<u>Base Proposal</u>	<u>Alt. #1</u>	<u>Days</u>
Holchemont Const. (291)	\$7,463,000.00	(\$287,000.00)	235
E-Con Const. (287.6)	\$7,450,000.00	\$210,000.00	180
Central Builders (260.2)	\$8,000,000.00	\$500,000.00	180

Note:

Alternate #1 is for a larger custom-built press box of which Administration recommends approving. Both E-Con Construction and Central Builders have an additional cost for this alternate, as per Holchemont Construction their base bid includes the larger custom press box. Should MCISD select the smaller pre-fabricated press box Holchemont has a \$287,000.00 deduct from their base bid. The intention is for a notice to proceed (NTP) to be issued on or before February 01, 2017 with a substantial completion date of July 31, 2017, which is 180 days, Holchemont has a substantial completion date of September 24, 2017. Proposals and days are all prior to negotiations.

At a Special Board of Trustees meeting to be held on Monday, January 23, 2017, the Board will consider and possibly approve the rankings to allow negotiations to begin. It is Administrations intent to bring forward at the Regular Board of Trustees meeting to be held on Wednesday, January 25, 2017 an approval and recommendation for a best and final offer (BAFO) and to enter into contract with the selected general contractor. It is MCISD's construction procurement process to present all items for Facilities Committee discussion prior to presenting to the Board of Trustees for final approval.

At the Regular Board of Trustees meeting held on Wednesday, January 25, 2017, the board approved the best and final offer (BAFO) from Holchemont in the amount of \$7,463,000.00 with alternate #01 custom press box included as part of the contract. Notice to proceed (NTP) was issued on February 02, 2017 with a substantial completion date of August 21, 2017.

At the Regular Board of Trustees meeting held on Wednesday, April 12, 2017, the board approved and pulled the following items:

Consideration and Approval of AEA #01 for CPR #02 to Furnish and Install Sports Lighting for the Tom Landry Stadium Renovations Project.

Sports Lighting Allowance:	\$600,000.00 AEA #01
Sports Lighting:	<u>\$580,392.00</u>
Balance:	\$ 19,608.00

Consideration and Approval of AEA #02 for CPR #03 to Furnish and Install a Scoreboard Sound System for the Tom Landry Stadium Renovations Project. Item was pulled for further pricing on additional speakers throughout the stadium.

Consideration and Approval of AEA #03 for CPR #04 to Furnish and Install Football Safety Netting System for the Tom Landry Stadium Renovations Project. Item was pulled due to MCISD having the netting and poles and only required pricing for the installation.

Consideration and Approval of AEA #04R to "Credit" the Allowances for the Tom Landry Stadium Renovations Project. Item was pulled due to other items being pulled thus not being able to present an accurate balance total.

Consideration and Approval of CPR #06 to Change the Size of the Bronze Statue for the Tom Landry Stadium Renovations Project.

Bronze Statue Allowance:	\$ 50,000.00
CPR#06 Bronze Statue:	<u>\$129,400.00</u>
Bronze Statue Allowance Balance:	(\$ 79,400.00)

Due to inclement weather in the month of March Holchemont Construction requested additional delay days, thus, they presented Consideration and Approval of CPR #09 for Seven (7) Delay Days for the Tom Landry Stadium Renovations Project. The new substantial completion date is August 28, 2017.

Administration presented Consideration and Approval of Selection of Color and Pattern for the Reserved Seating on Home Side for the Tom Landry Stadium Renovations Project. The Board approved option #1 alternating colors.

At the Regular Board of Trustees meeting held on Wednesday, May 10, 2017, the Board approved and pulled the following items:

Contingency Allowance:	\$100,000.00
AEA #01 Sports Lighting:	\$ 19,608.00
CPR #6 Bronze Statue:	<u>\$ (79,400.00)</u>
Contingency Balance:	\$ 40,208.00

Consideration and Approval of AEA #03R for CPR #04 to Furnish and Install Football Safety Netting System for the Tom Landry Stadium Renovations Project.

Football Safety Net System Allowance:	\$10,000.00
AEA#03 Football Safety Net System:	<u>(\$ 7,500.00)</u>
Balance:	\$ 2,500.00

Consideration and Approval of CPR #08 to Construct a Riser Room / Fire Pump for the Tom Landry Stadium Renovations Project.

Fire Suppression Pump Allowance Balance:	\$ 50,000.00
CPR # 08 Riser Room:	<u>\$ 110,428.53</u>
Balance:	(\$ 60,428.53)

Contingency Balance:	\$40,208.00
CPR #8 Riser Room:	(\$60,428.53)
Plus, Overhead and Profit	<u>(\$2730.47)</u>
Contingency Balance:	(\$22,951.00)

Due to inclement weather in the month of April and MCISD testing Holchemont Construction requested additional delay days, thus, they presented Consideration and Approval of CPR #09 for Eight (8) Additional Delay Days for the Tom Landry Stadium Renovations Project. The new substantial completion date is September 05, 2017.

Note: The first scheduled football game is for Friday, September 01, 2017 with VMHS vs Harlingen. Substantial completion is granted when the facility can be utilized for its intended use. The City of Mission Fire Marshal must approve the facility to include all fire systems are inspected and tagged "approved" along with all ADA inspections and approvals and to include the inspection and approval of the elevator system and to include any other inspections required. Coaches are working on a Plan "B" should the stadium not be completed on time.

Administration recommended Consideration and Approval of Re-naming for the Tom Landry Stadium Renovations Project as "Tom Landry Hall of Fame Stadium".

Administration recommended Consideration and Approval of Selection of Color for Reserved Seating on Home Side for the Tom Landry Stadium Renovations Project.

Recommendation is based on the colors selected by Coach Detmer, Coach Gilpin, Athletic Director Joe Sanchez and Athletic Director Leticia Ibarra.

Royal Blue
Texas A&M – Maroon

After a lengthy discussion on possible color dis-coloration of the royal blue and maroon seats the Board approved “grey” for the reserved seating.

Alvarado Architects presented a “pose” selection on the statue. At the Facilities Committee meeting held on Wednesday, May 03, 2017, the Committee along with members of the Campus Construction Over-Sight Committee members reviewed and discussed the five (5) options of poses brought forward by Mr. Alvarado. By virtue of the discussion and by show of hands, options #1 and #4 were selected for presentation to the Board. The Board approved Consideration and Approval of Tom Landry Statue Pose for the Tom Landry Stadium Renovations Project Option #1.

At the Facilities/Environment Committee meeting held on Wednesday, June 07, 2017 several CPR’s were presented and discussed. These CPR’s may become change orders should current available allowances not cover the over-budget of the project when it is finalized. MCISD Administration stressed to Alvarado Architects and Holchemont Construction the discontent of change orders and requests for additional construction time. Administration stressed the importance of having the project completed as per the original substantial completion date.

At a Special Board of Trustees meeting held on Wednesday, June 07, 2017, the Board granted Superintendent Dr. Ricardo Lopez authority to approve change orders/change proposal request for the Tom Landry Stadium Renovations Project in the amount not to exceed a total of \$250,000.00. This action was to facilitate the change order/CPR process and not delay the general contractor waiting for a decision.

The following Change Orders/CPR’s were approved by Superintendent Dr. Ricardo Lopez on Wednesday, June 07, 2017:

Supt. Approval Balance:	\$250,000.00
CPR#05R Structural Steel:	\$ 31,824.00 CPR#06R
Bronze Statue Foundation:	\$ 12,161.00 CPR#11 for MEP
changes at the Press Box:	\$ 8,674.00 CPR#14 for HVAC at the Gift
Shop:	\$ 12,268.00 CPR#19 for Additional Gates for Eagle
Drive:	<u>\$ 1,816.00</u>
Supt. Approval Balance:	\$183,257.00

Consideration and Approval of CPR#05R for Structural Steel between Grandstands and Custom Press Box for the Tom Landry Stadium Renovations Project.

Contingency Balance:	(\$22,951.00)
Structural Steel Additions Cost:	<u>\$31,824.00</u>
Contingency Balance:	37 (\$54,775.00)

Consideration and Approval of CPR#06R for Bronze Statue Foundation and Base for the Tom Landry Stadium Renovations Project.

Contingency Balance:	(\$54,775.00)
Bronze Statue Base Foundation Cost:	<u>\$12,131.00</u>
Contingency Balance:	(\$66,906.00)

Consideration and Approval of CPR#11 for MEP changes at the Press Box for the Elevator for the Tom Landry Stadium Renovations Project. Holchemont, LTD is requesting eight (8) additional day, if approved, the new substantial completion date is September 13, 2017. As per Alvarado Architects additional days will not be submitted.

Contingency Balance:	(\$66,906.00)
Electrical at press box Cost:	<u>\$ 8,674.00</u>
Contingency Balance:	(\$75,580.00)

Consideration and Approval of CPR#14 for HVAC at the Gift Shop for the Tom Landry Stadium Renovations Project.

Contingency Balance:	(\$75,580.00)
HVAC at gift shop Cost:	<u>\$12,268.00</u>
Contingency Balance:	(\$87,848.00)

Consideration and Approval of CPR#19 for Additional Gates for Eagle Drive for the Tom Landry Stadium Renovations Project

Contingency Balance:	(\$87,848.00)
Gates at Eagle Drive Cost:	<u>\$ 1,816.00</u>
Contingency Balance:	(\$89,664.00)

At the Regular Board of Trustees meeting held on Wednesday, June 21, 2017, The Board did not approve Consideration and Approval of CPR#20 for Additional Four (4) Rain Days for the Month of May for the Tom Landry Stadium Renovations Project.

*Note: After meeting with Alvarado Architects and Holchemont LTD, they were advised that Administration will be questioning any further delay days submitted and that Holchemont should continue working on a recovery schedule plan to attempt to bring this project at the initial substantial completion date of August 21, 2017.

The following Change Orders/CPR's were approved by Superintendent Dr. Ricardo Lopez on Thursday, June 29, 2017 in order to have the project continue without contractor delays:

Supt. Approval Balance Granted:	\$183,257.00
CPR#12 Track Timing System:	<u>\$ 45,322.00</u>
Supt. Approval Balance:	\$137,935.00

Change Order Amount to Date:	(\$134,986.00)
------------------------------	----------------

Note: General Contractor has added 12% overhead and profit and 1.5% for project bonding on all change order amounts.

Soil Stabilization Allowance:	\$10,000.00
CPR #16 Soil Stabilization:	<u>\$10,000.00</u>
Balance:	\$ 0.00

Utility Allowance:	\$20,000.00
CPR #21 Boring & Trenching:	<u>\$16,830.00</u>
Balance:	\$3,170.00

At the Special Board of Trustees Meeting to be held on Thursday, July 27, 2017, Administration presented to the Board Consideration and Approval of CPR#15 for Graphics for the Tom Landry Stadium Renovations Project. This amount is to be taken from the graphics allowance already included in the original contract.

Graphics Allowance Balance:	\$100,000.00
Banner system:	(\$ 51,148.50)
Identification signage:	(\$ 26,815.00)
Bleacher section signage:	(\$ 13,625.00)
Traffic signage:	(\$ 2,136.00)
Fire lane striping:	<u>(\$ 3,700.00)</u>
Balance:	\$ 2,575.50

At the Regular Board of Trustees meeting held on Wednesday, August 09, 2017, the Board considered and approved some of the following items:

As per our Legal Counsel, the Board did not need to vote on agenda item, Consideration and Approval of Additional Seven (7) Delay Days for AEA#11 for CPR #21 for the Tom Landry Stadium Renovations Project which was previously denied but being brought forward by Holchemont, LTD. once again for consideration. The Board had stated it would possibly revisit this request and no action was taken.

Consideration and Approval of AEA#12 for CPR #22 for Landscaping and Irrigation for the Tom Landry Stadium Renovations Project.

Landscape/Irrigation Allowance:	\$20,000.00
CPR#22 Landscape & Irrigation:	<u>\$17,383.00</u>
Balance:	\$ 2,617.00

Consideration and Approval of AEA#13 for CPR #24 to Up-grade the Scoreboard System for the Tom Landry Stadium Renovations Project.

Scoreboard Sound System Allowance:	\$55,000.00
CPR#24 Scoreboard System:	<u>\$34,934.00</u>
Balance:	\$20,066.00

Consideration and Approval of CPR #23 for Speaker System for the Tom Landry Stadium Renovations Project. This agenda item³⁹ was pulled.

At the Regular Board of Trustees meeting held on Wednesday, September 13, 2017, the Board revisited and approved Consideration and Approval of Additional Seven (7) Delay Days for AEA#11 for CPR #21 for the Tom Landry Stadium Renovations Project. As of the date of this Board of Trustees meeting Holchemont LTD will be into possible liquidated damages as per contract of \$1,500.00 per day of not meeting the substantial completion date. Administration brought forward this request, the new substantial completion date is September 12, 2017.

At the Regular Board of Trustees meeting held on Wednesday, October 11, 2017, the Board took the following actions for the following items:

Consideration and Approval of CPR #12R3 for Additional Power for the Tom Landry Stadium Renovations Project. Please note that Holchemont, LTD will require and extra four (4) days. If approved, the new substantial completion date is September 16, 2017. This item was pulled until further review.

Note: MCISD does not agree with this pricing, however, there will be a cost associated with installing conduits within the concrete slab which was done earlier. If the revised pricing is not approved MCISD Maintenance will complete the electrical connections.

Contingency Balance:	(\$134,986.00)
CPR#12R3 for Additional Power:	<u>\$ 0.00</u> (Org. price \$10,134.42)
Change Order Amount to Date:	(\$134,986.00)

Consideration and Approval of CPR #12R5 for Additional Cabling for Track Timing System for the Tom Landry Stadium Renovations Project. Please note that Holchemont, LTD will require and extra fourteen (14) days. If approved, the new substantial completion date is September 30, 2017. This item was pulled until further review.

Contingency Balance:	(\$134,986.00)
CPR#12R5 Additional Cabling:	<u>\$ 0.00</u> (Org. price \$54,468.65)
Change Order Amount to Date:	(\$134,986.00)

Consideration and Approval of CPR #17 to "Credit" Two (2) Wireless Access Points, Shortel Phone and Video Server for the Tom Landry Stadium Renovations Project. This item was approved.

Contingency Balance:	(\$134,956.00)
CPR#17 "Credit" on Technology:	<u>\$ 5,000.00</u> "Credit"
Change Order Amount to Date:	(\$129,986.00)

Consideration and Approval of CPR #18 to "Credit" Fire Alarm and Intrusion Systems for the Tom Landry Stadium Renovations Project. This item was approved.

Contingency Balance: (\$129,986.00)
CPR#18 "Credit" Fire Alarm System: \$ 2,800.00 "Credit"
Change Order Amount to Date: (\$127,186.00)

Consideration and Approval of CPR #25 to Relocate Cross Bracing at Concession Stands for the Tom Landry Stadium Renovations Project. This item was approved with the cost change to \$5,221.00

Contingency Balance: (\$127,186.00)
CPR #25 to Relocate Cross Bracing: (\$ 5,221.00) (Org. price \$10,442.00) Change
Order Amount to Date: (\$132,407.00)

Consideration and Approval of CPR #26 to Remove and Replace Concrete from the Ramps for the Tom Landry Stadium Renovations Project. Please note that Holchemont, LTD will require and extra two (2) days. If approved, the new substantial completion date is October 2, 2017. This item was pulled, Javier Hinojosa Civil Engineer will take care of this item.

Contingency Balance: (\$132,407.00)
CPR #26 to Remove and Replace Concrete: \$ 0.00 (Org. price \$4,483.25)
Change Order Amount to Date: (\$132,407.00)

Consideration and Approval of CPR #27 to Add IDF Rack, Quad Receptacles and Data Drops on the Visitor's Side Bleachers for the Tom Landry Stadium Renovations Project. Please note that Holchemont, LTD will require and extra three (3) days. If approved, the new substantial completion date is October 5, 2017. This item was pulled, MCISD will take care of this item.

Contingency Balance: (\$132,407.00)
CPR #27 to Add IDF Rack: \$ 0.00 (Org. price \$18,357.49)
Change Order Amount to Date (\$132,407.00)

Consideration and Approval of CPR #29 for Additional Eleven (11) Delay Days for the Tom Landry Stadium Renovations Project. If approved, the new substantial completion date is October 16, 2017 pending all other CPR's being submitted. The Board took no action on this item.

Consideration and Approval to Grant Administration Authority to Approve Substantial Completion for the Tom Landry Stadium Renovations Project. Dr. Lopez, Superintendent will have the authorization. This item was approved.

Note: No additional delay days were approved at this meeting. Substantial completion continues to be approximately September 12, 2017.

At the Regular Board of Trustees meeting held on Wednesday, November 08, 2017, the Board took the following actions for the following items:

Consideration and Approval of CCD#01 for CPR#30 for Modifications to the Elevator Equipment Room for the Tom Landry Stadium Renovations Project. No additional days were approved.

Contingency Balance:	(\$132,407.00)
CCD#01/CPR#30 Elevator Equipment Room:	<u>\$ 3,957.00</u>
Change Order Amount to Date	(\$136,364.00)

Consideration and Approval of CPR#31 to "Credit" for Use of Owners Utilities for the Tom Landry Stadium Renovations Project. MCISD presented a "credit" for \$5,900.00, however, Holchemont offered only a credit amount of \$900.00.

Contingency Balance:	(\$136,364.00)
CPR#31 Use of Owners utilities:	<u>\$ 5,900.00 "Credit"</u>
Change Order Amount to Date:	(\$130,464.00)

Consideration and Approval of CPR#32 for HVAC Test and Balance for the Tom Landry Stadium Renovations Project.

Test and Balance Allowance:	\$5,000.00
CPR#32 HVAC Test & Balance:	<u>\$2,500.00</u>
Balance:	\$2,500.00

Consideration and Approval of CPR#33 for Two (2) Additional Fire Extinguishers for the Tom Landry Stadium Renovations Project.

Contingency Balance:	(\$130,464.00)
CPR#33 Fire Extinguishers:	<u>\$ 268.00</u>
Change Order Amount to Date	(\$130,732.00)

At the Regular Board of Trustees meeting held on Wednesday, December 13, 2017, the Board took the following actions for the following items:

Consideration and Approval of CPR #12R3 for Additional Power for the Tom Landry Stadium Renovations Project. This item was approved.

Contingency Balance:	(\$130,732.00)
CPR#12R3 additional power:	<u>\$ 6,327.00</u>
Balance:	(\$137,059.00)

Consideration and Approval of CPR#34 for "Credit" for the VIP Chair Allowance for the Tom Landry Stadium Renovations Project. VIP Chair Allowance "Credit" is \$5000.00. This item was approved.

Discussion and Possible Action on Paving Repair Schedule for the Tom Landry Stadium Renovations Project.

Consideration and Approval for Final Completion, Less Betterment Fund Allowance and Final Payment, Less Liquidated Damages for the Tom Landry Stadium Renovations Project. This item was pulled due to punch list items and other contractual obligations were noncompliance.

At the Regular Board of Trustees meeting held on Wednesday, April 11, 2018 the Board took the following actions for the following items:

Consideration and Approval of CPR#23 for Sound System Raceways for the Tom Landry Stadium Renovations Project. Holchemont LTD is requesting fourteen (14) additional delay days for this work, if approved the new substantial completion date is September 26, 2017.

Contingency Balance:	(\$137,059.00)
CPR#23 for Sound System:	<u>\$ 39,839.37</u>
Balance:	(\$176,898.37)

Consideration and Approval of Grievance Agreement for Use of Owners Utilities for the Tom Landry Stadium Renovations Project. As per the November approved CPR #31, MCISD approved an owner's credit for utility use of \$5,900.00. As per grievance agreement the amount was reduced to \$2,350.00, thus an adjustment needed to be made.

Previous: \$5,900.00
Final approved as per Grievance: \$2,350.00
Adjustment: \$3,550.00

Contingency Balance:	(\$180,448.37)
----------------------	----------------

Discussion and Possible Legal Action Regarding Parking Lot Repairs for the Tom Landry Stadium Renovations Project. At this time the Board invoked the "Self Help Provision" of the contract authorizing Administration to make necessary parking lot repairs utilizing a different contractor.

2GS and Earthworks re-paving Cost: \$24,700.00 - Parking Lot Re-paving completion date was achieved on August 06, 2018.

At the Regular Board of Trustees meeting held on Wednesday, May 08, 2019, the Board took no action on the following item: Consideration and Approval for Final Completion, Less Betterment Fund Allowance and Final Payment, Less Liquidated Damages for the Tom Landry Stadium Renovations Project. At this meeting Administration also recommended to authorize Administration and Dr. Perez to approve final completion at a later time, this was rejected with direction from the Board that they wanted this brought forward when the time came for consideration and approval.

At the Regular Board of Trustees meeting held on Tuesday, June 11, 2019 the Board took the following actions

Administration, Mr. Eli Alvarado, Architect, and Mr. Michael Montalvo, General Contractor have met six times since April 25, 2019 with the latest meeting held on Tuesday, June 04,

2019, to discuss what is required from all parties to bring this project for final recommendation and to possibly come to a mutual agreement and present to the Board of Trustees Consideration and Approval for Final Completion, Less Betterment Fund Allowance and Final Payment, Less Liquidated Damages for the Tom Landry Stadium Renovations Project. At the latest meeting Mr. Montalvo was not able to attend and for many of these meetings Dr. Perez, Superintendent was present. A 1 ½ year warranty project walk-through was conducted as per contract specifications on Friday, May 03, 2019 with Mr. Alvarado, his design staff, Mr. Montalvo, his sub-contractors and MCISD personnel present to identify any warranty items that are still pending and need correction. The meetings that are being conducted are to balance and agree on all financial/accounting matters and pending correction of work if applicable. Any matters that concern additional request for time or matters that may concern any deduction from the remaining balance owed to the contractor such as additional fees/costs or possible liquidated damages incurred the general contractor will need to follow the process as written in his contract.

As noted, Administration and Alvarado Architects believes it has tried, with due diligence, to work on all pending accounting/fiscal matters with Mr. Montalvo, however, we continue to not agree on a mutual amount. Administration presents Discussion with Legal Counsel Regarding Closeout for the Tom Landry Stadium Renovations Project with MCISD processing any possible pay applications to Holchemont Construction with monies being withheld that are not in contention.

Note: Additional structural assessment is continuing by Rick Hinojosa, Structural Engineering and is pending completion. They are pending additional concrete test results.

Tom Landry Stadium Project Timeline:

Notice to Proceed (NTP) – 02/01/2017
Original Substantial Completion Date – 08/21/2017
36 delay days Board approved due to testing, weather, change orders
New substantial completion date – 09/26/2017
Approved substantial completion date – 11/10/2017 (45 days late)
Original Final Completion Date – 12/10/2017
New Final Completion Due Date – 04/20/2018 (131 days late)

Possible LD's for not meeting Subst. Completion: 45 days X \$1,500.00 = \$67,500.00
Possible LD's for not meeting Final Completion: 131 days X \$500.00 = \$65,500.00
Possible LD's for delay in re-paving of parking lot: 7 days x\$500.00 per day = \$3,500.00

Possible LD's Incurred: \$136,500.00

Other Possible Fees/Costs:

Re-paving of parking lot = \$24,700.00
Structural Engineering cursory inspection = \$5,000.00 (Rick Hinojosa, Structural Engineering)
Hinojosa full structural assessment = \$30,000.00 (if applicable)
TDLR re-inspections = \$285.00

Terracon Structural additional services = \$15,000.00
Pending "credit" for three (3) parking lot poles not installed = \$53,489.08

Approximate Possible Total Amount of addtl. fees/costs: \$128,474.08

Additional Architect Fees: \$85,695.00 (if applicable/pending)

Balance on contract:	\$416,406.11	
Possible LD's:	\$136,500.00	Possible
addtl. Costs:	\$128,474.08	
Possible addtl. Arch. Fees:	\$ 85,695.00	
Paid Holchemont:	\$ 43,189.25	(07/24/19 Pay App. #10 rev.3)

Est. Current Balance on Contract: ~~\$380,251.23~~ as of 04/21/2021 \$347,206.23

Est. Construction Costs:	\$6,000,000.00
Est. Total Construction w/Soft Costs:	\$8,000,000.00

BAFO Const. Cost:	\$7,463,000.00
Change Orders:	<u>\$ 142,020.37</u>
Final Const. Cost:	\$7,605,020.37

Architect Fees:	\$485,095.00	6.5% of Construction Cost
Addtl. Arch. Fees for C/O's:	<u>\$9,231.32</u>	
Architect Fees:	\$494,326.32	(excluding addtl. Fees pending)

At the Regular Board of Trustees meeting held on Wednesday, August 14, 2019 the Board took the following actions.

At this meeting the Mr. Rick Hinojosa Structural Engineering Assessment report was not available for the Board of Trustees to review, however, Administration had preliminary verbal discussions with Hinojosa on what he was to submit, the report was to be finalized on Friday, August 16, 2019. Should the report state that repairs were required Administration presented Consideration and Possible Action Regarding Procurement of Design and Construction Services for the Tom Landry Stadium Repairs in advance.

After conducting field reviews and inspections Mission CISD contracted with Rick Hinojosa Structural Engineering to conduct a third party Visual Cursory Observation on the bleachers for the visitor's side of Tom Landry Stadium. On September 06, 2018 the observation report with conclusions and recommendations was submitted. In brief, Hinojosa stated that the cracked piers did not affect the immediate load carrying capacity of the structure and the stadium could be used. However, the recommendations were to conduct a complete assessment of all piers and repair all necessary items addressed in the complete assessment.

Administration was approved to contract with Hinojosa to conduct a full stadium assessment to include not only concrete piers but to inspect the entire structure of the

stadium. On August 08, 2019, Hinojosa Engineering submitted a preliminary assessment letter for our review noting possible reinforcement required.

On August 16, 2019, Hinojosa Structural Engineering submitted their Visual Structural Condition Assessment of Tom Landry Stadium for our review.

At the September 11, 2019 Regular Board of Trustees meeting and based on Mr. Hinojosa's report, Administration presented Consideration and Approval of Design and Construction Services for the Tom Landry Stadium Repairs.

The Board of Trustees must take the necessary action in accordance with Texas Education Code 44.035 which consisted of the selection/designation of an architect and/or engineer to prepare construction documents for this project. The engineer and/or architect selected or designated will have full responsibility for complying with the Texas Engineering Practice Act (Article 3271a, Vernon's Texas Civil Statutes) or Chapter 478, Acts of the 45th Legislature, Regular Session, 1937 (Article 249a, Vernon's Texas Civil Statutes) as applicable.

If the engineer or architect is not a full-time employee of the District, the Board must select the engineer or architect on the basis of demonstrated competence and qualifications as provided by Section 2254.004, Government Code. The selected architect/engineer along with preparing construction documents will be required to provide MCISD with an estimated project budget.

Current and/or past structural engineers that have worked with MCISD are listed below, the Board of Trustees may select from one of these engineers on the basis of demonstrated competence and qualifications or may direct Administration to seek for Request for Qualifications (RFQ's) on an engineer or architect.

Rick Hinojosa Structural Engineering (conducted assessments)
Chanin Structural Engineering (original project structural engineer)

The Board of Trustees selected Mr. Rick Hinojosa Structural Engineering to conduct a thorough third-party structural assessment of the Tom Landry Stadium Project.

On or about January 27, 2020, Mr. Hinojosa submitted to Administration a proposal for forensic engineering services from MEG Engineers. The Forensic Engineering Services will include Ground Penetrating Radar (GPR) Scans of one-hundred and fifty-six (156) piers by scanning four (4) grids at each pier location. A grid will consist of a three (3) foot by two (2) foot rectangle made up of thirty-five (35) gridlines spaced at six (6) inches on center. Total linear footage of scanning will be eighteen thousand and ninety-six (18,096) feet. The report will include detailed rebar locations of the piers. The proposal cost for this service was \$56,000.00.

At the Facilities/Environment Committee Meeting of February 05, 2020 this proposal and engineering service was presented and discussed. At this time the decision was made for Administration to proceed with Hinojosa Structural Engineering and MEG Engineers to conduct only seventy-eight (78) GPR Scans on the stadium. These scans would be divided between the home and visitors side piers at a proposal cost of \$34,988.00.

At the Regular Board of Trustees meeting held on April 08, 2020 the Board approved the following, Preliminary reports from both engineering firms indicate that a complete GPR Scan of all piers would be advisable to have a complete pier assessment on the stadium. Thus, Administration recommends Consideration and Approval of Additional Ground Penetrating Radar (GPR) Scans for Piers at the Tom Landry Stadium Bleacher Project. The estimated proposal cost would be the difference from the original proposal to what has been approved for the first phase. Estimated proposal \$21,012.00.

At the Regular Board of Trustees meeting held on September 09, 2020, as an informational Board Item, a presentation was given by Rick Hinojosa Structural Engineering, Mr. Albert Trevino, on the Tom Landry Stadium Renovation Project status. Mr. Trevino reported on the findings for the GPR scans conducted and has stated, "the scans in the report indicate that the majority of the piers do not have pier reinforcement per the shop/erection drawings provided by Sturdy Steel who provided the bleachers".

At the meeting of September 09, 2020, Hinojosa Structural Engineering was to provide a final and complete comprehensive report on the findings and recommendations for correction on all items indicated on the assessment. Findings and recommendations were to include and not limited to the disciplines of Structural, Mechanical, Electrical, Plumbing (MEP) and Civil. At this meeting Hinojosa Structural Engineering was directed to provide this comprehensive report and not only the GPR scans report.

Since this initial directive, Hinojosa Structural Engineering has been contacted both on October and December 2020 for the final report and we continue to have no response. Administration will continue to utilize all avenues to request the final report so that we may move forward with repairs required.

On January 14, 2021, Rick Hinojosa Structural Engineering was sent both an email correspondence and a certified letter requesting his personal appearance at the Wednesday, January 20, 2021 Board of Trustees Work Shop to present the final project findings. At 4:01 p.m. on that day Mr. Hinojosa contacted us that he had a family emergency and would try to attend. With this correspondence he attached "Mission CISD Tom Landry Stadium Ground Penetration Radar (GPR) Scanning Findings Letter". This letter referenced the GPR scanning done at the stadium.

In discussion at the Work Shop of January 14, 2021, the Board instructed our legal counsel to draft a letter to request Mr. Hinojosa's presence and to once again present his findings at the Board Work Shop of Wednesday, February 03, 2021. Legal counsel sent a certified letter and emailed the letter to Mr. Hinojosa's attention on Tuesday, January 26, 2021. My office then proceeded to re-send this letter to Mr. Hinojosa the following day. A "read receipt" message was received from his office on Friday, January 29, 2021 at approximately 12:10 p.m. acknowledging receipt of our request to be present.

At this Work Shop of Wednesday, February 03, 2021, the Board will hear the presentation and may have a question and answer session with Mr. Hinojosa on the findings and recommendations. At this time the Work Shop may have a Discussion and Possible Action to Procure Engineering Services for Analysis and Remediation for the Tom Landry Stadium Project and to Grant Administration Authorization to Procure Services. The

presentation was not held at the Work Shop and was presented at a Special Board of Trustees Meeting after.

At the Special Board of Trustees meeting of Wednesday, February 03, 2021, Mr. Rick Hinojosa presented his "Mission CISD Tom Landry Structural Comprehensive Assessment Report". After discussion with the Board of Trustees and Administration, Mr. Hinojosa was directed to once again present at the Regular Board of Trustees meeting of Wednesday, February 10, 2021. This presentation is to mainly address all the viable options on how to correct the issue of the piers found to be not safe and not constructed as per code as noted in the report and reported by Mr. Hinojosa at the meeting. He is to also present a scope of work and a phasing plan of repairs beginning with the most safety critical items. What will also need to be addressed is if any other areas will be damaged while repairing the piers, such as the flatwork. Each option(s) will need to satisfy all building and structural codes along with satisfying all safety compliance codes. At this meeting Mr. Hinojosa was advised that time was critical for the usage of the stadium since graduation ceremonies have already been scheduled. Mr. Hinojosa stated that plans and specifications should be finalized soon and we may be able to advertise for competitive sealed proposals (CSP's) within the next couple of weeks and possibly have a contractor begin repairs as quickly as the procurement process allows, that is the goal.

The procurement process will be Competitive Sealed Proposals (CSP's) of which the Board adopted as the method of delivery. The Board approved the Hidalgo County Prevailing Wage Rate of which is an exhibit and was attached. The Board also adopted the selection criteria of which proposals are evaluated and ranked. Administration also recommended that the Board authorized the Superintendent to rank the proposals and to negotiate an agreement with the highest ranked contractor.

On February 10, 2021, the Board approved Consideration and Possible Action Regarding Permanent and Emergency Repairs for the Tom Landry Stadium to Include the Wage Rate, Selection Criteria, and Authorization to Dr. Perez as mentioned under the Administrative considerations.

Advertisements in the local newspapers for Competitive Sealed Proposals (CSP's) were posted on March 24, 2021 and March 31, 2021. Proposals were to be opened April 08, 2021 and firms would be able to view remotely. The virtual pre-proposal meeting was Thursday, April 01, 2021 at 2:00 p.m. to allow all prospective contractors the opportunity to ask questions concerning the project plans and specifications.

CSP's were to be submitted on April 8, 2021, and were to be reviewed and ranked by the Administration Committee. This Administrative review was to be presented at the Regular Board of Trustees Meeting of Wednesday, April 14, 2021.

On Wednesday, April 06, 2021 Hinojosa Structural Engineering submitted a recommendation to extend the bid date by two weeks to allow contractors and sub-contractors more time to bid on the project. He also stated that a second pre-bid conference be held followed by a walk-through of the stadium facility. This recommendation was due also to no contractors attending the initial pre-bid conference. This recommendation was presented at the Board of Trustees Work Shop on Wednesday, April 08, 2021.

A second pre-proposal meeting was held on Thursday, April 15, 2021. With the two-week extension proposals were due and publicly opened on Thursday, April 22, 2021 at 2:00 p.m. at the Central Office Board Room. Proposals were reviewed, evaluated and ranked on Monday, April 26, 2021 at 2:00 p.m. by Ms. Rimalda Ruiz, Ms. Dora Garcia, Ms. Lorena Garcia, Mr. Joel Garcia and Mr. Ricardo Rivera with Ms. Daisy Cuevas assisting.

Due to the timeline to begin permanent repairs Administration requested a Special Board of Trustees meeting on Tuesday, April 27, 2021 at 12:00 p.m. at the Central Office Board Room. At this meeting Administration presented and the Board approved Consideration and Approval to Accept Administrations Rankings and Enter Into Negotiations in the Order of Ranking for the Tom Landry Stadium Repairs Project.

G & G Construction

Base Bid: \$1,024,850.00 with 210 construction days

Alternate Bird Screen: \$127,000.00 with an additional 45 construction days

TOTAL: \$1,151,850.00 with 255 days from notice to proceed (approx. 8.5 months)

Terra Fuerte Const.

Base Bid: \$1,141,000.00 with 180 construction days

Alternate Bird Screen: \$30,000.00 with an additional 30 construction days

TOTAL: \$1,171,000.00 with 210 days from notice to proceed (approx. 7 months)

Project negotiations were scheduled for Wednesday, May 05, 2021 at 10:00 a.m. as per G & G Constructions earliest available meeting date and time. Administration presented Consideration and Approval to Accept the Best and Final Offer (BAFO) and to Enter Into Contract for the Tom Landry Stadium Repairs Project and requested for a Special Board of Trustees meeting following the Board Work Shop to consider action on this item.

The Board of Trustees has the option to accept this BAFO, the initial base proposal, to decline the offer and direct Administration to enter into negotiations with the next contractor or to reject all offers and re-advertise for the project using the same specifications and design or direct the engineer to re-design the project.

At the Special Board meeting held on May 5, 2021, the Board approved G & G Contractors Best and final offer Base Bid: \$1,024,850.00 with 210 construction days. Notice to proceed was effective July 28, 2021, with substantial completion will be February 23, 2022.

At the Regular Board meeting held on November 10, 2021, the Board approved the following items:

Consideration and Approval of Allowance Expenditure Authorization (AEA) #01 for Structural Repairs on Various Piers for the Tom Landry Stadium Repairs.

Contingency Allowance:	\$20,000.00
AEA #1 Various Piers:	<u>\$ 8,241.88</u>
Balance:	\$11,758.12

Consideration and Approval of Change Order #1 for Forty-four (44) Delay Days due to the structural repairs on various piers for the Tom Landry Stadium Repairs. If approved the new substantial completion will be April 08, 2022.

On Friday, December 10, 2021 a letter was sent by MCISD to Mr. Rick Hinojosa, Hinojosa Structural Engineering and to Mr. Rene Garza, RG Enterprises LLC. referencing the Tom Landry Stadium Repair Project.

At the request of Mr. Garza, a project meeting was held on Wednesday morning, December 15, 2021 to discuss items referenced in the letter. Present at the meeting were staff members of R. Hinojosa Structural Engineering, Raba Kistner, Geo-tech Testing, G&G Const. and MCISD Staff.

At the Regular Board of Trustees meeting held on December 15, 2021, Mr. Albert Trevino. Hinojosa Structural Engineering and Mr. Rene Garza, RG Enterprises LLC presented an update on the project. During the presentation at least five (5) possible change orders which consist of additional costs and time were mentioned as forthcoming.

The Board expressed concern that the project needed to move forward and that requests for special meetings would be acceptable in order to expedite change orders needed as to not delay the project further.

A Special Board of Trustees Meeting has been requested for Wednesday, January 05, 2022 for Consideration and Approval of Change Order(s) for the Tom Landry Stadium Repairs Project.

At the Regular Board of Trustees meeting of December 15, 2021, both firms were instructed to work on change proposals to be submitted at the special called meeting of Wednesday, January 5, 2022. During the presentation by both Mr. Albert Trevino – Hinojosa Structural Engineering and Mr. Rene Garza – RG Enterprises, LLC they presented seven (7) possible construction proposal requests (CPR's). They were directed to present to the Administration and Board of Trustees detailed explanations for each CPR on why these were required, if by Code or other reasons. They were also directed to ensure that these CPR costs were the only option(s). It was also directed that they needed to specify if any of the CPR's would either delete or offset any of the work already included in their original scope of work and that the adjustment of all time and materials associated needed to be reflected as a "credit" to the district. As per Mr. Trevino, he would only inform the Administration and the Board of receipt of these CPR's and at this time would not formally present them for consideration since he had not yet reviewed them with RG Enterprises, LLC and did have some questions for them. Both firms were made aware that legally the project could not exceed 25% of the total cost of the project in change orders. Administration and the Board once again reiterated the need to resume work at the stadium and were very receptive to having meetings to review and possibly approve items to have the project progress. The Board asked which CPR's were critical at this time so that the project would continue and items #3, #5 and #6 that were presented that evening were noted. Both firms were directed to work on submitting these CPR's using the required AIA Document G701 - 2017 which specifically is designed to submit change

orders to the project and present them at a Special Board of Trustees meeting on Wednesday, January 12, 2022.

At the Special Board of Trustees meeting held on Wednesday, January 12, 2022, R. Hinojosa Structural Engineering and RG Enterprises, LLC presented possible change orders #2, #3 and #4. Change order #4 was the combination of Change Proposal Requests (CPR's) #5 and #6 that were presented at the previous meeting of January 05, 2022. Along with cost information were additional days requested. In consultation with Mr. David Hansen - Legal Counsel it was asked that the change orders be reviewed once again and that the costs and days all be incorporated into one single change order document. The change order was to be sent to our legal office to be incorporated into our required change order document. Both firms were asked to create a work schedule separating time from the home side versus the visitor side. A presentation is scheduled to be made once again at the Regular Board of Trustees meeting on Wednesday, January 19, 2022.

At the Regular Board of Trustees meeting held on Wednesday, January 19, 2022, R. Hinojosa Structural Engineering and RG Enterprises, LLC once again presented possible costs and change orders with a substantial completion date of early November 2022. This item was taken into Executive Session for consultation with our legal counsel.

After consultation and review, the decision and directive to both R. Hinojosa and RG Enterprises was to split the project between the home side repairs and the visitor repairs. Each side was to be a separate project with RG Enterprises submitting a change order for credit to work being separated from the visitor side and an updated schedule of values for completing the home side as this was the priority. A brief meeting was held after the Board of Trustees meeting with the design team, the general contractor, and MCISD staff to ensure that they understood the directive issued, of which they acknowledged that they understood. The directive was to have the change order with new updated costs, credits and timeline by the regularly scheduled Board Workshop on Wednesday, February 02, 2022.

ADMINISTRATIVE CONSIDERATIONS

Correspondences continued this past week with uncertainty from RG Enterprises about what was required and expecting a written authorization from Dr. Perez, MCISD Superintendent concerning what was directed at the previous Board meeting. A Zoom meeting was held on Thursday, January 27, 2022 with R. Hinojosa Staff, Mr. Manuel Leal, G & G Construction Superintendent, Mr. Adrian Hernandez, Mr. Adan Rivera, Ms. Lorena Garcia, and Mr. Rick Rivera to clarify the directive and expectations and the urgency for submitting the required change orders. It was presented that there would be no written authorization from Dr. Perez and that the directive issued at the Board meeting would suffice. It was also discussed that the general contractor was directed in an email by R. Hinojosa and Mr. Adrian Hernandez of what was required, Mr. Leal acknowledged the direction. A Zoom meeting was once again scheduled for Friday, January 28, 2022 to review the status of the change order. Once again both the general contractor and design team were directed to submit all change orders in a timely manner and not at the last minute when Administration does not have time to review before the presentations to Dr. Perez and the Board of Trustees. It was also noted that for all meetings we needed to have either Mr. Adrian Hernandez or ⁵Mr. Adan Rivera present.

FUNDING SOURCE

General Funds and Possible other funding sources to be determined by the Finance Dept. (TBD)

RECOMMENDATION

Administration presents Consideration and Approval of Change Order(s) for the Tom Landry Stadium Repairs Project – Ricardo Hinojosa Structural Engineering & G& G Contracting.

EXHIBIT

Change Order(s) Pending – (to be distributed at the meeting)

CONTACT PERSONS

Ricardo Rivera, Assistant Superintendent for Operations

Adrian Hernandez, Coordinator for Project & Energy Management

SUBJECT: Consideration and Approval of Project and Proposed Budget for Supplemental Repairs (Visitors Side) for the Tom Landry Stadium Project

PRESENTER: Ricardo Rivera
Assistant Superintendent for Operations

BACKGROUND INFORMATION

STADIUM:

Tom Landry Stadium was built in approximately 1976 and additional seating was installed in approximately 1989. It currently has only four (4) handicap seating spaces on both the home and visitors' side. The home side has a seating capacity for 5000 persons and the visitor's side has a seating capacity for 4000 persons.

At the Regular Board of Trustees meeting held on Wednesday, August 11, 2010 the Board approved a structural assessment to be conducted by Rick Hinojosa Structural Engineering. A report was completed on August 27, 2010. No further action was taken.

At a football game on September 26, 2013 and at the Regular Board of Trustees meeting of Wednesday, October 09, 2013, a concerned citizen brought to attention the fact that Tom Landry Stadium was not in compliance with the American Disabilities Act (ADA) current code concerning the required handicap seating spaces. As per ADA the breakdown for seating is 6 spaces for 1 – 500 seats then 1 seat for every 150 additional seats. As per calculations required additional seating on the home side will be 36 ADA seats and, on the visitors, side will be an additional 30.

On October 08, 2013 I contacted Mr. Tim Petty, Program Specialist V with the Texas Education Agency (TEA) to discuss this issue and he confirmed that we were not in compliance with current codes and standards concerning stadium seating.

At the Regular Board of Trustees meeting held on Wednesday, December 11, 2013 and after consultation with our legal counsel, the Board approved for renovations to the Tom Landry Stadium Press Box and for the additional required ADA stadium seating.

The current press box is approximately 30 years old and has never been renovated. When new bleacher seating was installed the press was moved by crane to its current location. With the installation of a new scoreboard additional staff will need to be placed in the press box to operate the system. Currently approximately nine persons are in the box, however, it is now estimated that up to twenty-two persons may be in the box at any given time. This added weight along with the additional weight of chairs and equipment may cause a stress on the structure. As per our legal counsel, there is no legal law that states that the structure needs to be evaluated, however, for safety precautions Administration is considering a structural assessment study to be conducted on the press box to ensure that the structure is capable of sustaining the additional weight.

At the Regular Board of Trustees meeting held on Wednesday, March 20, 2013 Administration presented and the Board approved Consideration and Approval to Contract with Rick Hinojosa Engineering for a Re-Assessment of the Tom Landry Stadium Press Box.

At the Regular Board of Trustees meeting held on Wednesday, April 10, 2013 the Board was advised that due to concerns and possible code regulations requiring an elevator to be installed for the press box, inquiries were made to Mr. David Hansen, Legal Counsel. As per building code an elevator is required should the square footage of a press box be larger than 500 sq. ft. Our current press box is approximately 40' X 8' which is 320 sq. ft.. However, should only renovations be required without the addition of sq. footage the initial structural assessment will need to be considered. Furthermore, it is the responsibility of the structural engineer to make the decisions of what is currently within building codes and regulations even if it is only renovations. The possible recommendation of constructing adjacent press boxes may still require an elevator to be installed. The sq. footage requirement applies to the "aggregate" total sq. footage of all press boxes. Again, it will be the responsibility of the structural engineer to make that determination. Renovations to include floor support, the construction of an interior wall, counter tops, sliding windows.

At the February 05, 2014 Facilities Committee meeting, a presentation by Rick Hinojosa Structural Engineering stated that current plans to improve the press box must include the installation of an elevator or a ramp access to the press box as per the State of Texas current code. At this meeting the committee decided to cancel the press box renovation project.

At the Special Board of Trustees Meeting held on Wednesday, April 20, 2016, the Board approved the following:

Administration is again exploring the possibility of a stadium renovation to include a new press box, new reserve section seating with back rests, new concession stands, new concrete base under the bleachers along with new bleachers to meet current ADA rules and regulations. New bleachers to also include those at Leo Najo Baseball Park.

Administration is requesting approval to advertise for Request for Qualifications (RFQ's) for architectural/civil engineer services as the recommended process for the selection.

The ranking of Request for Qualifications responses must be on the basis of demonstrated competence, qualifications, capability to perform, the past performance of the firm and members of the firm, and other appropriate factors submitted by the firm in response to the request for qualifications, except that cost-related or price related evaluation factors are not permitted as provided by Section 2254.004, Government Code.

If approved, Administration will begin advertising for architects and then begin the process of reviewing the firms as per the RFQ's and schedule presentations for the Board to review and possibly select a firm.

Advertisements for Request for Qualifications (RFQ's) for architects were advertised in the local newspaper on Wednesday, June 1st and June 8th, 2016 along with being posted on the MCISD website. RFQ's were due at Central Office on Thursday, June 23, 2016 at 2:00 p.m...

Three (3) architectural firms submitted an RFQ and they were reviewed for completeness and adherence to the instructions of the request by Mr. Roosevelt Rios, Purchasing Coordinator and Ms. Tammy Tijerina, ⁵⁴Project Manager on Thursday, July 28, 2016. The firms are listed below:

PBK Architects GIGNAC & Assoc.
Alvarado Architects

This agenda item and presentation(s) were originally scheduled for Wednesday, August 03, 2016, however, they were postponed for a later date and time.

At the Facilities/Environment Committee held on Wednesday, August 24, 2016, the three ranked firms were invited to make a presentation to a Special Facilities/Environment Committee meeting and those Board members in attendance. The Committee allowed the firms a 15-minute presentation session along with a 15-minute question and answer session. The Committee along with Mr. Ricardo Rivera evaluated and ranked the firms on the basis of demonstrated competence and qualifications pursuant to the Professional Services Procurement Act as per the presentations. The rankings were then presented at the Special Board of Trustees meeting for consideration and approval for the selection of services.

At the Special Board Meeting held on Wednesday, August 24, 2016, the Board approved the rankings and selection of Alvarado Architects for services for the Tom Landry Stadium Renovations Project.

At the Regular Board Meeting held on Wednesday, September 14, 2016, the Board approved the contract for Alvarado Architects for the Tom Landry Stadium Renovations Project.

At the Regular Board Meeting held on Wednesday, November 09, 2016, the Board approved the project and budget, the procurement method and Alvarado Architects request of Schematic Design and Design Development for the Tom Landry Stadium Renovations Project. Alvarado Architects, District Staff and Coaches have been working on the design due to the extremely tight timeline, this project has to be completed by late July 2017. Current design will have new concession stands, new parking, new parking over-lay where needed, concrete area below home side, new stadium fascia, new complete seating bleachers at both home and visitor side, home side reserved seating to have back rests, seating and ramps to be ADA compliant, new ticket booths, press box with elevator as recommended design, new stadium lighting as required along with other required items needed for the project.

At the Regular Board meeting held on Wednesday, December 14, 2016, the Board approved Alvarado & Associates final design and Approval for 24-inch-Wide Seats in the Reserved Section for the Tom Landry Stadium Renovations Project.

Advertisements in the local newspapers and at the Association of General Contractors Office (AGC) were posted on December 18, 2016 and December 25, 2016 for the new design. A pre-proposal meeting was held on Tuesday, January 10, 2017 at 2:00 P.M. at Central Office.

Proposals were publicly opened on Tuesday, January 17, 2017 at 4:00 P.M. at Central Office. Pre-ranking of the proposals were conducted by Mr. Roosevelt Rios, Mr. Albert Rodriguez and Mr. Adrian Hernandez, Project Manager on Tuesday, January 17 and Wednesday, January 18, 2017.

At the Facilities Committee meeting the Committee reviewed the pre-ranking of firms and then proceeded to officially rank the firm's proposals. These rankings will then be presented to the Board of Trustees for consideration and approval for entering into negotiations in the order of ranking recommended at a special called meeting on Monday, January 23, 2017 at 7:30 a.m.

Pre-ranking of proposals by Administration is merely a district process to pre-check if all requested documents and information in the Request for Proposals (RFP) was submitted prior to the Evaluation and Selection Committee formal evaluation. The pre-ranking of proposals is strictly unofficial. The Request for Proposal (RFP) package includes document CSP – 00350 Evaluation and Selection Criteria for Competitive Sealed Proposals which defines this portion of the procurement process. The District Evaluation and Selection Committee is comprised of three (3) Board of Trustees Facilities Committee Members and one (1) appointed Administration Staff. The Evaluation and Selection Committee will evaluate, rank and publish all proposals. The Evaluation and Selection criteria has been approved by the Mission C. I. S. D.'s Board. Once the M. C. I. S. D. Board of Trustees approves the ranking, the District Evaluation and Selection Committee will then proceed to negotiate a contract with the highest-ranking Proposer.

The Finance department in conjunction with the districts finance consultants have been designing a funding package for this project. In order to ensure this project under this funding source be securely financed Administration is recommending to adjust the contingency budget by an increase of \$2 million. Thus, the total construction budget to include all soft-costs will not exceed \$10 million.

Three proposals were submitted for this project and were ranked by the Facilities Committee as per MCISD guidelines and procedures. The Board must now consider the rankings and approve to enter into negotiations with the top ranked firms in the order selected. Rankings listed below:

Company	Base Proposal	Alt. #1	Days
Holchemont Const. (291)	\$7,463,000.00	(\$287,000.00)	235
E-Con Const. (287.6)	\$7,450,000.00	\$210,000.00	180
Central Builders (260.2)	\$8,000,000.00	\$500,000.00	180

Note:

Alternate #1 is for a larger custom-built press box of which Administration recommends approving. Both E-Con Construction and Central Builders have an additional cost for this alternate, as per Holchemont Construction their base bid includes the larger custom press box. Should MCISD select the smaller pre-fabricated press box Holchemont has a \$287,000.00 deduct from their base bid. The intention is for a notice to proceed (NTP) to be issued on or before February 01, 2017 with a substantial completion date of July 31, 2017, which is 180 days, Holchemont has a substantial completion date of September 24, 2017. Proposals and days are all prior to negotiations.

At a Special Board of Trustees meeting to be held on Monday, January 23, 2017, the Board will consider and possibly approve the rankings to allow negotiations to begin. It is Administrations intent to bring forward at the Regular Board of Trustees meeting to be held

on Wednesday, January 25, 2017 an approval and recommendation for a best and final offer (BAFO) and to enter into contract with the selected general contractor. It is MCISD's construction procurement process to present all items for Facilities Committee discussion prior to presenting to the Board of Trustees for final approval.

At the Regular Board of Trustees meeting held on Wednesday, January 25, 2017, the board approved the best and final offer (BAFO) from Holchemont in the amount of \$7,463,000.00 with alternate #01 custom press box included as part of the contract. Notice to proceed (NTP) was issued on February 02, 2017 with a substantial completion date of August 21, 2017.

At the Regular Board of Trustees meeting held on Wednesday, April 12, 2017, the board approved and pulled the following items:

Consideration and Approval of AEA #01 for CPR #02 to Furnish and Install Sports Lighting for the Tom Landry Stadium Renovations Project.

Sports Lighting Allowance: \$600,000.00 AEA #01 Sports Lighting:
\$580,392.00

Balance: \$ 19,608.00

Consideration and Approval of AEA #02 for CPR #03 to Furnish and Install a Scoreboard Sound System for the Tom Landry Stadium Renovations Project. Item was pulled for further pricing on additional speakers throughout the stadium.

Consideration and Approval of AEA #03 for CPR #04 to Furnish and Install Football Safety Netting System for the Tom Landry Stadium Renovations Project. Item was pulled due to MCISD having the netting and poles and only required pricing for the installation.

Consideration and Approval of AEA #04R to "Credit" the Allowances for the Tom Landry Stadium Renovations Project. Item was pulled due to other items being pulled thus not being able to present an accurate balance total.

Consideration and Approval of CPR #06 to Change the Size of the Bronze Statue for the Tom Landry Stadium Renovations Project.

Bronze Statue Allowance: \$ 50,000.00
CPR#06 Bronze Statue: \$129,400.00
Bronze Statue Allowance Balance: (\$ 79,400.00)

Due to inclement weather in the month of March Holchemont Construction requested additional delay days, thus, they presented Consideration and Approval of CPR #09 for Seven (7) Delay Days for the Tom Landry Stadium Renovations Project. The new substantial completion date is August 28, 2017.

Administration presented Consideration and Approval of Selection of Color and Pattern for the Reserved Seating on Home Side for the Tom Landry Stadium Renovations Project. The Board approved option #1 alternating colors.

At the Regular Board of Trustees meeting held on Wednesday, May 10, 2017, the Board approved and pulled the following items:

Contingency Allowance:	\$100,000.00
AEA #01 Sports Lighting:	\$ 19,608.00
CPR #6 Bronze Statue:	\$ (79,400.00)
Contingency Balance:	\$ 40,208.00

Consideration and Approval of AEA #03R for CPR #04 to Furnish and Install Football Safety Netting System for the Tom Landry Stadium Renovations Project.

Football Safety Net System Allowance:	\$10,000.00
AEA#03 Football Safety Net System:	(\$ 7,500.00)
Balance:	\$ 2,500.00

Consideration and Approval of CPR #08 to Construct a Riser Room / Fire Pump for the Tom Landry Stadium Renovations Project.

Fire Suppression Pump Allowance Balance:	\$ 50,000.00
CPR # 08 Riser Room:	\$ 110,428.53
Balance:	
	(\$ 60,428.53)

Contingency Balance:	\$40,208.00
CPR #8 Riser Room:	(\$60,428.53)
Plus, Overhead and Profit	(\$2730.47)
Contingency Balance:	(\$22,951.00)

Due to inclement weather in the month of April and MCISD testing Holchemont Construction requested additional delay days, thus, they presented Consideration and Approval of CPR #09 for Eight (8) Additional Delay Days for the Tom Landry Stadium Renovations Project. The new substantial completion date is September 05, 2017.

Note: The first scheduled football game is for Friday, September 01, 2017 with VMHS vs Harlingen. Substantial completion is granted when the facility can be utilized for its intended use. The City of Mission Fire Marshal must approve the facility to include all fire systems are inspected and tagged "approved" along with all ADA inspections and approvals and to include the inspection and approval of the elevator system and to include any other inspections required. Coaches are working on a Plan "B" should the stadium not be completed on time.

Administration recommended Consideration and Approval of Re-naming for the Tom Landry Stadium Renovations Project as "Tom Landry Hall of Fame Stadium".

Administration recommended Consideration and Approval of Selection of Color for Reserved Seating on Home Side for the Tom Landry Stadium Renovations Project.

Recommendation is based on the colors selected by Coach Detmer, Coach Gilpin, Athletic Director Joe Sanchez and Athletic Director Leticia Ibarra.

Royal Blue
Texas A&M – Maroon

After a lengthy discussion on possible color dis-coloration of the royal blue and maroon seats the Board approved “grey” for the reserved seating.

Alvarado Architects presented a “pose” selection on the statue. At the Facilities Committee meeting held on Wednesday, May 03, 2017, the Committee along with members of the Campus Construction Over-Sight Committee members reviewed and discussed the five (5) options of poses brought forward by Mr. Alvarado. By virtue of the discussion and by show of hands, options #1 and #4 were selected for presentation to the Board. The Board approved Consideration and Approval of Tom Landry Statue Pose for the Tom Landry Stadium Renovations Project Option #1.

At the Facilities/Environment Committee meeting held on Wednesday, June 07, 2017 several CPR’s were presented and discussed. These CPR’s may become change orders should current available allowances not cover the over-budget of the project when it is finalized. MCISD Administration stressed to Alvarado Architects and Holchemont Construction the discontent of change orders and requests for additional construction time. Administration stressed the importance of having the project completed as per the original substantial completion date.

At a Special Board of Trustees meeting held on Wednesday, June 07, 2017, the Board granted Superintendent Dr. Ricardo Lopez authority to approve change orders/change proposal request for the Tom Landry Stadium Renovations Project in the amount not to exceed a total of \$250,000.00. This action was to facilitate the change order/CPR process and not delay the general contractor waiting for a decision.

The following Change Orders/CPR’s were approved by Superintendent Dr. Ricardo Lopez on Wednesday, June 07, 2017:

Supt. Approval Balance:	\$250,000.00
CPR#05R Structural Steel:	\$ 31,824.00
Foundation:	\$ 12,161.00
CPR#14 for HVAC at the Gift Shop:	\$ 1,816.00
Supt. Approval Balance:	\$183,257.00
CPR#06R Bronze Statue	
Foundation:	\$ 8,674.00
CPR#11 for MEP changes at the Press Box:	\$ 12,268.00
CPR#19 for	
Additional Gates for Eagle Drive:	\$ 1,816.00

Consideration and Approval of CPR#05R for Structural Steel between Grandstands and Custom Press Box for the Tom Landry Stadium Renovations Project.

Contingency Balance:	(\$22,951.00)
Structural Steel Additions Cost:	\$31,824.00
Contingency Balance:	(\$54,775.00)

Consideration and Approval of CPR#06R for Bronze Statue Foundation and Base for the Tom Landry Stadium Renovations Project.

Contingency Balance: (\$54,775.00)
Bronze Statue Base Foundation Cost: \$12,131.00
Contingency Balance: (\$66,906.00)

Consideration and Approval of CPR#11 for MEP changes at the Press Box for the Elevator for the Tom Landry Stadium Renovations Project. Holchemont, LTD is requesting eight (8) additional day, if approved, the new substantial completion date is September 13, 2017. As per Alvarado Architects additional days will not be submitted.

Contingency Balance: (\$66,906.00)
Electrical at press box Cost: \$ 8,674.00
Contingency Balance: (\$75,580.00)

Consideration and Approval of CPR#14 for HVAC at the Gift Shop for the Tom Landry Stadium Renovations Project.

Contingency Balance: (\$75,580.00)
HVAC at gift shop Cost: \$12,268.00
Contingency Balance: (\$87,848.00)

Consideration and Approval of CPR#19 for Additional Gates for Eagle Drive for the Tom Landry Stadium Renovations Project

Contingency Balance: (\$87,848.00)
Gates at Eagle Drive Cost: \$ 1,816.00
Contingency Balance: (\$89,664.00)

At the Regular Board of Trustees meeting held on Wednesday, June 21, 2017, The Board did not approve Consideration and Approval of CPR#20 for Additional Four (4) Rain Days for the Month of May for the Tom Landry Stadium Renovations Project.

*Note: After meeting with Alvarado Architects and Holchemont LTD, they were advised that Administration will be questioning any further delay days submitted and that Holchemont should continue working on a recovery schedule plan to attempt to bring this project at the initial substantial completion date of August 21, 2017.

The following Change Orders/CPR's were approved by Superintendent Dr. Ricardo Lopez on Thursday, June 29, 2017 in order to have the project continue without contractor delays:

Supt. Approval Balance Granted: \$183,257.00
CPR#12 Track Timing System: \$ 45,322.00
Supt. Approval Balance:
\$137,935.00
Change Order Amount to Date: (\$134,986.00)

Note: General Contractor has added 12% overhead and profit and 1.5% for project bonding on all change order amounts.

Soil Stabilization Allowance: \$90,000.00

CPR #16 Soil Stabilization:	\$10,000.00
Balance:	\$ 0.00
Utility Allowance:	\$20,000.00
CPR #21 Boring & Trenching:	\$16,830.00
Balance:	\$3,170.00

At the Special Board of Trustees Meeting to be held on Thursday, July 27, 2017, Administration presented to the Board Consideration and Approval of CPR#15 for Graphics for the Tom Landry Stadium Renovations Project. This amount is to be taken from the graphics allowance already included in the original contract.

Graphics Allowance Balance:	\$100,000.00
Banner system:	(\$ 51,148.50)
Identification signage:	(\$ 26,815.00)
Bleacher section signage:	(\$ 13,625.00)
Traffic signage:	(\$ 2,136.00)
Fire lane striping:	(\$ 3,700.00)
Balance:	\$ 2,575.50

At the Regular Board of Trustees meeting held on Wednesday, August 09, 2017, the Board considered and approved some of the following items:

As per our Legal Counsel, the Board did not need to vote on agenda item, Consideration and Approval of Additional Seven (7) Delay Days for AEA#11 for CPR #21 for the Tom Landry Stadium Renovations Project which was previously denied but being brought forward by Holchemont, LTD. once again for consideration. The Board had stated it would possibly revisit this request and no action was taken.

Consideration and Approval of AEA#12 for CPR #22 for Landscaping and Irrigation for the Tom Landry Stadium Renovations Project.

Landscape/Irrigation Allowance:	\$20,000.00
CPR#22 Landscape & Irrigation:	\$17,383.00
Balance:	\$ 2,617.00

Consideration and Approval of AEA#13 for CPR #24 to Up-grade the Scoreboard System for the Tom Landry Stadium Renovations Project.

Scoreboard Sound System Allowance:	\$55,000.00
CPR#24 Scoreboard System:	\$34,934.00
Balance:	\$20,066.00

Consideration and Approval of CPR #23 for Speaker System for the Tom Landry Stadium Renovations Project. This agenda item was pulled.

At the Regular Board of Trustees meeting held on Wednesday, September 13, 2017, the Board revisited and approved Consideration and Approval of Additional Seven (7) Delay Days for AEA#11 for CPR #21 for the Tom Landry Stadium Renovations Project. As of

the date of this Board of Trustees meeting Holchemont LTD will be into possible liquidated damages as per contract of \$1,500.00 per day of not meeting the substantial completion date. Administration brought forward this request, the new substantial completion date is September 12, 2017.

At the Regular Board of Trustees meeting held on Wednesday, October 11, 2017, the Board took the following actions for the following items:

Consideration and Approval of CPR #12R3 for Additional Power for the Tom Landry Stadium Renovations Project. Please note that Holchemont, LTD will require and extra four (4) days. If approved, the new substantial completion date is September 16, 2017. This item was pulled until further review.

Note: MCISD does not agree with this pricing, however, there will be a cost associated with installing conduits within the concrete slab which was done earlier. If the revised pricing is not approved MCISD Maintenance will complete the electrical connections.

Contingency Balance: (\$134,986.00)
CPR#12R3 for Additional Power: \$ 0.00 (Org. price \$10,134.42)
Change Order Amount to Date: (\$134,986.00)

Consideration and Approval of CPR #12R5 for Additional Cabling for Track Timing System for the Tom Landry Stadium Renovations Project. Please note that Holchemont, LTD will require and extra fourteen (14) days. If approved, the new substantial completion date is September 30, 2017. This item was pulled until further review.

Contingency Balance: (\$134,986.00)
CPR#12R5 Additional Cabling: \$ 0.00 (Org. price \$54,468.65)
Change Order Amount to Date: (\$134,986.00)

Consideration and Approval of CPR #17 to "Credit" Two (2) Wireless Access Points, Shortel Phone and Video Server for the Tom Landry Stadium Renovations Project. This item was approved.

Contingency Balance: (\$134,956.00)
CPR#17 "Credit" on Technology: \$ 5,000.00 "Credit"
Change Order Amount to Date: (\$129,986.00)

Consideration and Approval of CPR #18 to "Credit" Fire Alarm and Intrusion Systems for the Tom Landry Stadium Renovations Project. This item was approved.

Contingency Balance: (\$129,986.00)
CPR#18 "Credit" Fire Alarm System: \$ 2,800.00 "Credit"
Change Order Amount to Date: (\$127,186.00)

Consideration and Approval of CPR #25 to Relocate Cross Bracing at Concession Stands for the Tom Landry Stadium Renovations Project. This item was approved with the cost change to \$5,221.00

Contingency Balance: (\$127,186.00)
CPR #25 to Relocate Cross Bracing: (\$ 5,221.00) (Org. price \$10,442.00) Change Order
Amount to Date: (\$132,407.00)

Consideration and Approval of CPR #26 to Remove and Replace Concrete from the Ramps for the Tom Landry Stadium Renovations Project. Please note that Holchemont, LTD will require and extra two (2) days. If approved, the new substantial completion date is October 2, 2017. This item was pulled, Javier Hinojosa Civil Engineer will take care of this item.

Contingency Balance: (\$132,407.00)
CPR #26 to Remove and Replace Concrete: \$ 0.00 (Org. price \$4,483.25)
Change Order Amount to Date: (\$132,407.00)

Consideration and Approval of CPR #27 to Add IDF Rack, Quad Receptacles and Data Drops on the Visitor's Side Bleachers for the Tom Landry Stadium Renovations Project. Please note that Holchemont, LTD will require and extra three (3) days. If approved, the new substantial completion date is October 5, 2017. This item was pulled, MCISD will take care of this item.

Contingency Balance: (\$132,407.00)
CPR #27 to Add IDF Rack: \$ 0.00 (Org. price \$18,357.49)
Change Order Amount to Date (\$132,407.00)

Consideration and Approval of CPR #29 for Additional Eleven (11) Delay Days for the Tom Landry Stadium Renovations Project. If approved, the new substantial completion date is October 16, 2017 pending all other CPR's being submitted. The Board took no action on this item.

Consideration and Approval to Grant Administration Authority to Approve Substantial Completion for the Tom Landry Stadium Renovations Project. Dr. Lopez, Superintendent will have the authorization. This item was approved.

Note: No additional delay days were approved at this meeting. Substantial completion continues to be approximately September 12, 2017.

At the Regular Board of Trustees meeting held on Wednesday, November 08, 2017, the Board took the following actions for the following items:

Consideration and Approval of CCD#01 for CPR#30 for Modifications to the Elevator Equipment Room for the Tom Landry Stadium Renovations Project. No additional days were approved.

Contingency Balance: (\$132,407.00)
CCD#01/CPR#30 Elevator Equipment Room: \$ 3,957.00
Change Order Amount to Date (\$136,364.00)

Consideration and Approval of CPR#31 to "Credit" for Use of Owners Utilities for the Tom Landry Stadium Renovations Project. MCISD presented a "credit" for \$5,900.00, however, Holchemont offered only a credit amount of \$900.00.

Contingency Balance: (\$136,364.00)
CPR#31 Use of Owners utilities: \$ 5,900.00 "Credit"
Change Order Amount to Date: (\$130,464.00)

Consideration and Approval of CPR#32 for HVAC Test and Balance for the Tom Landry Stadium Renovations Project.

Test and Balance Allowance: \$5,000.00
CPR#32 HVAC Test & Balance: \$2,500.00
Balance: \$2,500.00

Consideration and Approval of CPR#33 for Two (2) Additional Fire Extinguishers for the Tom Landry Stadium Renovations Project.

Contingency Balance: (\$130,464.00)
CPR#33 Fire Extinguishers: \$ 268.00 Change Order Amount
to Date (\$130,732.00)

At the Regular Board of Trustees meeting held on Wednesday, December 13, 2017, the Board took the following actions for the following items:

Consideration and Approval of CPR #12R3 for Additional Power for the Tom Landry Stadium Renovations Project. This item was approved.

Contingency Balance: (\$130,732.00)
CPR#12R3 additional power: \$ 6,327.00
Balance: (\$137,059.00)

Consideration and Approval of CPR#34 for "Credit" for the VIP Chair Allowance for the Tom Landry Stadium Renovations Project. VIP Chair Allowance "Credit" is \$5000.00. This item was approved.

Discussion and Possible Action on Paving Repair Schedule for the Tom Landry Stadium Renovations Project.

Consideration and Approval for Final Completion, Less Betterment Fund Allowance and Final Payment, Less Liquidated Damages for the Tom Landry Stadium Renovations Project. This item was pulled due to punch list items and other contractual obligations were noncompliance.

At the Regular Board of Trustees meeting held on Wednesday, April 11, 2018 the Board took the following actions for the following items:

Consideration and Approval of CPR#23 for Sound System Raceways for the Tom Landry Stadium Renovations Project. Holchemont LTD is requesting fourteen (14) additional

delay days for this work, if approved the new substantial completion date is September 26, 2017.

Contingency Balance: (\$137,059.00)
CPR#23 for Sound System: \$ 39,839.37
Balance: (\$176,898.37)

Consideration and Approval of Grievance Agreement for Use of Owners Utilities for the Tom Landry Stadium Renovations Project. As per the November approved CPR #31, MCISD approved an owner's credit for utility use of \$5,900.00. As per grievance agreement the amount was reduced to \$2,350.00, thus an adjustment needed to be made.

Previous: \$5,900.00
Final approved as per Grievance: \$2,350.00
Adjustment: \$3,550.00

Contingency Balance: (\$180,448.37)

Discussion and Possible Legal Action Regarding Parking Lot Repairs for the Tom Landry Stadium Renovations Project. At this time the Board invoked the "Self Help Provision" of the contract authorizing Administration to make necessary parking lot repairs utilizing a different contractor.

2GS and Earthworks re-paving Cost: \$24,700.00 - Parking Lot Re-paving completion date was achieved on August 06, 2018.

At the Regular Board of Trustees meeting held on Wednesday, May 08, 2019, the Board took no action on the following item: Consideration and Approval for Final Completion, Less Betterment Fund Allowance and Final Payment, Less Liquidated Damages for the Tom Landry Stadium Renovations Project. At this meeting Administration also recommended to authorize Administration and Dr. Perez to approve final completion at a later time, this was rejected with direction from the Board that they wanted this brought forward when the time came for consideration and approval.

At the Regular Board of Trustees meeting held on Tuesday, June 11, 2019 the Board took the following actions

Administration, Mr. Eli Alvarado, Architect, and Mr. Michael Montalvo, General Contractor have met six times since April 25, 2019 with the latest meeting held on Tuesday, June 04, 2019, to discuss what is required from all parties to bring this project for final recommendation and to possibly come to a mutual agreement and present to the Board of Trustees Consideration and Approval for Final Completion, Less Betterment Fund Allowance and Final Payment, Less Liquidated Damages for the Tom Landry Stadium Renovations Project. At the latest meeting Mr. Montalvo was not able to attend and for many of these meetings Dr. Perez, Superintendent was present. A 1 ½ year warranty project walk-through was conducted as per contract specifications on Friday, May 03, 2019 with Mr. Alvarado, his design staff, Mr. Montalvo, his sub-contractors and MCISD personnel present to identify any warranty items that are still pending and need correction. The meetings that are being conducted are to balance and agree on all

financial/accounting matters and pending correction of work if applicable. Any matters that concern additional request for time or matters that may concern any deduction from the remaining balance owed to the contractor such as additional fees/costs or possible liquidated damages incurred the general contractor will need to follow the process as written in his contract.

As noted, Administration and Alvarado Architects believes it has tried, with due diligence, to work on all pending accounting/fiscal matters with Mr. Montalvo, however, we continue to not agree on a mutual amount. Administration presents Discussion with Legal Counsel Regarding Closeout for the Tom Landry Stadium Renovations Project with MCISD processing any possible pay applications to Holchemont Construction with monies being withheld that are not in contention.

Note: Additional structural assessment is continuing by Rick Hinojosa, Structural Engineering and is pending completion. They are pending additional concrete test results.

Tom Landry Stadium Project Timeline:

Notice to Proceed (NTP) – 02/01/2017

Original Substantial Completion Date – 08/21/2017

36 delay days Board approved due to testing, weather, change orders

New substantial completion date – 09/26/2017

Approved substantial completion date – 11/10/2017 (45 days late)

Original Final Completion Date – 12/10/2017

New Final Completion Due Date – 04/20/2018 (131 days late)

Possible LD's for not meeting Subst. Completion: 45 days X \$1,500.00 = \$67,500.00

Possible LD's for not meeting Final Completion: 131 days X \$500.00 = \$65,500.00

Possible LD's for delay in re-paving of parking lot: 7 days x \$500.00 per day = \$3,500.00

Possible LD's Incurred: \$136,500.00

Other Possible Fees/Costs:

Re-paving of parking lot = \$24,700.00

Structural Engineering cursory inspection = \$5,000.00 (Rick Hinojosa, Structural Engineering)

Hinojosa full structural assessment = \$30,000.00 (if applicable)

TDLR re-inspections = \$285.00

Terracon Structural additional services = \$15,000.00

Pending "credit" for three (3) parking lot poles not installed = \$53,489.08

Approximate Possible Total Amount of addtl. fees/costs: \$128,474.08

Additional Architect Fees: \$85,695.00 (if applicable/pending)

Balance on contract: \$416,406.11

Possible LD's: \$136,500.00 Possible addtl. Costs:

\$128,474.08

Possible addtl. Arch. Fees: \$ 85,695.00

Paid Holchemont: \$ 43,189.25 (07/24/19 Pay App. #10 rev.3)

Est. Current Balance on Contract: \$380,251.23 as of 04/21/2021 \$347,206.23

Est. Construction Costs: \$6,000,000.00

Est. Total Construction w/Soft Costs: \$8,000,000.00

BAFO Const. Cost: \$7,463,000.00

Change Orders: \$ 142,020.37

Final Const. Cost: \$7,605,020.37

Architect Fees: \$485,095.00 6.5% of Construction Cost

Addtl. Arch. Fees for C/O's: \$9,231.32

Architect Fees: \$494,326.32 (excluding addtl. Fees pending)

At the Regular Board of Trustees meeting held on Wednesday, August 14, 2019 the Board took the following actions.

At this meeting the Mr. Rick Hinojosa Structural Engineering Assessment report was not available for the Board of Trustees to review, however, Administration had preliminary verbal discussions with Hinojosa on what he was to submit, the report was to be finalized on Friday, August 16, 2019. Should the report state that repairs were required Administration presented Consideration and Possible Action Regarding Procurement of Design and Construction Services for the Tom Landry Stadium Repairs in advance.

After conducting field reviews and inspections Mission CISD contracted with Rick Hinojosa Structural Engineering to conduct a third party Visual Cursory Observation on the bleachers for the visitor's side of Tom Landry Stadium. On September 06, 2018 the observation report with conclusions and recommendations was submitted. In brief, Hinojosa stated that the cracked piers did not affect the immediate load carrying capacity of the structure and the stadium could be used. However, the recommendations were to conduct a complete assessment of all piers and repair all necessary items addressed in the complete assessment.

Administration was approved to contract with Hinojosa to conduct a full stadium assessment to include not only concrete piers but to inspect the entire structure of the stadium. On August 08, 2019, Hinojosa Engineering submitted a preliminary assessment letter for our review noting possible reinforcement required.

On August 16, 2019, Hinojosa Structural Engineering submitted their Visual Structural Condition Assessment of Tom Landry Stadium for our review.

At the September 11, 2019 Regular Board of Trustees meeting and based on Mr. Hinojosa's report, Administration presented Consideration and Approval of Design and Construction Services for the Tom Landry Stadium Repairs.

The Board of Trustees must take the necessary action in accordance with Texas Education Code 44.035 which consisted of the selection/designation of an architect and/or engineer to prepare construction documents for this project. The engineer and/or architect selected or designated will have full responsibility for complying with the Texas Engineering Practice Act (Article 3271a, Vernon's Texas Civil Statutes) or Chapter 478, Acts of the 45th Legislature, Regular Session, 1937 (Article 249a, Vernon's Texas Civil Statutes) as applicable.

If the engineer or architect is not a full-time employee of the District, the Board must select the engineer or architect on the basis of demonstrated competence and qualifications as provided by Section 2254.004, Government Code. The selected architect/engineer along with preparing construction documents will be required to provide MCISD with an estimated project budget.

Current and/or past structural engineers that have worked with MCISD are listed below, the Board of Trustees may select from one of these engineers on the basis of demonstrated competence and qualifications or may direct Administration to seek for Request for Qualifications (RFQ's) on an engineer or architect.

Rick Hinojosa Structural Engineering (conducted assessments)
Chanin Structural Engineering (original project structural engineer)

The Board of Trustees selected Mr. Rick Hinojosa Structural Engineering to conduct a thorough third-party structural assessment of the Tom Landry Stadium Project.

On or about January 27, 2020, Mr. Hinojosa submitted to Administration a proposal for forensic engineering services from MEG Engineers. The Forensic Engineering Services will include Ground Penetrating Radar (GPR) Scans of one-hundred and fifty-six (156) piers by scanning four (4) grids at each pier location. A grid will consist of a three (3) foot by two (2) foot rectangle made up of thirty-five (35) gridlines spaced at six (6) inches on center. Total linear footage of scanning will be eighteen thousand and ninety-six (18,096) feet. The report will include detailed rebar locations of the piers. The proposal cost for this service was \$56,000.00.

At the Facilities/Environment Committee Meeting of February 05, 2020 this proposal and engineering service was presented and discussed. At this time the decision was made for Administration to proceed with Hinojosa Structural Engineering and MEG Engineers to conduct only seventy-eight (78) GPR Scans on the stadium. These scans would be divided between the home and visitors side piers at a proposal cost of \$34,988.00.

At the Regular Board of Trustees meeting held on April 08, 2020 the Board approved the following, Preliminary reports from both engineering firms indicate that a complete GPR Scan of all piers would be advisable to have a complete pier assessment on the stadium. Thus, Administration recommends Consideration and Approval of Additional Ground Penetrating Radar (GPR) Scans for Piers at the Tom Landry Stadium Bleacher Project. The estimated proposal cost would be the difference from the original proposal to what has been approved for the first phase. Estimated proposal \$21,012.00.

At the Regular Board of Trustees meeting held on September 09, 2020, as an informational Board Item, a presentation was given by Rick Hinojosa Structural Engineering, Mr. Albert

Trevino, on the Tom Landry Stadium Renovation Project status. Mr. Trevino reported on the findings for the GPR scans conducted and has stated, “the scans in the report indicate that the majority of the piers do not have pier reinforcement per the shop/erection drawings provided by Sturdy Steel who provided the bleachers”.

At the meeting of September 09, 2020, Hinojosa Structural Engineering was to provide a final and complete comprehensive report on the findings and recommendations for correction on all items indicated on the assessment. Findings and recommendations were to include and not limited to the disciplines of Structural, Mechanical, Electrical, Plumbing (MEP) and Civil. At this meeting Hinojosa Structural Engineering was directed to provide this comprehensive report and not only the GPR scans report.

Since this initial directive, Hinojosa Structural Engineering has been contacted both on October and December 2020 for the final report and we continue to have no response. Administration will continue to utilize all avenues to request the final report so that we may move forward with repairs required.

On January 14, 2021, Rick Hinojosa Structural Engineering was sent both an email correspondence and a certified letter requesting his personal appearance at the Wednesday, January 20, 2021 Board of Trustees Work Shop to present the final project findings. At 4:01 p.m. on that day Mr. Hinojosa contacted us that he had a family emergency and would try to attend. With this correspondence he attached “Mission CISD Tom Landry Stadium Ground Penetration Radar (GPR) Scanning Findings Letter”. This letter referenced the GPR scanning done at the stadium.

In discussion at the Work Shop of January 14, 2021, the Board instructed our legal counsel to draft a letter to request Mr. Hinojosa’s presence and to once again present his findings at the Board Work Shop of Wednesday, February 03, 2021. Legal counsel sent a certified letter and emailed the letter to Mr. Hinojosa’s attention on Tuesday, January 26, 2021. My office then proceeded to re-send this letter to Mr. Hinojosa the following day. A “read receipt” message was received from his office on Friday, January 29, 2021 at approximately 12:10 p.m. acknowledging receipt of our request to be present.

At this Work Shop of Wednesday, February 03, 2021, the Board will hear the presentation and may have a question and answer session with Mr. Hinojosa on the findings and recommendations. At this time the Work Shop may have a Discussion and Possible Action to Procure Engineering Services for Analysis and Remediation for the Tom Landry Stadium Project and to Grant Administration Authorization to Procure Services. The presentation was not held at the Work Shop and was presented at a Special Board of Trustees Meeting after.

At the Special Board of Trustees meeting of Wednesday, February 03, 2021, Mr. Rick Hinojosa presented his “Mission CISD Tom Landry Structural Comprehensive Assessment Report”. After discussion with the Board of Trustees and Administration, Mr. Hinojosa was directed to once again present at the Regular Board of Trustees meeting of Wednesday, February 10, 2021. This presentation is to mainly address all the viable options on how to correct the issue of the piers found to be not safe and not constructed as per code as noted in the report and reported by Mr. Hinojosa at the meeting. He is to also present a scope of work and a phasing plan of repairs beginning with the most safety critical items. What will also need to be addressed is if any other areas will be damaged

while repairing the piers, such as the flatwork. Each option(s) will need to satisfy all building and structural codes along with satisfying all safety compliance codes. At this meeting Mr. Hinojosa was advised that time was critical for the usage of the stadium since graduation ceremonies have already been scheduled. Mr. Hinojosa stated that plans and specifications should be finalized soon and we may be able to advertise for competitive sealed proposals (CSP's) within the next couple of weeks and possibly have a contractor begin repairs as quickly as the procurement process allows, that is the goal.

The procurement process will be Competitive Sealed Proposals (CSP's) of which the Board adopted as the method of delivery. The Board approved the Hidalgo County Prevailing Wage Rate of which is an exhibit and was attached. The Board also adopted the selection criteria of which proposals are evaluated and ranked. Administration also recommended that the Board authorized the Superintendent to rank the proposals and to negotiate an agreement with the highest ranked contractor.

On February 10, 2021, the Board approved Consideration and Possible Action Regarding Permanent and Emergency Repairs for the Tom Landry Stadium to Include the Wage Rate, Selection Criteria, and Authorization to Dr. Perez as mentioned under the Administrative considerations.

Advertisements in the local newspapers for Competitive Sealed Proposals (CSP's) were posted on March 24, 2021 and March 31, 2021. Proposals were to be opened April 08, 2021 and firms would be able to view remotely. The virtual pre-proposal meeting was Thursday, April 01, 2021 at 2:00 p.m. to allow all prospective contractors the opportunity to ask questions concerning the project plans and specifications.

CSP's were to be submitted on April 8, 2021, and were to be reviewed and ranked by the Administration Committee. This Administrative review was to be presented at the Regular Board of Trustees Meeting of Wednesday, April 14, 2021.

On Wednesday, April 06, 2021 Hinojosa Structural Engineering submitted a recommendation to extend the bid date by two weeks to allow contractors and sub-contractors more time to bid on the project. He also stated that a second pre-bid conference be held followed by a walk-through of the stadium facility. This recommendation was due also to no contractors attending the initial pre-bid conference. This recommendation was presented at the Board of Trustees Work Shop on Wednesday, April 08, 2021.

A second pre-proposal meeting was held on Thursday, April 15, 2021. With the two-week extension proposals were due and publicly opened on Thursday, April 22, 2021 at 2:00 p.m. at the Central Office Board Room. Proposals were reviewed, evaluated and ranked on Monday, April 26, 2021 at 2:00 p.m. by Ms. Rumalda Ruiz, Ms. Dora Garcia, Ms. Lorena Garcia, Mr. Joel Garcia and Mr. Ricardo Rivera with Ms. Daisy Cuevas assisting.

Due to the timeline to begin permanent repairs Administration requested a Special Board of Trustees meeting on Tuesday, April 27, 2021 at 12:00 p.m. at the Central Office Board Room. At this meeting Administration presented and the Board approved Consideration and Approval to Accept Administrations Rankings and Enter Into Negotiations in the Order of Ranking for the Tom Landry Stadium Repairs Project.

G & G Construction

Base Bid: \$1,024,850.00 with 210 construction days

Alternate Bird Screen: \$127,000.00 with an additional 45 construction days

TOTAL: \$1,151,850.00 with 255 days from notice to proceed (approx. 8.5 months)

Terra Fuerte Const.

Base Bid: \$1,141,000.00 with 180 construction days

Alternate Bird Screen: \$30,000.00 with an additional 30 construction days

TOTAL: \$1,171,000.00 with 210 days from notice to proceed (approx. 7 months)

Project negotiations were scheduled for Wednesday, May 05, 2021 at 10:00 a.m. as per G & G Constructions earliest available meeting date and time. Administration presented Consideration and Approval to Accept the Best and Final Offer (BAFO) and to Enter Into Contract for the Tom Landry Stadium Repairs Project and requested for a Special Board of Trustees meeting following the Board Work Shop to consider action on this item.

The Board of Trustees has the option to accept this BAFO, the initial base proposal, to decline the offer and direct Administration to enter into negotiations with the next contractor or to reject all offers and re-advertise for the project using the same specifications and design or direct the engineer to re-design the project.

At the Special Board meeting held on May 5, 2021, the Board approved G & G Contractors Best and final offer Base Bid: \$1,024,850.00 with 210 construction days. Notice to proceed was effective July 28, 2021, with substantial completion will be February 23, 2022.

At the Regular Board meeting held on November 10, 2021, the Board approved the following items:

Consideration and Approval of Allowance Expenditure Authorization (AEA) #01 for Structural Repairs on Various Piers for the Tom Landry Stadium Repairs.

Contingency Allowance:	\$20,000.00
AEA #1 Various Piers:	\$ 8,241.88
Balance:	\$11,758.12

Consideration and Approval of Change Order #1 for Forty-four (44) Delay Days due to the structural repairs on various piers for the Tom Landry Stadium Repairs. If approved the new substantial completion will be April 08, 2022.

On Friday, December 10, 2021 a letter was sent by MCISD to Mr. Rick Hinojosa, Hinojosa Structural Engineering and to Mr. Rene Garza, RG Enterprises LLC. referencing the Tom Landry Stadium Repair Project.

At the request of Mr. Garza, a project meeting was held on Wednesday morning, December 15, 2021 to discuss items referenced in the letter. Present at the meeting were staff members of R. Hinojosa Structural Engineering, Raba Kistner, Geo-tech Testing, G&G Const. and MCISD Staff.

At the Regular Board of Trustees meeting held on December 15, 2021, Mr. Albert Trevino. Hinojosa Structural Engineering and Mr. Rene Garza, RG Enterprises LLC presented an update on the project. During the presentation at least five (5) possible change orders which consist of additional costs and time were mentioned as forthcoming.

The Board expressed concern that the project needed to move forward and that requests for special meetings would be acceptable in order to expedite change orders needed as to not delay the project further.

A Special Board of Trustees Meeting has been requested for Wednesday, January 05, 2022 for Consideration and Approval of Change Order(s) for the Tom Landry Stadium Repairs Project.

At the Regular Board of Trustees meeting of December 15, 2021, both firms were instructed to work on change proposals to be submitted at the special called meeting of Wednesday, January 5, 2022. During the presentation by both Mr. Albert Trevino – Hinojosa Structural Engineering and Mr. Rene Garza – RG Enterprises, LLC they presented seven (7) possible construction proposal requests (CPR's). They were directed to present to the Administration and Board of Trustees detailed explanations for each CPR on why these were required, if by Code or other reasons. They were also directed to ensure that these CPR costs were the only option(s). It was also directed that they needed to specify if any of the CPR's would either delete or offset any of the work already included in their original scope of work and that the adjustment of all time and materials associated needed to be reflected as a "credit" to the district. As per Mr. Trevino, he would only inform the Administration and the Board of receipt of these CPR's and at this time would not formally present them for consideration since he had not yet reviewed them with RG Enterprises, LLC and did have some questions for them. Both firms were made aware that legally the project could not exceed 25% of the total cost of the project in change orders. Administration and the Board once again reiterated the need to resume work at the stadium and were very receptive to having meetings to review and possibly approve items to have the project progress. The Board asked which CPR's were critical at this time so that the project would continue and items #3, #5 and #6 that were presented that evening were noted. Both firms were directed to work on submitting these CPR's using the required AIA Document G701 - 2017 which specifically is designed to submit change orders to the project and present them at a Special Board of Trustees meeting on Wednesday, January 12, 2022.

At the Special Board of Trustees meeting held on Wednesday, January 12, 2022, R. Hinojosa Structural Engineering and RG Enterprises, LLC presented possible change orders #2, #3 and #4. Change order #4 was the combination of Change Proposal Requests (CPR's) #5 and #6 that were presented at the previous meeting of January 05, 2022. Along with cost information were additional days requested. In consultation with Mr. David Hansen - Legal Counsel it was asked that the change orders be reviewed once again and that the costs and days all be incorporated into one single change order document. The change order was to be sent to our legal office to be incorporated into our required change order document. Both firms were asked to create a work schedule separating time from the home side versus the visitor side. A presentation is scheduled to be made once again at the Regular Board of Trustees meeting on Wednesday, January 19, 2022.

At the Regular Board of Trustees meeting held on Wednesday, January 19, 2022, R. Hinojosa Structural Engineering and RG Enterprises, LLC once again presented possible costs and change orders with a substantial completion date of early November 2022. This item was taken into Executive Session for consultation with our legal counsel.

After consultation and review, the decision and directive to both R. Hinojosa and RG Enterprises was to split the project between the home side repairs and the visitor repairs. Each side was to be a separate project with RG Enterprises submitting a change order for credit to work being separated from the visitor side and an updated schedule of values for completing the home side as this was the priority. A brief meeting was held after the Board of Trustees meeting with the design team, the general contractor, and MCISD staff to ensure that they understood the directive issued, of which they acknowledged that they understood. The directive was to have the change order with new updated costs, credits and timeline by the regularly scheduled Board Workshop on Wednesday, February 02, 2022.

Correspondences and meetings continued the week January 24 – 28th with uncertainty from RG Enterprises about what was required and expecting a written authorization from Dr. Perez, MCISD Superintendent concerning what was directed at the previous Board meeting. A Zoom meeting was held on Thursday, January 27, 2022 with R. Hinojosa Staff, Mr. Manuel Leal, G & G Construction Superintendent, Mr. Adrian Hernandez, Mr. Adan Rivera, Ms. Lorena Garcia, and Mr. Rick Rivera to clarify the directive and expectations and the urgency for submitting the required change orders. It was presented that there would be no written authorization from Dr. Perez and that the directive issued at the Board meeting would suffice. It was also discussed that the general contractor was directed in an email by R. Hinojosa and Mr. Adrian Hernandez of what was required, Mr. Leal acknowledged the direction. A Zoom meeting was once again scheduled for Friday, January 28, 2022 to review the status of the change order. Once again both the general contractor and design team were directed to submit all change orders in a timely manner and not at the last minute when Administration does not have time to review before the presentations to Dr. Perez and the Board of Trustees. It was also noted that for all meetings we needed to have either Mr. Adrian Hernandez or Mr. Adan Rivera present.

ADMINISTRATIVE CONSIDERATIONS

Administration and the Board of Trustees have made a decision to separate the Tom Landry Stadium Repairs into two separate projects, home side and visitors side. The home side will be a priority with the current contract. Currently RG Enterprises, LLC, general contractor, is to submit a new schedule of values, credits and a new timeline for them to continue and complete the home side as scheduled. The visitor's side will now be considered a new project and thus Administration presents Project and Proposed Budget for Supplemental Repairs (Visitors Side) for the Tom Landry Stadium Project.

FUNDING SOURCE

General Funds and Possible other funding sources to be determined by the Finance Dept. (TBD)

RECOMMENDATION

Administration presents Consideration and Approval of Project and Proposed Budget for Supplemental Repairs (Visitors Side) for the Tom Landry Stadium Project

EXHIBIT

N/A

CONTACT PERSONS

Ricardo Rivera, Assistant Superintendent for Operations

Adrian Hernandez, Coordinator for Project & Energy Management

SUBJECT: Consideration and Approval of Procurement Method, Selection Criteria, Review and Ranking Committee, Wage Rate, and Authorization to Seek Proposals/Bids for Supplemental Repairs (Visitors Side) for the Tom Landry Stadium Project

PRESENTER: Ricardo Rivera
Assistant Superintendent for Operations

BACKGROUND INFORMATION

STADIUM:

Tom Landry Stadium was built in approximately 1976 and additional seating was installed in approximately 1989. It currently has only four (4) handicap seating spaces on both the home and visitors' side. The home side has a seating capacity for 5000 persons and the visitor's side has a seating capacity for 4000 persons.

At the Regular Board of Trustees meeting held on Wednesday, August 11, 2010 the Board approved a structural assessment to be conducted by Rick Hinojosa Structural Engineering. A report was completed on August 27, 2010. No further action was taken.

At a football game on September 26, 2013 and at the Regular Board of Trustees meeting of Wednesday, October 09, 2013, a concerned citizen brought to attention the fact that Tom Landry Stadium was not in compliance with the American Disabilities Act (ADA) current code concerning the required handicap seating spaces. As per ADA the breakdown for seating is 6 spaces for 1 – 500 seats then 1 seat for every 150 additional seats. As per calculations required additional seating on the home side will be 36 ADA seats and, on the visitors, side will be an additional 30.

On October 08, 2013 I contacted Mr. Tim Petty, Program Specialist V with the Texas Education Agency (TEA) to discuss this issue and he confirmed that we were not in compliance with current codes and standards concerning stadium seating.

At the Regular Board of Trustees meeting held on Wednesday, December 11, 2013 and after consultation with our legal counsel, the Board approved for renovations to the Tom Landry Stadium Press Box and for the additional required ADA stadium seating.

The current press box is approximately 30 years old and has never been renovated. When new bleacher seating was installed the press was moved by crane to its current location. With the installation of a new scoreboard additional staff will need to be placed in the press box to operate the system. Currently approximately nine persons are in the box, however, it is now estimated that up to twenty-two persons may be in the box at any given time. This added weight along with the additional weight of chairs and equipment may cause a stress on the structure. As per our legal counsel, there is no legal law that states that the structure needs to be evaluated, however, for safety precautions Administration is considering a structural assessment study to be conducted on the press box to ensure that the structure is capable of sustaining the additional weight.

At the Regular Board of Trustees meeting held on Wednesday, March 20, 2013 Administration presented and the Board approved Consideration and Approval to Contract with Rick Hinojosa Engineering for a Re-Assessment of the Tom Landry Stadium Press Box.

At the Regular Board of Trustees meeting held on Wednesday, April 10, 2013 the Board was advised that due to concerns and possible code regulations requiring an elevator to be installed for the press box, inquiries were made to Mr. David Hansen, Legal Counsel. As per building code an elevator is required should the square footage of a press box be larger than 500 sq. ft. Our current press box is approximately 40' X 8' which is 320 sq. ft.. However, should only renovations be required without the addition of sq. footage the initial structural assessment will need to be considered. Furthermore, it is the responsibility of the structural engineer to make the decisions of what is currently within building codes and regulations even if it is only renovations. The possible recommendation of constructing adjacent press boxes may still require an elevator to be installed. The sq. footage requirement applies to the "aggregate" total sq. footage of all press boxes. Again, it will be the responsibility of the structural engineer to make that determination. Renovations to include floor support, the construction of an interior wall, counter tops, sliding windows.

At the February 05, 2014 Facilities Committee meeting, a presentation by Rick Hinojosa Structural Engineering stated that current plans to improve the press box must include the installation of an elevator or a ramp access to the press box as per the State of Texas current code. At this meeting the committee decided to cancel the press box renovation project.

At the Special Board of Trustees Meeting held on Wednesday, April 20, 2016, the Board approved the following:

Administration is again exploring the possibility of a stadium renovation to include a new press box, new reserve section seating with back rests, new concession stands, new concrete base under the bleachers along with new bleachers to meet current ADA rules and regulations. New bleachers to also include those at Leo Najó Baseball Park.

Administration is requesting approval to advertise for Request for Qualifications (RFQ's) for architectural/civil engineer services as the recommended process for the selection.

The ranking of Request for Qualifications responses must be on the basis of demonstrated competence, qualifications, capability to perform, the past performance of the firm and members of the firm, and other appropriate factors submitted by the firm in response to the request for qualifications, except that cost-related or price related evaluation factors are not permitted as provided by Section 2254.004, Government Code.

If approved, Administration will begin advertising for architects and then begin the process of reviewing the firms as per the RFQ's and schedule presentations for the Board to review and possibly select a firm.

Advertisements for Request for Qualifications (RFQ's) for architects were advertised in the local newspaper on Wednesday, June 1st and June 8th, 2016 along with being posted on the MCISD website. RFQ's were due at Central Office on Thursday, June 23, 2016 at 2:00 p.m...

Three (3) architectural firms submitted an RFQ and they were reviewed for completeness and adherence to the instructions of the request by Mr. Roosevelt Rios, Purchasing

Coordinator and Ms. Tammy Tijerina, Project Manager on Thursday, July 28, 2016. The firms are listed below:

PBK Architects GIGNAC &
Assoc.
Alvarado Architects

This agenda item and presentation(s) were originally scheduled for Wednesday, August 03, 2016, however, they were postponed for a later date and time.

At the Facilities/Environment Committee held on Wednesday, August 24, 2016, the three ranked firms were invited to make a presentation to a Special Facilities/Environment Committee meeting and those Board members in attendance. The Committee allowed the firms a 15-minute presentation session along with a 15-minute question and answer session. The Committee along with Mr. Ricardo Rivera evaluated and ranked the firms on the basis of demonstrated competence and qualifications pursuant to the Professional Services Procurement Act as per the presentations. The rankings were then presented at the Special Board of Trustees meeting for consideration and approval for the selection of services.

At the Special Board Meeting held on Wednesday, August 24, 2016, the Board approved the rankings and selection of Alvarado Architects for services for the Tom Landry Stadium Renovations Project.

At the Regular Board Meeting held on Wednesday, September 14, 2016, the Board approved the contract for Alvarado Architects for the Tom Landry Stadium Renovations Project.

At the Regular Board Meeting held on Wednesday, November 09, 2016, the Board approved the project and budget, the procurement method and Alvarado Architects request of Schematic Design and Design Development for the Tom Landry Stadium Renovations Project. Alvarado Architects, District Staff and Coaches have been working on the design due to the extremely tight timeline, this project has to be completed by late July 2017. Current design will have new concession stands, new parking, new parking over-lay where needed, concrete area below home side, new stadium fascia, new complete seating bleachers at both home and visitor side, home side reserved seating to have back rests, seating and ramps to be ADA compliant, new ticket booths, press box with elevator as recommended design, new stadium lighting as required along with other required items needed for the project.

At the Regular Board meeting held on Wednesday, December 14, 2016, the Board approved Alvarado & Associates final design and Approval for 24-inch-Wide Seats in the Reserved Section for the Tom Landry Stadium Renovations Project.

Advertisements in the local newspapers and at the Association of General Contractors Office (AGC) were posted on December 18, 2016 and December 25, 2016 for the new design. A pre-proposal meeting was held on Tuesday, January 10, 2017 at 2:00 P.M. at Central Office.

Proposals were publicly opened on Tuesday, January 17, 2017 at 4:00 P.M. at Central Office. Pre-ranking of the proposals were conducted by Mr. Roosevelt Rios, Mr. Albert Rodriguez and Mr. Adrian Hernandez, Project Manager on Tuesday, January 17 and Wednesday, January 18, 2017.

At the Facilities Committee meeting the Committee reviewed the pre-ranking of firms and then proceeded to officially rank the firm's proposals. These rankings will then be presented to the Board of Trustees for consideration and approval for entering into negotiations in the order of ranking recommended at a special called meeting on Monday, January 23, 2017 at 7:30 a.m.

Pre-ranking of proposals by Administration is merely a district process to pre-check if all requested documents and information in the Request for Proposals (RFP) was submitted prior to the Evaluation and Selection Committee formal evaluation. The pre-ranking of proposals is strictly unofficial. The Request for Proposal (RFP) package includes document CSP – 00350 Evaluation and Selection Criteria for Competitive Sealed Proposals which defines this portion of the procurement process. The District Evaluation and Selection Committee is comprised of three (3) Board of Trustees Facilities Committee Members and one (1) appointed Administration Staff. The Evaluation and Selection Committee will evaluate, rank and publish all proposals. The Evaluation and Selection criteria has been approved by the Mission C. I. S. D.'s Board. Once the M. C. I. S. D. Board of Trustees approves the ranking, the District Evaluation and Selection Committee will then proceed to negotiate a contract with the highest-ranking Proposer.

The Finance department in conjunction with the districts finance consultants have been designing a funding package for this project. In order to ensure this project under this funding source be securely financed Administration is recommending to adjust the contingency budget by an increase of \$2 million. Thus, the total construction budget to include all soft-costs will not exceed \$10 million.

Three proposals were submitted for this project and were ranked by the Facilities Committee as per MCISD guidelines and procedures. The Board must now consider the rankings and approve to enter into negotiations with the top ranked firms in the order selected. Rankings listed below:

<u>Company</u>	<u>Base Proposal</u>	<u>Alt. #1</u>	<u>Days</u>
Holchemont Const. (291)	\$7,463,000.00	(\$287,000.00)	235
E-Con Const. (287.6)	\$7,450,000.00	\$210,000.00	180
Central Builders (260.2)	\$8,000,000.00	\$500,000.00	180

Note:

Alternate #1 is for a larger custom-built press box of which Administration recommends approving. Both E-Con Construction and Central Builders have an additional cost for this alternate, as per Holchemont Construction their base bid includes the larger custom press box. Should MCISD select the smaller pre-fabricated press box Holchemont has a \$287,000.00 deduct from their base bid. The intention is for a notice to proceed (NTP) to be issued on or before February 01, 2017 with a substantial completion date of July 31, 2017, which is 180 days, Holchemont has a substantial completion date of September 24, 2017. Proposals and days are all prior to negotiations.

At a Special Board of Trustees meeting to be held on Monday, January 23, 2017, the Board will consider and possibly approve the rankings to allow negotiations to begin. It is Administrations intent to bring forward at the Regular Board of Trustees meeting to be held on Wednesday, January 25, 2017 an approval and recommendation for a best and final offer (BAFO) and to enter into contract with the selected general contractor. It is MCISD's construction procurement process to present all items for Facilities Committee discussion prior to presenting to the Board of Trustees for final approval.

At the Regular Board of Trustees meeting held on Wednesday, January 25, 2017, the board approved the best and final offer (BAFO) from Holchemont in the amount of \$7,463,000.00 with alternate #01 custom press box included as part of the contract. Notice to proceed (NTP) was issued on February 02, 2017 with a substantial completion date of August 21, 2017.

At the Regular Board of Trustees meeting held on Wednesday, April 12, 2017, the board approved and pulled the following items:

Consideration and Approval of AEA #01 for CPR #02 to Furnish and Install Sports Lighting for the Tom Landry Stadium Renovations Project.

Sports Lighting Allowance:	\$600,000.00 AEA #01
Sports Lighting:	<u>\$580,392.00</u>
Balance:	\$ 19,608.00

Consideration and Approval of AEA #02 for CPR #03 to Furnish and Install a Scoreboard Sound System for the Tom Landry Stadium Renovations Project. Item was pulled for further pricing on additional speakers throughout the stadium.

Consideration and Approval of AEA #03 for CPR #04 to Furnish and Install Football Safety Netting System for the Tom Landry Stadium Renovations Project. Item was pulled due to MCISD having the netting and poles and only required pricing for the installation.

Consideration and Approval of AEA #04R to "Credit" the Allowances for the Tom Landry Stadium Renovations Project. Item was pulled due to other items being pulled thus not being able to present an accurate balance total.

Consideration and Approval of CPR #06 to Change the Size of the Bronze Statue for the Tom Landry Stadium Renovations Project.

Bronze Statue Allowance:	\$ 50,000.00
CPR#06 Bronze Statue:	<u>\$129,400.00</u>
Bronze Statue Allowance Balance:	(\$ 79,400.00)

Due to inclement weather in the month of March Holchemont Construction requested additional delay days, thus, they presented Consideration and Approval of CPR #09 for Seven (7) Delay Days for the Tom Landry Stadium Renovations Project. The new substantial completion date is August 28, 2017.

Administration presented Consideration and Approval of Selection of Color and Pattern for the Reserved Seating on Home Side for the Tom Landry Stadium Renovations Project. The Board approved option #1 alternating colors.

At the Regular Board of Trustees meeting held on Wednesday, May 10, 2017, the Board approved and pulled the following items:

Contingency Allowance:	\$100,000.00
AEA #01 Sports Lighting:	\$ 19,608.00
CPR #6 Bronze Statue:	<u>\$ (79,400.00)</u>
Contingency Balance:	\$ 40,208.00

Consideration and Approval of AEA #03R for CPR #04 to Furnish and Install Football Safety Netting System for the Tom Landry Stadium Renovations Project.

Football Safety Net System Allowance:	\$10,000.00
AEA#03 Football Safety Net System:	<u>(\$ 7,500.00)</u>
Balance:	\$ 2,500.00

Consideration and Approval of CPR #08 to Construct a Riser Room / Fire Pump for the Tom Landry Stadium Renovations Project.

Fire Suppression Pump Allowance Balance:	\$ 50,000.00
CPR # 08 Riser Room:	<u>\$ 110,428.53</u>
Balance:	(\$ 60,428.53)

Contingency Balance:	\$40,208.00
CPR #8 Riser Room:	(\$60,428.53)
Plus, Overhead and Profit	<u>(\$2730.47)</u>
Contingency Balance:	(\$22,951.00)

Due to inclement weather in the month of April and MCISD testing Holchemont Construction requested additional delay days, thus, they presented Consideration and Approval of CPR #09 for Eight (8) Additional Delay Days for the Tom Landry Stadium Renovations Project. The new substantial completion date is September 05, 2017.

Note: The first scheduled football game is for Friday, September 01, 2017 with VMHS vs Harlingen. Substantial completion is granted when the facility can be utilized for its intended use. The City of Mission Fire Marshal must approve the facility to include all fire systems are inspected and tagged "approved" along with all ADA inspections and approvals and to include the inspection and approval of the elevator system and to include any other inspections required. Coaches are working on a Plan "B" should the stadium not be completed on time.

Administration recommended Consideration and Approval of Re-naming for the Tom Landry Stadium Renovations Project as "Tom Landry Hall of Fame Stadium".

Administration recommended Consideration and Approval of Selection of Color for Reserved Seating on Home Side for the Tom Landry Stadium Renovations Project.

Recommendation is based on the colors selected by Coach Detmer, Coach Gilpin, Athletic Director Joe Sanchez and Athletic Director Leticia Ibarra.

Royal Blue
Texas A&M – Maroon

After a lengthy discussion on possible color dis-coloration of the royal blue and maroon seats the Board approved “grey” for the reserved seating.

Alvarado Architects presented a “pose” selection on the statue. At the Facilities Committee meeting held on Wednesday, May 03, 2017, the Committee along with members of the Campus Construction Over-Sight Committee members reviewed and discussed the five (5) options of poses brought forward by Mr. Alvarado. By virtue of the discussion and by show of hands, options #1 and #4 were selected for presentation to the Board. The Board approved Consideration and Approval of Tom Landry Statue Pose for the Tom Landry Stadium Renovations Project Option #1.

At the Facilities/Environment Committee meeting held on Wednesday, June 07, 2017 several CPR’s were presented and discussed. These CPR’s may become change orders should current available allowances not cover the over-budget of the project when it is finalized. MCISD Administration stressed to Alvarado Architects and Holchemont Construction the discontent of change orders and requests for additional construction time. Administration stressed the importance of having the project completed as per the original substantial completion date.

At a Special Board of Trustees meeting held on Wednesday, June 07, 2017, the Board granted Superintendent Dr. Ricardo Lopez authority to approve change orders/change proposal request for the Tom Landry Stadium Renovations Project in the amount not to exceed a total of \$250,000.00. This action was to facilitate the change order/CPR process and not delay the general contractor waiting for a decision.

The following Change Orders/CPR’s were approved by Superintendent Dr. Ricardo Lopez on Wednesday, June 07, 2017:

Supt. Approval Balance:	\$250,000.00
CPR#05R Structural Steel:	\$ 31,824.00 CPR#06R
Bronze Statue Foundation:	\$ 12,161.00 CPR#11 for MEP
changes at the Press Box:	\$ 8,674.00 CPR#14 for HVAC at the Gift
Shop:	\$ 12,268.00 CPR#19 for Additional Gates for Eagle
Drive:	<u>\$ 1,816.00</u>
Supt. Approval Balance:	\$183,257.00

Consideration and Approval of CPR#05R for Structural Steel between Grandstands and Custom Press Box for the Tom Landry Stadium Renovations Project.

Contingency Balance:		(\$22,951.00)
Structural Steel Additions Cost:		<u>\$31,824.00</u>
Contingency Balance:	81	(\$54,775.00)

Consideration and Approval of CPR#06R for Bronze Statue Foundation and Base for the Tom Landry Stadium Renovations Project.

Contingency Balance:	(\$54,775.00)
Bronze Statue Base Foundation Cost:	<u>\$12,131.00</u>
Contingency Balance:	(\$66,906.00)

Consideration and Approval of CPR#11 for MEP changes at the Press Box for the Elevator for the Tom Landry Stadium Renovations Project. Holchemont, LTD is requesting eight (8) additional day, if approved, the new substantial completion date is September 13, 2017. As per Alvarado Architects additional days will not be submitted.

Contingency Balance:	(\$66,906.00)
Electrical at press box Cost:	<u>\$ 8,674.00</u>
Contingency Balance:	(\$75,580.00)

Consideration and Approval of CPR#14 for HVAC at the Gift Shop for the Tom Landry Stadium Renovations Project.

Contingency Balance:	(\$75,580.00)
HVAC at gift shop Cost:	<u>\$12,268.00</u>
Contingency Balance:	(\$87,848.00)

Consideration and Approval of CPR#19 for Additional Gates for Eagle Drive for the Tom Landry Stadium Renovations Project

Contingency Balance:	(\$87,848.00)
Gates at Eagle Drive Cost:	<u>\$ 1,816.00</u>
Contingency Balance:	(\$89,664.00)

At the Regular Board of Trustees meeting held on Wednesday, June 21, 2017, The Board did not approve Consideration and Approval of CPR#20 for Additional Four (4) Rain Days for the Month of May for the Tom Landry Stadium Renovations Project.

*Note: After meeting with Alvarado Architects and Holchemont LTD, they were advised that Administration will be questioning any further delay days submitted and that Holchemont should continue working on a recovery schedule plan to attempt to bring this project at the initial substantial completion date of August 21, 2017.

The following Change Orders/CPR's were approved by Superintendent Dr. Ricardo Lopez on Thursday, June 29, 2017 in order to have the project continue without contractor delays:

Supt. Approval Balance Granted:	\$183,257.00
CPR#12 Track Timing System:	<u>\$ 45,322.00</u>
Supt. Approval Balance:	\$137,935.00

Change Order Amount to Date:	(\$134,986.00)
------------------------------	----------------

Note: General Contractor has added 12% overhead and profit and 1.5% for project bonding on all change order amounts.

Soil Stabilization Allowance:	\$10,000.00
CPR #16 Soil Stabilization:	<u>\$10,000.00</u>
Balance:	\$ 0.00

Utility Allowance:	\$20,000.00
CPR #21 Boring & Trenching:	<u>\$16,830.00</u>
Balance:	\$3,170.00

At the Special Board of Trustees Meeting to be held on Thursday, July 27, 2017, Administration presented to the Board Consideration and Approval of CPR#15 for Graphics for the Tom Landry Stadium Renovations Project. This amount is to be taken from the graphics allowance already included in the original contract.

Graphics Allowance Balance:	\$100,000.00
Banner system:	(\$ 51,148.50)
Identification signage:	(\$ 26,815.00)
Bleacher section signage:	(\$ 13,625.00)
Traffic signage:	(\$ 2,136.00)
Fire lane striping:	<u>(\$ 3,700.00)</u>
Balance:	\$ 2,575.50

At the Regular Board of Trustees meeting held on Wednesday, August 09, 2017, the Board considered and approved some of the following items:

As per our Legal Counsel, the Board did not need to vote on agenda item, Consideration and Approval of Additional Seven (7) Delay Days for AEA#11 for CPR #21 for the Tom Landry Stadium Renovations Project which was previously denied but being brought forward by Holchemont, LTD. once again for consideration. The Board had stated it would possibly revisit this request and no action was taken.

Consideration and Approval of AEA#12 for CPR #22 for Landscaping and Irrigation for the Tom Landry Stadium Renovations Project.

Landscape/Irrigation Allowance:	\$20,000.00
CPR#22 Landscape & Irrigation:	<u>\$17,383.00</u>
Balance:	\$ 2,617.00

Consideration and Approval of AEA#13 for CPR #24 to Up-grade the Scoreboard System for the Tom Landry Stadium Renovations Project.

Scoreboard Sound System Allowance:	\$55,000.00
CPR#24 Scoreboard System:	<u>\$34,934.00</u>
Balance:	\$20,066.00

Consideration and Approval of CPR #23 for Speaker System for the Tom Landry Stadium Renovations Project. This agenda item⁸³ was pulled.

At the Regular Board of Trustees meeting held on Wednesday, September 13, 2017, the Board revisited and approved Consideration and Approval of Additional Seven (7) Delay Days for AEA#11 for CPR #21 for the Tom Landry Stadium Renovations Project. As of the date of this Board of Trustees meeting Holchemont LTD will be into possible liquidated damages as per contract of \$1,500.00 per day of not meeting the substantial completion date. Administration brought forward this request, the new substantial completion date is September 12, 2017.

At the Regular Board of Trustees meeting held on Wednesday, October 11, 2017, the Board took the following actions for the following items:

Consideration and Approval of CPR #12R3 for Additional Power for the Tom Landry Stadium Renovations Project. Please note that Holchemont, LTD will require and extra four (4) days. If approved, the new substantial completion date is September 16, 2017. This item was pulled until further review.

Note: MCISD does not agree with this pricing, however, there will be a cost associated with installing conduits within the concrete slab which was done earlier. If the revised pricing is not approved MCISD Maintenance will complete the electrical connections.

Contingency Balance:	(\$134,986.00)
CPR#12R3 for Additional Power:	<u>\$ 0.00</u> (Org. price \$10,134.42)
Change Order Amount to Date:	(\$134,986.00)

Consideration and Approval of CPR #12R5 for Additional Cabling for Track Timing System for the Tom Landry Stadium Renovations Project. Please note that Holchemont, LTD will require and extra fourteen (14) days. If approved, the new substantial completion date is September 30, 2017. This item was pulled until further review.

Contingency Balance:	(\$134,986.00)
CPR#12R5 Additional Cabling:	<u>\$ 0.00</u> (Org. price \$54,468.65)
Change Order Amount to Date:	(\$134,986.00)

Consideration and Approval of CPR #17 to "Credit" Two (2) Wireless Access Points, Shortel Phone and Video Server for the Tom Landry Stadium Renovations Project. This item was approved.

Contingency Balance:	(\$134,956.00)
CPR#17 "Credit" on Technology:	<u>\$ 5,000.00</u> "Credit"
Change Order Amount to Date:	(\$129,986.00)

Consideration and Approval of CPR #18 to "Credit" Fire Alarm and Intrusion Systems for the Tom Landry Stadium Renovations Project. This item was approved.

Contingency Balance:	(\$129,986.00)
CPR#18 "Credit" Fire Alarm System:	\$ <u>2,800.00</u> "Credit"
Change Order Amount to Date:	(\$127,186.00)

Consideration and Approval of CPR #25 to Relocate Cross Bracing at Concession Stands for the Tom Landry Stadium Renovations Project. This item was approved with the cost change to \$5,221.00

Contingency Balance:	(\$127,186.00)
CPR #25 to Relocate Cross Bracing:	\$ <u>5,221.00</u> (Org. price \$10,442.00)
Change Order Amount to Date:	(\$132,407.00)

Consideration and Approval of CPR #26 to Remove and Replace Concrete from the Ramps for the Tom Landry Stadium Renovations Project. Please note that Holchemont, LTD will require and extra two (2) days. If approved, the new substantial completion date is October 2, 2017. This item was pulled, Javier Hinojosa Civil Engineer will take care of this item.

Contingency Balance:	(\$132,407.00)
CPR #26 to Remove and Replace Concrete:	\$ <u>0.00</u> (Org. price \$4,483.25)
Change Order Amount to Date:	(\$132,407.00)

Consideration and Approval of CPR #27 to Add IDF Rack, Quad Receptacles and Data Drops on the Visitor's Side Bleachers for the Tom Landry Stadium Renovations Project. Please note that Holchemont, LTD will require and extra three (3) days. If approved, the new substantial completion date is October 5, 2017. This item was pulled, MCISD will take care of this item.

Contingency Balance:	(\$132,407.00)
CPR #27 to Add IDF Rack:	\$ <u>0.00</u> (Org. price \$18,357.49)
Change Order Amount to Date	(\$132,407.00)

Consideration and Approval of CPR #29 for Additional Eleven (11) Delay Days for the Tom Landry Stadium Renovations Project. If approved, the new substantial completion date is October 16, 2017 pending all other CPR's being submitted. The Board took no action on this item.

Consideration and Approval to Grant Administration Authority to Approve Substantial Completion for the Tom Landry Stadium Renovations Project. Dr. Lopez, Superintendent will have the authorization. This item was approved.

Note: No additional delay days were approved at this meeting. Substantial completion continues to be approximately September 12, 2017.

At the Regular Board of Trustees meeting held on Wednesday, November 08, 2017, the Board took the following actions for the following items:

Consideration and Approval of CCD#01 for CPR#30 for Modifications to the Elevator Equipment Room for the Tom Landry Stadium Renovations Project. No additional days were approved.

Contingency Balance:	(\$132,407.00)
CCD#01/CPR#30 Elevator Equipment Room:	<u>\$ 3,957.00</u>
Change Order Amount to Date	(\$136,364.00)

Consideration and Approval of CPR#31 to "Credit" for Use of Owners Utilities for the Tom Landry Stadium Renovations Project. MCISD presented a "credit" for \$5,900.00, however, Holchemont offered only a credit amount of \$900.00.

Contingency Balance:	(\$136,364.00)
CPR#31 Use of Owners utilities:	<u>\$ 5,900.00 "Credit"</u>
Change Order Amount to Date:	(\$130,464.00)

Consideration and Approval of CPR#32 for HVAC Test and Balance for the Tom Landry Stadium Renovations Project.

Test and Balance Allowance:	\$5,000.00
CPR#32 HVAC Test & Balance:	<u>\$2,500.00</u>
Balance:	\$2,500.00

Consideration and Approval of CPR#33 for Two (2) Additional Fire Extinguishers for the Tom Landry Stadium Renovations Project.

Contingency Balance:	(\$130,464.00)
CPR#33 Fire Extinguishers:	<u>\$ 268.00</u>
Change Order Amount to Date	(\$130,732.00)

At the Regular Board of Trustees meeting held on Wednesday, December 13, 2017, the Board took the following actions for the following items:

Consideration and Approval of CPR #12R3 for Additional Power for the Tom Landry Stadium Renovations Project. This item was approved.

Contingency Balance:	(\$130,732.00)
CPR#12R3 additional power:	<u>\$ 6,327.00</u>
Balance:	(\$137,059.00)

Consideration and Approval of CPR#34 for "Credit" for the VIP Chair Allowance for the Tom Landry Stadium Renovations Project. VIP Chair Allowance "Credit" is \$5000.00. This item was approved.

Discussion and Possible Action on Paving Repair Schedule for the Tom Landry Stadium Renovations Project.

Consideration and Approval for Final Completion, Less Betterment Fund Allowance and Final Payment, Less Liquidated Damages for the Tom Landry Stadium Renovations Project. This item was pulled due to punch list items and other contractual obligations were noncompliance.

At the Regular Board of Trustees meeting held on Wednesday, April 11, 2018 the Board took the following actions for the following items:

Consideration and Approval of CPR#23 for Sound System Raceways for the Tom Landry Stadium Renovations Project. Holchemont LTD is requesting fourteen (14) additional delay days for this work, if approved the new substantial completion date is September 26, 2017.

Contingency Balance:	(\$137,059.00)
CPR#23 for Sound System:	<u>\$ 39,839.37</u>
Balance:	(\$176,898.37)

Consideration and Approval of Grievance Agreement for Use of Owners Utilities for the Tom Landry Stadium Renovations Project. As per the November approved CPR #31, MCISD approved an owner's credit for utility use of \$5,900.00. As per grievance agreement the amount was reduced to \$2,350.00, thus an adjustment needed to be made.

Previous: \$5,900.00
Final approved as per Grievance: \$2,350.00
Adjustment: \$3,550.00

Contingency Balance:	(\$180,448.37)
----------------------	----------------

Discussion and Possible Legal Action Regarding Parking Lot Repairs for the Tom Landry Stadium Renovations Project. At this time the Board invoked the "Self Help Provision" of the contract authorizing Administration to make necessary parking lot repairs utilizing a different contractor.

2GS and Earthworks re-paving Cost: \$24,700.00 - Parking Lot Re-paving completion date was achieved on August 06, 2018.

At the Regular Board of Trustees meeting held on Wednesday, May 08, 2019, the Board took no action on the following item: Consideration and Approval for Final Completion, Less Betterment Fund Allowance and Final Payment, Less Liquidated Damages for the Tom Landry Stadium Renovations Project. At this meeting Administration also recommended to authorize Administration and Dr. Perez to approve final completion at a later time, this was rejected with direction from the Board that they wanted this brought forward when the time came for consideration and approval.

At the Regular Board of Trustees meeting held on Tuesday, June 11, 2019 the Board took the following actions

Administration, Mr. Eli Alvarado, Architect, and Mr. Michael Montalvo, General Contractor have met six times since April 25, 2019 with the latest meeting held on Tuesday, June 04,

2019, to discuss what is required from all parties to bring this project for final recommendation and to possibly come to a mutual agreement and present to the Board of Trustees Consideration and Approval for Final Completion, Less Betterment Fund Allowance and Final Payment, Less Liquidated Damages for the Tom Landry Stadium Renovations Project. At the latest meeting Mr. Montalvo was not able to attend and for many of these meetings Dr. Perez, Superintendent was present. A 1 ½ year warranty project walk-through was conducted as per contract specifications on Friday, May 03, 2019 with Mr. Alvarado, his design staff, Mr. Montalvo, his sub-contractors and MCISD personnel present to identify any warranty items that are still pending and need correction. The meetings that are being conducted are to balance and agree on all financial/accounting matters and pending correction of work if applicable. Any matters that concern additional request for time or matters that may concern any deduction from the remaining balance owed to the contractor such as additional fees/costs or possible liquidated damages incurred the general contractor will need to follow the process as written in his contract.

As noted, Administration and Alvarado Architects believes it has tried, with due diligence, to work on all pending accounting/fiscal matters with Mr. Montalvo, however, we continue to not agree on a mutual amount. Administration presents Discussion with Legal Counsel Regarding Closeout for the Tom Landry Stadium Renovations Project with MCISD processing any possible pay applications to Holchemont Construction with monies being withheld that are not in contention.

Note: Additional structural assessment is continuing by Rick Hinojosa, Structural Engineering and is pending completion. They are pending additional concrete test results.

Tom Landry Stadium Project Timeline:

Notice to Proceed (NTP) – 02/01/2017
Original Substantial Completion Date – 08/21/2017
36 delay days Board approved due to testing, weather, change orders
New substantial completion date – 09/26/2017
Approved substantial completion date – 11/10/2017 (45 days late)
Original Final Completion Date – 12/10/2017
New Final Completion Due Date – 04/20/2018 (131 days late)

Possible LD's for not meeting Subst. Completion: 45 days X \$1,500.00 = \$67,500.00
Possible LD's for not meeting Final Completion: 131 days X \$500.00 = \$65,500.00
Possible LD's for delay in re-paving of parking lot: 7 days x\$500.00 per day = \$3,500.00

Possible LD's Incurred: \$136,500.00

Other Possible Fees/Costs:

Re-paving of parking lot = \$24,700.00
Structural Engineering cursory inspection = \$5,000.00 (Rick Hinojosa, Structural Engineering)
Hinojosa full structural assessment = \$30,000.00 (if applicable)
TDLR re-inspections = \$285.00

Terracon Structural additional services = \$15,000.00
Pending "credit" for three (3) parking lot poles not installed = \$53,489.08

Approximate Possible Total Amount of addtl. fees/costs: \$128,474.08

Additional Architect Fees: \$85,695.00 (if applicable/pending)

Balance on contract:	\$416,406.11	
Possible LD's:	\$136,500.00	Possible
addtl. Costs:	\$128,474.08	
Possible addtl. Arch. Fees:	\$ 85,695.00	
Paid Holchemont:	\$ 43,189.25	(07/24/19 Pay App. #10 rev.3)

Est. Current Balance on Contract: ~~\$380,251.23~~ as of 04/21/2021 \$347,206.23

Est. Construction Costs:	\$6,000,000.00
Est. Total Construction w/Soft Costs:	\$8,000,000.00

BAFO Const. Cost:	\$7,463,000.00
Change Orders:	<u>\$ 142,020.37</u>
Final Const. Cost:	\$7,605,020.37

Architect Fees:	\$485,095.00	6.5% of Construction Cost
Addtl. Arch. Fees for C/O's:	<u>\$9,231.32</u>	
Architect Fees:	\$494,326.32	(excluding addtl. Fees pending)

At the Regular Board of Trustees meeting held on Wednesday, August 14, 2019 the Board took the following actions.

At this meeting the Mr. Rick Hinojosa Structural Engineering Assessment report was not available for the Board of Trustees to review, however, Administration had preliminary verbal discussions with Hinojosa on what he was to submit, the report was to be finalized on Friday, August 16, 2019. Should the report state that repairs were required Administration presented Consideration and Possible Action Regarding Procurement of Design and Construction Services for the Tom Landry Stadium Repairs in advance.

After conducting field reviews and inspections Mission CISD contracted with Rick Hinojosa Structural Engineering to conduct a third party Visual Cursory Observation on the bleachers for the visitor's side of Tom Landry Stadium. On September 06, 2018 the observation report with conclusions and recommendations was submitted. In brief, Hinojosa stated that the cracked piers did not affect the immediate load carrying capacity of the structure and the stadium could be used. However, the recommendations were to conduct a complete assessment of all piers and repair all necessary items addressed in the complete assessment.

Administration was approved to contract with Hinojosa to conduct a full stadium assessment to include not only concrete piers but to inspect the entire structure of the

stadium. On August 08, 2019, Hinojosa Engineering submitted a preliminary assessment letter for our review noting possible reinforcement required.

On August 16, 2019, Hinojosa Structural Engineering submitted their Visual Structural Condition Assessment of Tom Landry Stadium for our review.

At the September 11, 2019 Regular Board of Trustees meeting and based on Mr. Hinojosa's report, Administration presented Consideration and Approval of Design and Construction Services for the Tom Landry Stadium Repairs.

The Board of Trustees must take the necessary action in accordance with Texas Education Code 44.035 which consisted of the selection/designation of an architect and/or engineer to prepare construction documents for this project. The engineer and/or architect selected or designated will have full responsibility for complying with the Texas Engineering Practice Act (Article 3271a, Vernon's Texas Civil Statutes) or Chapter 478, Acts of the 45th Legislature, Regular Session, 1937 (Article 249a, Vernon's Texas Civil Statutes) as applicable.

If the engineer or architect is not a full-time employee of the District, the Board must select the engineer or architect on the basis of demonstrated competence and qualifications as provided by Section 2254.004, Government Code. The selected architect/engineer along with preparing construction documents will be required to provide MCISD with an estimated project budget.

Current and/or past structural engineers that have worked with MCISD are listed below, the Board of Trustees may select from one of these engineers on the basis of demonstrated competence and qualifications or may direct Administration to seek for Request for Qualifications (RFQ's) on an engineer or architect.

Rick Hinojosa Structural Engineering (conducted assessments)
Chanin Structural Engineering (original project structural engineer)

The Board of Trustees selected Mr. Rick Hinojosa Structural Engineering to conduct a thorough third-party structural assessment of the Tom Landry Stadium Project.

On or about January 27, 2020, Mr. Hinojosa submitted to Administration a proposal for forensic engineering services from MEG Engineers. The Forensic Engineering Services will include Ground Penetrating Radar (GPR) Scans of one-hundred and fifty-six (156) piers by scanning four (4) grids at each pier location. A grid will consist of a three (3) foot by two (2) foot rectangle made up of thirty-five (35) gridlines spaced at six (6) inches on center. Total linear footage of scanning will be eighteen thousand and ninety-six (18,096) feet. The report will include detailed rebar locations of the piers. The proposal cost for this service was \$56,000.00.

At the Facilities/Environment Committee Meeting of February 05, 2020 this proposal and engineering service was presented and discussed. At this time the decision was made for Administration to proceed with Hinojosa Structural Engineering and MEG Engineers to conduct only seventy-eight (78) GPR Scans on the stadium. These scans would be divided between the home and visitors side piers at a proposal cost of \$34,988.00.

At the Regular Board of Trustees meeting held on April 08, 2020 the Board approved the following, Preliminary reports from both engineering firms indicate that a complete GPR Scan of all piers would be advisable to have a complete pier assessment on the stadium. Thus, Administration recommends Consideration and Approval of Additional Ground Penetrating Radar (GPR) Scans for Piers at the Tom Landry Stadium Bleacher Project. The estimated proposal cost would be the difference from the original proposal to what has been approved for the first phase. Estimated proposal \$21,012.00.

At the Regular Board of Trustees meeting held on September 09, 2020, as an informational Board Item, a presentation was given by Rick Hinojosa Structural Engineering, Mr. Albert Trevino, on the Tom Landry Stadium Renovation Project status. Mr. Trevino reported on the findings for the GPR scans conducted and has stated, "the scans in the report indicate that the majority of the piers do not have pier reinforcement per the shop/erection drawings provided by Sturdy Steel who provided the bleachers".

At the meeting of September 09, 2020, Hinojosa Structural Engineering was to provide a final and complete comprehensive report on the findings and recommendations for correction on all items indicated on the assessment. Findings and recommendations were to include and not limited to the disciplines of Structural, Mechanical, Electrical, Plumbing (MEP) and Civil. At this meeting Hinojosa Structural Engineering was directed to provide this comprehensive report and not only the GPR scans report.

Since this initial directive, Hinojosa Structural Engineering has been contacted both on October and December 2020 for the final report and we continue to have no response. Administration will continue to utilize all avenues to request the final report so that we may move forward with repairs required.

On January 14, 2021, Rick Hinojosa Structural Engineering was sent both an email correspondence and a certified letter requesting his personal appearance at the Wednesday, January 20, 2021 Board of Trustees Work Shop to present the final project findings. At 4:01 p.m. on that day Mr. Hinojosa contacted us that he had a family emergency and would try to attend. With this correspondence he attached "Mission CISD Tom Landry Stadium Ground Penetration Radar (GPR) Scanning Findings Letter". This letter referenced the GPR scanning done at the stadium.

In discussion at the Work Shop of January 14, 2021, the Board instructed our legal counsel to draft a letter to request Mr. Hinojosa's presence and to once again present his findings at the Board Work Shop of Wednesday, February 03, 2021. Legal counsel sent a certified letter and emailed the letter to Mr. Hinojosa's attention on Tuesday, January 26, 2021. My office then proceeded to re-send this letter to Mr. Hinojosa the following day. A "read receipt" message was received from his office on Friday, January 29, 2021 at approximately 12:10 p.m. acknowledging receipt of our request to be present.

At this Work Shop of Wednesday, February 03, 2021, the Board will hear the presentation and may have a question and answer session with Mr. Hinojosa on the findings and recommendations. At this time the Work Shop may have a Discussion and Possible Action to Procure Engineering Services for Analysis and Remediation for the Tom Landry Stadium Project and to Grant Administration Authorization to Procure Services. The

presentation was not held at the Work Shop and was presented at a Special Board of Trustees Meeting after.

At the Special Board of Trustees meeting of Wednesday, February 03, 2021, Mr. Rick Hinojosa presented his "Mission CISD Tom Landry Structural Comprehensive Assessment Report". After discussion with the Board of Trustees and Administration, Mr. Hinojosa was directed to once again present at the Regular Board of Trustees meeting of Wednesday, February 10, 2021. This presentation is to mainly address all the viable options on how to correct the issue of the piers found to be not safe and not constructed as per code as noted in the report and reported by Mr. Hinojosa at the meeting. He is to also present a scope of work and a phasing plan of repairs beginning with the most safety critical items. What will also need to be addressed is if any other areas will be damaged while repairing the piers, such as the flatwork. Each option(s) will need to satisfy all building and structural codes along with satisfying all safety compliance codes. At this meeting Mr. Hinojosa was advised that time was critical for the usage of the stadium since graduation ceremonies have already been scheduled. Mr. Hinojosa stated that plans and specifications should be finalized soon and we may be able to advertise for competitive sealed proposals (CSP's) within the next couple of weeks and possibly have a contractor begin repairs as quickly as the procurement process allows, that is the goal.

The procurement process will be Competitive Sealed Proposals (CSP's) of which the Board adopted as the method of delivery. The Board approved the Hidalgo County Prevailing Wage Rate of which is an exhibit and was attached. The Board also adopted the selection criteria of which proposals are evaluated and ranked. Administration also recommended that the Board authorized the Superintendent to rank the proposals and to negotiate an agreement with the highest ranked contractor.

On February 10, 2021, the Board approved Consideration and Possible Action Regarding Permanent and Emergency Repairs for the Tom Landry Stadium to Include the Wage Rate, Selection Criteria, and Authorization to Dr. Perez as mentioned under the Administrative considerations.

Advertisements in the local newspapers for Competitive Sealed Proposals (CSP's) were posted on March 24, 2021 and March 31, 2021. Proposals were to be opened April 08, 2021 and firms would be able to view remotely. The virtual pre-proposal meeting was Thursday, April 01, 2021 at 2:00 p.m. to allow all prospective contractors the opportunity to ask questions concerning the project plans and specifications.

CSP's were to be submitted on April 8, 2021, and were to be reviewed and ranked by the Administration Committee. This Administrative review was to be presented at the Regular Board of Trustees Meeting of Wednesday, April 14, 2021.

On Wednesday, April 06, 2021 Hinojosa Structural Engineering submitted a recommendation to extend the bid date by two weeks to allow contractors and sub-contractors more time to bid on the project. He also stated that a second pre-bid conference be held followed by a walk-through of the stadium facility. This recommendation was due also to no contractors attending the initial pre-bid conference. This recommendation was presented at the Board of Trustees Work Shop on Wednesday, April 08, 2021.

A second pre-proposal meeting was held on Thursday, April 15, 2021. With the two-week extension proposals were due and publicly opened on Thursday, April 22, 2021 at 2:00 p.m. at the Central Office Board Room. Proposals were reviewed, evaluated and ranked on Monday, April 26, 2021 at 2:00 p.m. by Ms. Rimalda Ruiz, Ms. Dora Garcia, Ms. Lorena Garcia, Mr. Joel Garcia and Mr. Ricardo Rivera with Ms. Daisy Cuevas assisting.

Due to the timeline to begin permanent repairs Administration requested a Special Board of Trustees meeting on Tuesday, April 27, 2021 at 12:00 p.m. at the Central Office Board Room. At this meeting Administration presented and the Board approved Consideration and Approval to Accept Administrations Rankings and Enter Into Negotiations in the Order of Ranking for the Tom Landry Stadium Repairs Project.

G & G Construction

Base Bid: \$1,024,850.00 with 210 construction days

Alternate Bird Screen: \$127,000.00 with an additional 45 construction days

TOTAL: \$1,151,850.00 with 255 days from notice to proceed (approx. 8.5 months)

Terra Fuerte Const.

Base Bid: \$1,141,000.00 with 180 construction days

Alternate Bird Screen: \$30,000.00 with an additional 30 construction days

TOTAL: \$1,171,000.00 with 210 days from notice to proceed (approx. 7 months)

Project negotiations were scheduled for Wednesday, May 05, 2021 at 10:00 a.m. as per G & G Constructions earliest available meeting date and time. Administration presented Consideration and Approval to Accept the Best and Final Offer (BAFO) and to Enter Into Contract for the Tom Landry Stadium Repairs Project and requested for a Special Board of Trustees meeting following the Board Work Shop to consider action on this item.

The Board of Trustees has the option to accept this BAFO, the initial base proposal, to decline the offer and direct Administration to enter into negotiations with the next contractor or to reject all offers and re-advertise for the project using the same specifications and design or direct the engineer to re-design the project.

At the Special Board meeting held on May 5, 2021, the Board approved G & G Contractors Best and final offer Base Bid: \$1,024,850.00 with 210 construction days. Notice to proceed was effective July 28, 2021, with substantial completion will be February 23, 2022.

At the Regular Board meeting held on November 10, 2021, the Board approved the following items:

Consideration and Approval of Allowance Expenditure Authorization (AEA) #01 for Structural Repairs on Various Piers for the Tom Landry Stadium Repairs.

Contingency Allowance:	\$20,000.00
AEA #1 Various Piers:	<u>\$ 8,241.88</u>
Balance:	\$11,758.12

Consideration and Approval of Change Order #1 for Forty-four (44) Delay Days due to the structural repairs on various piers for the Tom Landry Stadium Repairs. If approved the new substantial completion will be April 08, 2022.

On Friday, December 10, 2021 a letter was sent by MCISD to Mr. Rick Hinojosa, Hinojosa Structural Engineering and to Mr. Rene Garza, RG Enterprises LLC. referencing the Tom Landry Stadium Repair Project.

At the request of Mr. Garza, a project meeting was held on Wednesday morning, December 15, 2021 to discuss items referenced in the letter. Present at the meeting were staff members of R. Hinojosa Structural Engineering, Raba Kistner, Geo-tech Testing, G&G Const. and MCISD Staff.

At the Regular Board of Trustees meeting held on December 15, 2021, Mr. Albert Trevino. Hinojosa Structural Engineering and Mr. Rene Garza, RG Enterprises LLC presented an update on the project. During the presentation at least five (5) possible change orders which consist of additional costs and time were mentioned as forthcoming.

The Board expressed concern that the project needed to move forward and that requests for special meetings would be acceptable in order to expedite change orders needed as to not delay the project further.

A Special Board of Trustees Meeting has been requested for Wednesday, January 05, 2022 for Consideration and Approval of Change Order(s) for the Tom Landry Stadium Repairs Project.

At the Regular Board of Trustees meeting of December 15, 2021, both firms were instructed to work on change proposals to be submitted at the special called meeting of Wednesday, January 5, 2022. During the presentation by both Mr. Albert Trevino – Hinojosa Structural Engineering and Mr. Rene Garza – RG Enterprises, LLC they presented seven (7) possible construction proposal requests (CPR's). They were directed to present to the Administration and Board of Trustees detailed explanations for each CPR on why these were required, if by Code or other reasons. They were also directed to ensure that these CPR costs were the only option(s). It was also directed that they needed to specify if any of the CPR's would either delete or offset any of the work already included in their original scope of work and that the adjustment of all time and materials associated needed to be reflected as a "credit" to the district. As per Mr. Trevino, he would only inform the Administration and the Board of receipt of these CPR's and at this time would not formally present them for consideration since he had not yet reviewed them with RG Enterprises, LLC and did have some questions for them. Both firms were made aware that legally the project could not exceed 25% of the total cost of the project in change orders. Administration and the Board once again reiterated the need to resume work at the stadium and were very receptive to having meetings to review and possibly approve items to have the project progress. The Board asked which CPR's were critical at this time so that the project would continue and items #3, #5 and #6 that were presented that evening were noted. Both firms were directed to work on submitting these CPR's using the required AIA Document G701 - 2017 which specifically is designed to submit change

orders to the project and present them at a Special Board of Trustees meeting on Wednesday, January 12, 2022.

At the Special Board of Trustees meeting held on Wednesday, January 12, 2022, R. Hinojosa Structural Engineering and RG Enterprises, LLC presented possible change orders #2, #3 and #4. Change order #4 was the combination of Change Proposal Requests (CPR's) #5 and #6 that were presented at the previous meeting of January 05, 2022. Along with cost information were additional days requested. In consultation with Mr. David Hansen - Legal Counsel it was asked that the change orders be reviewed once again and that the costs and days all be incorporated into one single change order document. The change order was to be sent to our legal office to be incorporated into our required change order document. Both firms were asked to create a work schedule separating time from the home side versus the visitor side. A presentation is scheduled to be made once again at the Regular Board of Trustees meeting on Wednesday, January 19, 2022.

At the Regular Board of Trustees meeting held on Wednesday, January 19, 2022, R. Hinojosa Structural Engineering and RG Enterprises, LLC once again presented possible costs and change orders with a substantial completion date of early November 2022. This item was taken into Executive Session for consultation with our legal counsel.

After consultation and review, the decision and directive to both R. Hinojosa and RG Enterprises was to split the project between the home side repairs and the visitor repairs. Each side was to be a separate project with RG Enterprises submitting a change order for credit to work being separated from the visitor side and an updated schedule of values for completing the home side as this was the priority. A brief meeting was held after the Board of Trustees meeting with the design team, the general contractor, and MCISD staff to ensure that they understood the directive issued, of which they acknowledged that they understood. The directive was to have the change order with new updated costs, credits and timeline by the regularly scheduled Board Workshop on Wednesday, February 02, 2022.

Correspondences and meetings continued the week of January 24 – 28th with uncertainty from RG Enterprises about what was required and expecting a written authorization from Dr. Perez, MCISD Superintendent concerning what was directed at the previous Board meeting. A Zoom meeting was held on Thursday, January 27, 2022 with R. Hinojosa Staff, Mr. Manuel Leal, G & G Construction Superintendent, Mr. Adrian Hernandez, Mr. Adan Rivera, Ms. Lorena Garcia, and Mr. Rick Rivera to clarify the directive and expectations and the urgency for submitting the required change orders. It was presented that there would be no written authorization from Dr. Perez and that the directive issued at the Board meeting would suffice. It was also discussed that the general contractor was directed in an email by R. Hinojosa and Mr. Adrian Hernandez of what was required, Mr. Leal acknowledged the direction. A Zoom meeting was once again scheduled for Friday, January 28, 2022 to review the status of the change order. Once again both the general contractor and design team were directed to submit all change orders in a timely manner and not at the last minute when Administration does not have time to review before the presentations to Dr. Perez and the Board of Trustees. It was also noted that for all meetings we needed to have either Mr. Adrian Hernandez or Mr. Adan Rivera present.

Pending:

Administration and the Board of Trustees have made a decision to separate the Tom Landry Stadium Repairs into two separate projects, home side and visitor's side. The home side will be a priority with the current contract. Currently RG Enterprises, LLC, general contractor, is to submit a new schedule of values, credits and a new timeline for them to continue and complete the home side as scheduled. The visitor's side will now be considered a new project and thus Administration presents Project and Proposed Budget for Supplemental Repairs (Visitors Side) for the Tom Landry Stadium Project.

ADMINISTRATIVE CONSIDERATIONS

Administration does anticipate work by outside contracting firms for the Supplemental Repairs (Visitors Side) for the Tom Landry Stadium Project, thus, before soliciting bids or proposals for this project, Texas Education Code 44.031(a) requires the board of a school district, considering a construction project to take the following action.

1. The board must consider the method of delivery that provides the best value for this project. Administration recommends competitive sealed proposals as the method of delivery due to the nature of the project.

2. Selection criteria for the project must also be considered.

Attached is a copy of the recommended selection criteria used for previous District large scale projects.

3. The Board must designate the selection committee to evaluate and rank the proposals.

(This was reviewed and approved by the Purchasing Department

FUNDING SOURCE

General Funds and Possible other funding sources to be determined by the Finance Dept. (TBD)

RECOMMENDATION

Administration presents Consideration and Approval of Procurement Method, Selection Criteria, Review and Ranking Committee, Wage Rate, and Authorization to Seek Proposals/Bids for Supplemental Repairs (Visitors Side) for the Tom Landry Stadium Project.

Administration recommends using the attached evaluation and selection criteria.

EXHIBIT

Selection Criteria and Prevailing Wage Rates, pages 6

CONTACT PERSONS

Ricardo Rivera, Assistant Superintendent for Operations

Dora Garcia, Coordinator for Purchasing

Adrian Hernandez, Coordinator for Project & Energy Management

EVALUATION & SELECTION CRITERIA FOR COMPETITIVE SEALED PROPOSALS

BACKGROUND: The Mission Consolidated Independent School District Board of Trustees has authorized the District to solicit for a qualified Contractor for the construction of the project(s) identified above through Competitive Sealed Proposals (CSP) as opposed to Competitive Bids. The District will base its ranking of the Bidders on a combination of price and other factors that the District determines provides the best value to the District.

SELECTION CRITERIA AND RANKING: The selection of Proposer will be based on the following Evaluation and Selection Criteria.

SELECTION CRITERIA AND RELATIVE WEIGHTS

The total possible points that can be awarded for a proposal will be **100 points**.

<i>Monetary Value*</i>	<i>0-35</i>
<i>Qualifications and Reputation</i>	<i>0-20</i>
<i>Experience with Similar Projects for School Districts</i>	<i>0-15</i>
<i>Past Performance for Mission CISD</i>	<i>0-10</i>
<i>Quality of Work</i>	<i>(0-8)</i>
<i>Adherence to Contract Terms</i>	<i>(0-2)</i>
<i>Proposed Schedule</i>	<i>0-5</i>
<i>Contractor's Proposed Personnel</i>	<i>0-8</i>
<i>Financial Strength</i>	<i>0-2</i>
<i>HUB Certification</i>	<i>0-0.5</i>
<i>Thoroughness of Bid Submission and Quality of Presentation (may consider written submissions and interview quality as applicable)</i>	<i>0-4.5</i>

**MONETARY VALUE - WEIGHTED SCORE: The lowest RESPONSIVE bid will receive the maximum number of points (35). The Bids of Proposers that are higher than the lowest price will be calculated using the following weighted formula:*

WEIGHTED SCORE = (Lowest Responsive Bid / Proposer's Bid Price) x Assigned Points = Proposer's Points for Price

Exhibit A

"General Decision Number: TX20210255 01/01/2021

Superseded General Decision Number: TX20200255

State: Texas

Construction Type: Building

County: Hidalgo County in Texas.

BUILDING CONSTRUCTION PROJECTS (does not include single family homes or apartments up to and including 4 stories).

Note: Under Executive Order (EO) 13658, an hourly minimum wage of \$10.95 for calendar year 2021 applies to all contracts subject to the Davis-Bacon Act for which the contract is awarded (and any solicitation was issued) on or after January 1, 2015. If this contract is covered by the EO, the contractor must pay all workers in any classification listed on this wage determination at least \$10.95 per hour (or the applicable wage rate listed on this wage determination, if it is higher) for all hours spent performing on the contract in calendar year 2021. If this contract is covered by the EO and a classification considered necessary for performance of work on the contract does not appear on this wage determination, the contractor must pay workers in that classification at least the wage rate determined through the conformance process set forth in 29 CFR 5.5(a)(1)(ii) (or the EO minimum wage rate, if it is higher than the conformed wage rate). The EO minimum wage rate will be adjusted annually. Please note that this EO applies to the above-mentioned types of contracts entered into by the federal government that are subject to the Davis-Bacon Act itself, but it does not apply to contracts subject only to the Davis-Bacon Related Acts, including those set forth at 29 CFR 5.1(a)(2)-(60). Additional information on contractor requirements and worker protections under the EO is available at www.dol.gov/whd/govcontracts.

Modification Number	Publication Date
0	01/01/2021

BOIL0074-003 01/01/2017

	Rates	Fringes
BOILERMAKER.....	\$ 28.00	22.35

ENGI0178-005 06/01/2020

	Rates	Fringes
POWER EQUIPMENT OPERATOR		
(1) Tower Crane.....	\$ 32.85	13.10
(2) Cranes with Pile Driving or Caisson Attachment and Hydraulic Crane 60 tons and above.....	\$ 28.75	9810.60
(3) Hydraulic cranes 59 Tons and under.....	\$ 32.35	13.10

Exhibit A

* IRON0084-011 06/01/2020

	Rates	Fringes
IRONWORKER, ORNAMENTAL.....	\$ 25.26	7.13

PLUM0412-004 04/01/2013

	Rates	Fringes
PLUMBER.	\$ 31.14	12.43

SUTX2014-031 07/21/2014

	Rates	Fringes
BRICKLAYER.	\$ 16.17	0.00
CARPENTER.	\$ 14.21	2.22
CEMENT MASON/CONCRETE FINISHER...	\$ 12.46	0.00
ELECTRICIAN.	\$ 18.44	4.53
INSULATOR - MECHANICAL (Duct, Pipe & Mechanical System Insulation).	\$ 11.54	2.17
IRONWORKER, REINFORCING.	\$ 12.01	0.00
IRONWORKER, STRUCTURAL.	\$ 15.04	4.34
LABORER: Common or General.	\$ 8.00	0.00
LABORER: Mason Tender - Brick...	\$ 10.00	0.00
LABORER: Mason Tender - Cement/Concrete.	\$ 10.89	0.96
LABORER: Pipelayer.	\$ 11.00	3.47
LABORER: Roof Tearoff.	\$ 10.06	0.00
OPERATOR: Backhoe/Excavator/Trackhoe.	\$ 14.04	1.01
OPERATOR: Bobcat/Skid Steer/Skid Loader.	\$ 13.93	0.00
OPERATOR: Bulldozer.	\$ 18.29	1.31
OPERATOR: Drill.	\$ 16.22	0.34
OPERATOR: Forklift.	\$ 14.83	0.00
OPERATOR: Grader/Blade.	\$ 10.00	0.00
OPERATOR: Loader.	\$ 12.87	0.70
OPERATOR: Mechanic.	\$ 17.00	0.00
OPERATOR: Paver (Asphalt, Aggregate, and Concrete).	\$ 16.03	0.00

Exhibit A

OPERATOR: Roller.	\$ 12.70	0.00
PAINTER (Brush, Roller, and Spray).	\$ 11.27	0.00
PIPEFITTER.	\$ 15.22	3.16
ROOFER.	\$ 11.42	0.00
SHEET METAL WORKER (HVAC Duct Installation Only).	\$ 18.40	2.12
SHEET METAL WORKER, Excludes HVAC Duct Installation.	\$ 21.13	6.53
TILE FINISHER.	\$ 11.22	0.00
TILE SETTER.	\$ 12.15	0.00
TRUCK DRIVER: Dump Truck.	\$ 12.39	1.18
TRUCK DRIVER: Flatbed Truck. ...	\$ 19.65	8.57
TRUCK DRIVER: Semi-Trailer Truck.	\$ 12.50	0.00
TRUCK DRIVER: Water Truck.	\$ 12.00	4.11

WELDERS - Receive rate prescribed for craft performing operation to which welding is incidental.

Exhibit A

=====
Note: Executive Order (EO) 13706, Establishing Paid Sick Leave for Federal Contractors applies to all contracts subject to the Davis-Bacon Act for which the contract is awarded (and any solicitation was issued) on or after January 1, 2017. If this contract is covered by the EO, the contractor must provide employees with 1 hour of paid sick leave for every 30 hours they work, up to 56 hours of paid sick leave each year. Employees must be permitted to use paid sick leave for their own illness, injury or other health-related needs, including preventive care; to assist a family member (or person who is like family to the employee) who is ill, injured, or has other health-related needs, including preventive care; or for reasons resulting from, or to assist a family member (or person who is like family to the employee) who is a victim of, domestic violence, sexual assault, or stalking. Additional information on contractor requirements and worker protections under the EO is available at www.dol.gov/whd/govcontracts.

Unlisted classifications needed for work not included within the scope of the classifications listed may be added after award only as provided in the labor standards contract clauses (29CFR 5.5 (a) (1) (ii)).

The body of each wage determination lists the classification and wage rates that have been found to be prevailing for the cited type(s) of construction in the area covered by the wage determination. The classifications are listed in alphabetical order of ""identifiers"" that indicate whether the particular rate is a union rate (current union negotiated rate for local), a survey rate (weighted average rate) or a union average rate (weighted union average rate).

Union Rate Identifiers

A four letter classification abbreviation identifier enclosed in dotted lines beginning with characters other than ""SU"" or ""UAVG"" denotes that the union classification and rate were prevailing for that classification in the survey. Example: PLUM0198-005 07/01/2014. PLUM is an abbreviation identifier of the union which prevailed in the survey for this classification, which in this example would be Plumbers. 0198 indicates the local union number or district council number where applicable, i.e., Plumbers Local 0198. The next number, 005 in the example, is an internal number used in processing the wage determination. 07/01/2014 is the effective date of the most current negotiated rate, which in this example is July 1, 2014.

Union prevailing wage rates are updated to reflect all rate changes in the collective bargaining agreement (CBA) governing this classification and rate.

Exhibit A

Survey Rate Identifiers

Classifications listed under the ""SU"" identifier indicate that no one rate prevailed for this classification in the survey and the published rate is derived by computing a weighted average rate based on all the rates reported in the survey for that classification. As this weighted average rate includes all rates reported in the survey, it may include both union and non-union rates. Example: SULA2012-007 5/13/2014. SU indicates the rates are survey rates based on a weighted average calculation of rates and are not majority rates. LA indicates the State of Louisiana. 2012 is the year of survey on which these classifications and rates are based. The next number, 007 in the example, is an internal number used in producing the wage determination. 5/13/2014 indicates the survey completion date for the classifications and rates under that identifier.

Survey wage rates are not updated and remain in effect until a new survey is conducted.

Union Average Rate Identifiers

Classification(s) listed under the UAVG identifier indicate that no single majority rate prevailed for those classifications; however, 100% of the data reported for the classifications was union data. EXAMPLE: UAVG-OH-0010 08/29/2014. UAVG indicates that the rate is a weighted union average rate. OH indicates the state. The next number, 0010 in the example, is an internal number used in producing the wage determination. 08/29/2014 indicates the survey completion date for the classifications and rates under that identifier.

A UAVG rate will be updated once a year, usually in January of each year, to reflect a weighted average of the current negotiated/CBA rate of the union locals from which the rate is based.

Exhibit A

WAGE DETERMINATION APPEALS PROCESS

1.) Has there been an initial decision in the matter? This can be:

- * an existing published wage determination
- * a survey underlying a wage determination
- * a Wage and Hour Division letter setting forth a position on a wage determination matter
- * a conformance (additional classification and rate) ruling

On survey related matters, initial contact, including requests for summaries of surveys, should be with the Wage and Hour Regional Office for the area in which the survey was conducted because those Regional Offices have responsibility for the Davis-Bacon survey program. If the response from this initial contact is not satisfactory, then the process described in 2.) and 3.) should be followed.

With regard to any other matter not yet ripe for the formal process described here, initial contact should be with the Branch of Construction Wage Determinations. Write to:

Branch of Construction Wage Determinations
Wage and Hour Division
U.S. Department of Labor
200 Constitution Avenue, N.W.
Washington, DC 20210

2.) If the answer to the question in 1.) is yes, then an interested party (those affected by the action) can request review and reconsideration from the Wage and Hour Administrator (See 29 CFR Part 1.8 and 29 CFR Part 7). Write to:

Wage and Hour Administrator
U.S. Department of Labor
200 Constitution Avenue, N.W.
Washington, DC 20210

The request should be accompanied by a full statement of the interested party's position and by any information (wage payment data, project description, area practice material, etc.) that the requestor considers relevant to the issue.

3.) If the decision of the Administrator is not favorable, an interested party may appeal directly to the Administrative Review Board (formerly the Wage Appeals Board). Write to:

Administrative Review Board
U.S. Department of Labor
200 Constitution Avenue, N.W.
Washington, DC 20210

4.) All decisions by the Administrative Review Board are final.

=====

END OF GENERAL DECISION"
